

ID	% Complete	Task Name	Duration	Start	Finish	Predecessors	Resource Names	Nov 4, '12					
								S	S	M	T		
1	24%	Malware Protection Overhaul Project	110 days?	11/5/12	4/5/13								
2	100%	Planning	1 day	11/5/12	11/5/12								
3	100%	Define scope	1 day	11/5/12	11/5/12		Sophie						
4	100%	Review scope with Mark	1 day	11/5/12	11/5/12		Sophie						
5	100%	Kickoff Meeting - include other teams	1 day	11/5/12	11/5/12		Sophie						
6	100%	Communications	1 day?	11/14/12	11/14/12								
7	100%	Initial IT Leader meeting presentation	1 day?	11/14/12	11/14/12		Andrew						
8	100%	Contact IT Leaders to solicit volunteers for pilot	1 day	11/14/12	11/14/12		Tim						
9	100%	Checklist for pilot	1 day	11/14/12	11/14/12		Andrew						
10	19%	Windows Selection	103 days?	11/14/12	4/5/13								
11	100%	System Center 2012 (Forefront) Evaluation	57 days	11/14/12	1/31/13		Andrew						
12	100%	VM setup	1 day	11/14/12	11/14/12		Richard						
13	100%	Console setup	1 day	11/14/12	11/14/12		Richard						
14	100%	Console and client functionality evaluation	1 day	1/31/13	1/31/13								
15	100%	ESET Evaluation (v5.0 - Jan 2013)	1 day	11/14/12	11/14/12		Andrew						
16	100%	VM setup	1 day	11/14/12	11/14/12								
17	100%	Console setup	1 day	11/14/12	11/14/12								
18	100%	Console and client functionality evaluation	1 day	11/14/12	11/14/12								
19	9%	Vendor Demo	67 days	11/14/12	2/14/13								
20	100%	Determine invitees	1 day	11/14/12	11/14/12								
21	20%	Determine requirements	1 day	2/1/13	2/1/13								
22	0%	Demo	10 days	2/1/13	2/14/13								
23	0%	Team feedback	2 days	2/1/13	2/4/13								
24	20%	Analyze Recommendation and Solution	70 days	11/14/12	2/19/13								

Project: Malware Protection Overhaul Date: 2/4/13	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	

ID	% Comple	Task Name	Duration	Start	Finish	Predecessors	Resource Names	Nov 4, '12			
								S	S	M	T
25	100%	Peer school comparion breakdown	1 day	11/14/12	11/14/12		Andrew				
26	0%	Determine any contract/licensing issues	1 day	2/15/13	2/15/13	22					
27	0%	Determine total cost of ownership	1 day	2/15/13	2/15/13	22					
28	0%	Determine benefits and concerns	1 day	2/18/13	2/18/13	27					
29	0%	Determine support process/structure	1 day	2/19/13	2/19/13	28					
30	0%	Sponsor approval	5 days	2/19/13	2/26/13	24					
31	0%	Approval from sponsor									
32	33%	McAfee License	76 days?	11/14/12	2/27/13						
33	100%	Understand current McAfee license constraints	1 day	11/14/12	11/14/12						
34	0%	Understand what the license needs are									
35	0%	Adjust McAfee license based on new requirements	1 day?	2/27/13	2/27/13	30					
36	0%	Documentation and communication	1 day?	2/27/13	2/27/13	30					
37	0%	Helpdesk (awareness only)	1 day?	2/27/13	2/27/13						
38	0%	DITR (awareness only)	1 day?	2/27/13	2/27/13						
39	0%	ITLEADERS (awareness and preparing for early adaptors only)	1 day?	2/27/13	2/27/13						
40	0%	Pilot rollout (STAKEHOLDERS)	10 days	2/26/13	3/12/13	30					
46	0%	Procurement	10 days	3/12/13	3/26/13	40					
51	0%	EARLY ADOPTERS	10 days	3/12/13	3/26/13	40					
56	0%	Final Checkpoint: Present all feedback including beta rollout feedback to Sponsor	1 day?	11/14/12	11/14/12						
57	0%	General Communications	2 days	3/26/13	3/28/13	51					
59	0%	Prep Helpdesk for full rollout support	5 days	3/28/13	4/4/13	57					

Project: Malware Protection Over Date: 2/4/13

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	

ID	% Complete	Task Name	Duration	Start	Finish	Predecessors	Resource Names	Nov 4, '12			
								S	S	M	T
								61	0%	Full rollout (COMMUNITY)	1 day
63	20%	MAC Selection	101 days?	11/14/12	4/3/13						
64	100%	Evaluation	47 days	11/28/12	1/31/13						
65	100%	Sophos Evaluation	47 days	11/28/12	1/31/13		Andrew				
66	100%	VM setup	1 day	11/28/12	11/28/12						
67	100%	Console setup	1 day	12/5/12	12/5/12						
68	100%	Console and client functionality evaluation	1 day	11/28/12	11/28/12						
69	100%	Document Pros and cons	1 day	1/31/13	1/31/13						
70	100%	ESET Evaluation (v5.0 - Jan 2013)	42 days	12/5/12	1/31/13		Andrew				
71	100%	VM setup	1 day	12/5/12	12/5/12						
72	100%	Console setup	1 day	12/5/12	12/5/12						
73	100%	Console and client functionality evaluation	1 day	12/5/12	12/5/12						
74	100%	Document pros and cons	1 day	1/31/13	1/31/13						
75	44%	Vendor Demo	59 days?	11/14/12	2/4/13						
76	100%	Determine which vendor(s) to demo	1 day	11/14/12	11/14/12						
77	100%	Determine invitees	1 day	11/14/12	11/14/12						
78	20%	Determine requirements	1 day?	2/1/13	2/1/13						
79	0%	Demo	1 day?	2/1/13	2/1/13						
80	0%	Team feedback	1 day	2/4/13	2/4/13	79					
81	0%	Analyze Recommendation and Solution	2 days	2/7/13	2/8/13						
82	0%	Determine any contract/licensing issues	2 days	2/7/13	2/8/13	39					
83	0%	Determine total cost of ownership	2 days	2/7/13	2/8/13	39					
84	0%	Determine benefits and concerns	2 days	2/7/13	2/8/13	39					
85	0%	Determine support process/structure	2 days	2/7/13	2/8/13	39					

Project: Malware Protection Over Date: 2/4/13

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	

ID	% Complete	Task Name	Duration	Start	Finish	Predecessors	Resource Names	Nov 4, '12			
								S	S	M	T
								86	0%	Sponsor approval	5 days
88	0%	Documentation and communication	3 days	2/18/13	2/20/13	86					
89	0%	Helpdesk (awareness only)	1 day	2/18/13	2/18/13	86					
90	0%	DITR (awareness only)	1 day	2/19/13	2/19/13	89					
91	0%	ITLEADERS (awareness and preparing for early adaptors only)	1 day	2/20/13	2/20/13	90					
92	0%	Pilot rollout (STAKEHOLDERS)	5 days	2/18/13	2/22/13						
93	0%	Determine pilot rollout team	1 day	2/18/13	2/18/13	86					
94	0%	Determine timelines	1 day	2/20/13	2/20/13	93					
95	0%	determine pilot rollout strategy	1 day	2/21/13	2/21/13	94					
96	0%	Collect feedback	1 day	2/22/13	2/22/13	95					
97	0%	Procurement	10 days	2/22/13	3/8/13	92					
98	0%	Negotiate pricing									
99	0%	Contract agreement and signature									
100	0%	Purchase									
101	0%	Reminder: adjust McAfee contract									
102	0%	EARLY ADOPTERS	13 days	3/11/13	3/27/13	97					
103	0%	Determine early adopters participants	1 day	3/11/13	3/11/13	97					
104	0%	Determine timelines	1 day	3/12/13	3/12/13	103					
105	0%	determine beta rollout strategy	1 day	3/13/13	3/13/13	104					
106	0%	collect feedback	10 days	3/14/13	3/27/13	105					
107	0%	Final Checkpoint: Present all feedback including beta rollout feedback to Sponsor	1 day?	3/28/13	3/28/13	105					
108	0%	General Communications	1 day	3/28/13	3/29/13	107					
109	0%	to community									


Project: Malware Protection Over Date: 2/4/13	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	

ID	% Complete	Task Name	Duration	Start	Finish	Predecessors	Resource Names	Nov 4, '12			
								S	S	M	T
								110	0%	Prep Helpdesk for full rollout support	2 days
111	0%	any additional training/documentation	2 days	4/1/13	4/2/13	108					
112	0%	Full rollout (COMMUNITY)	1 day	4/2/13	4/3/13	110					
113	0%	Provide software to SWRT for distribution	1 day	4/3/13	4/3/13	110					
114	0%	Project Wrapup	1 day?	4/3/13	4/4/13	112					
115	0%	closeout project									


Project: Malware Protection Ove Date: 2/4/13	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	

				Nov 11, '12				Nov 18, '12				Nov 25, '12				Dec 2, '12				Dec 9, '12										
W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F


pphie
pphie
pphie

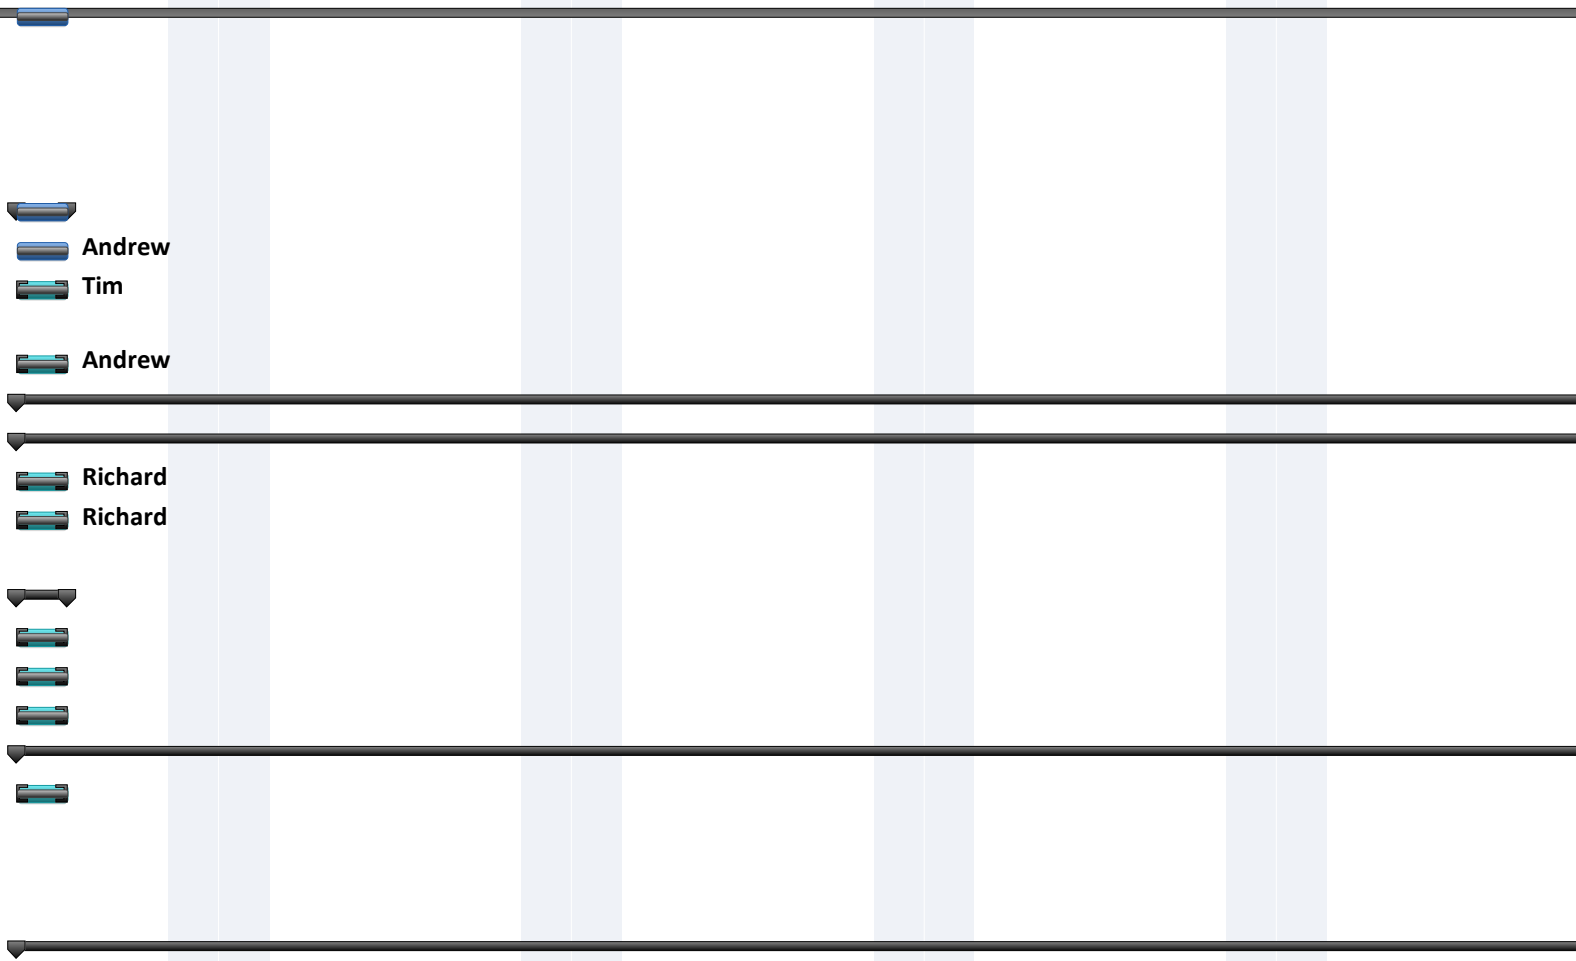


Project: Malware Protection Over Date: 2/4/13	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	

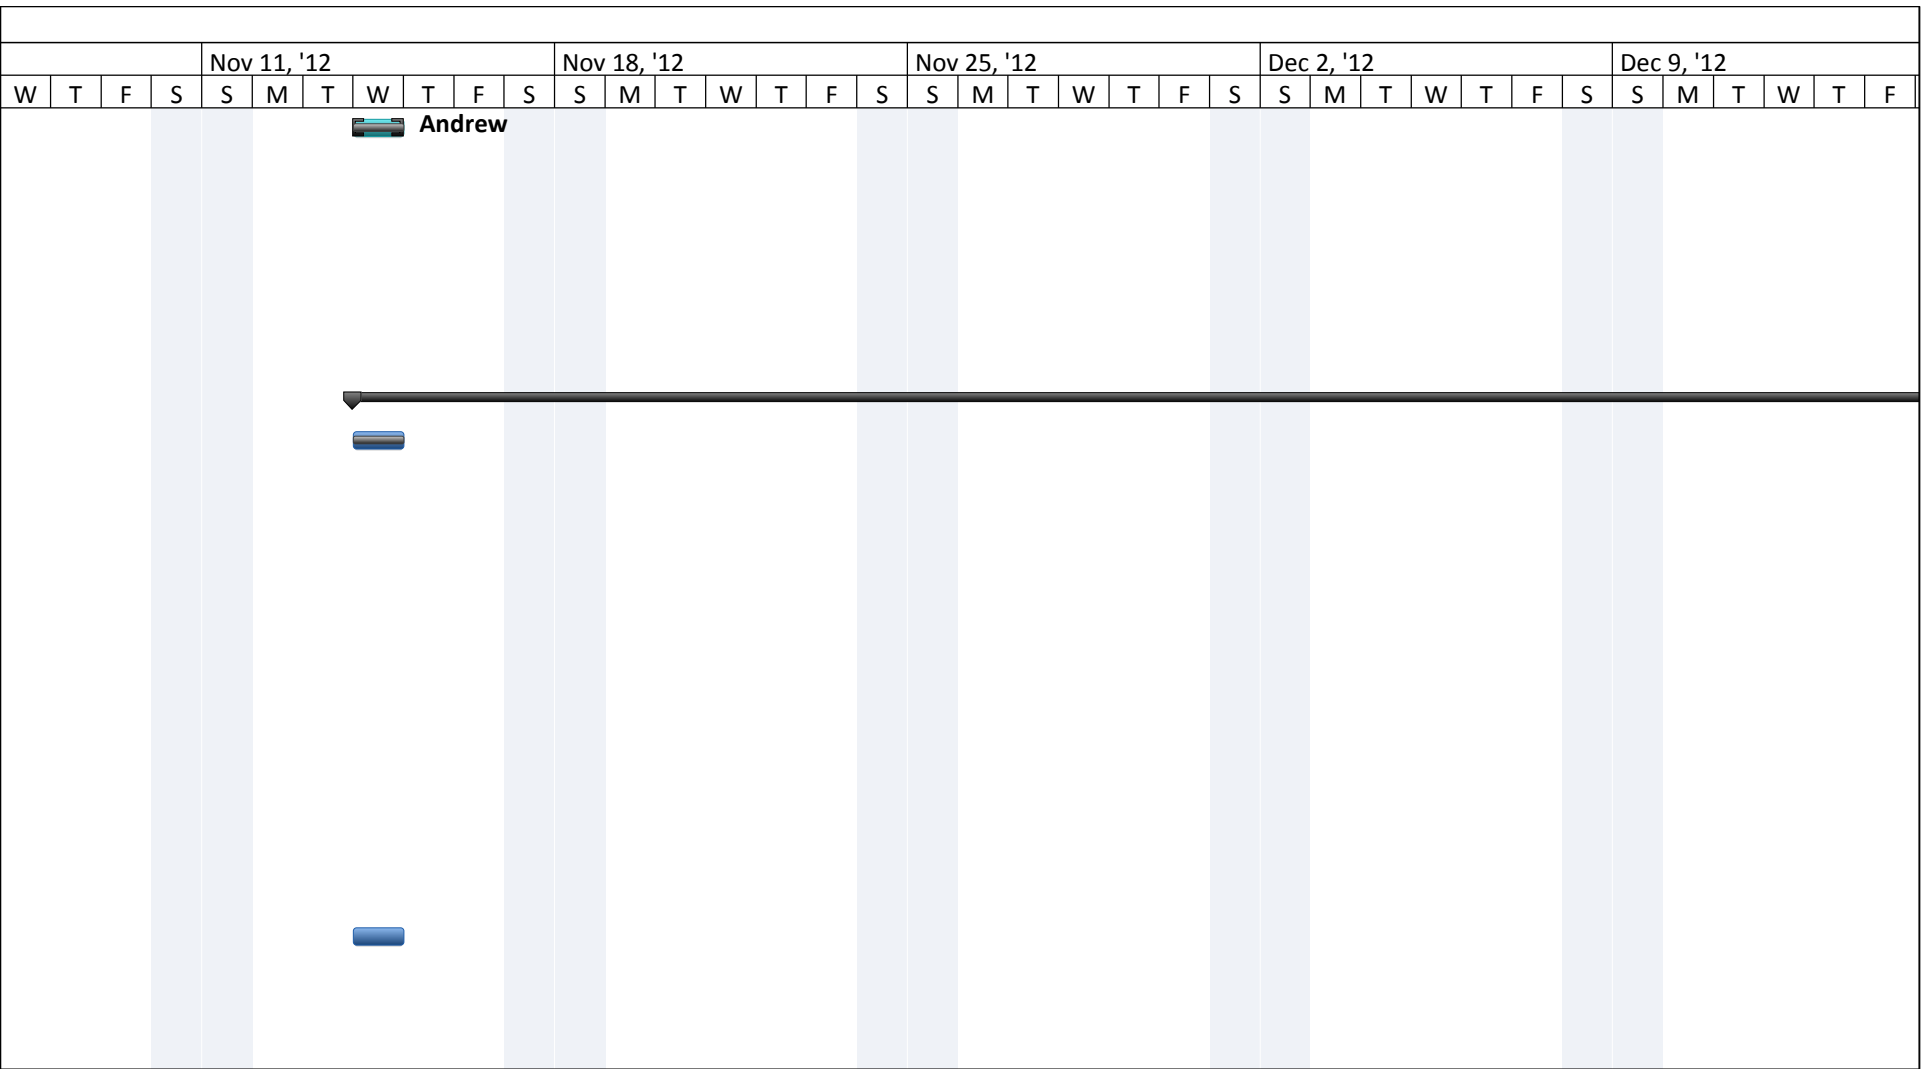

Project: Malware Protection Over Date: 2/4/13	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	

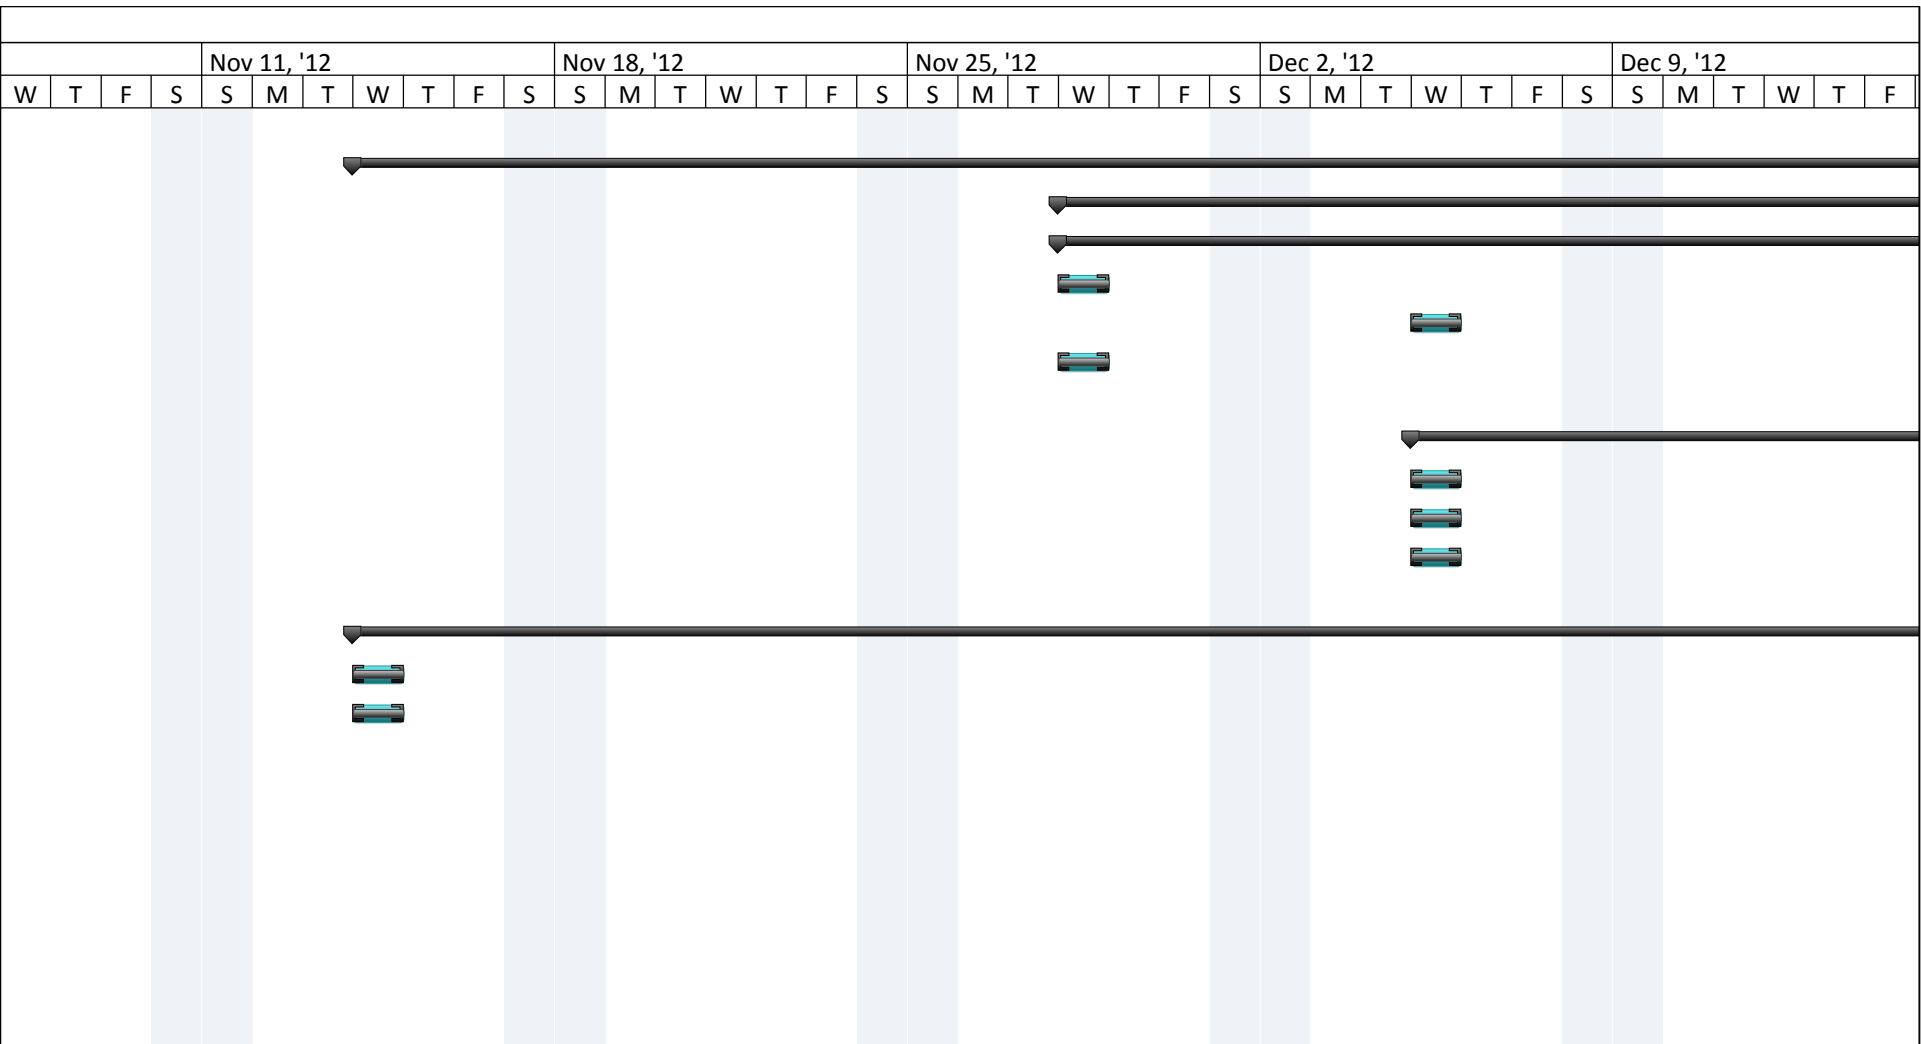

Project: Malware Protection Overdue Date: 2/4/13	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	

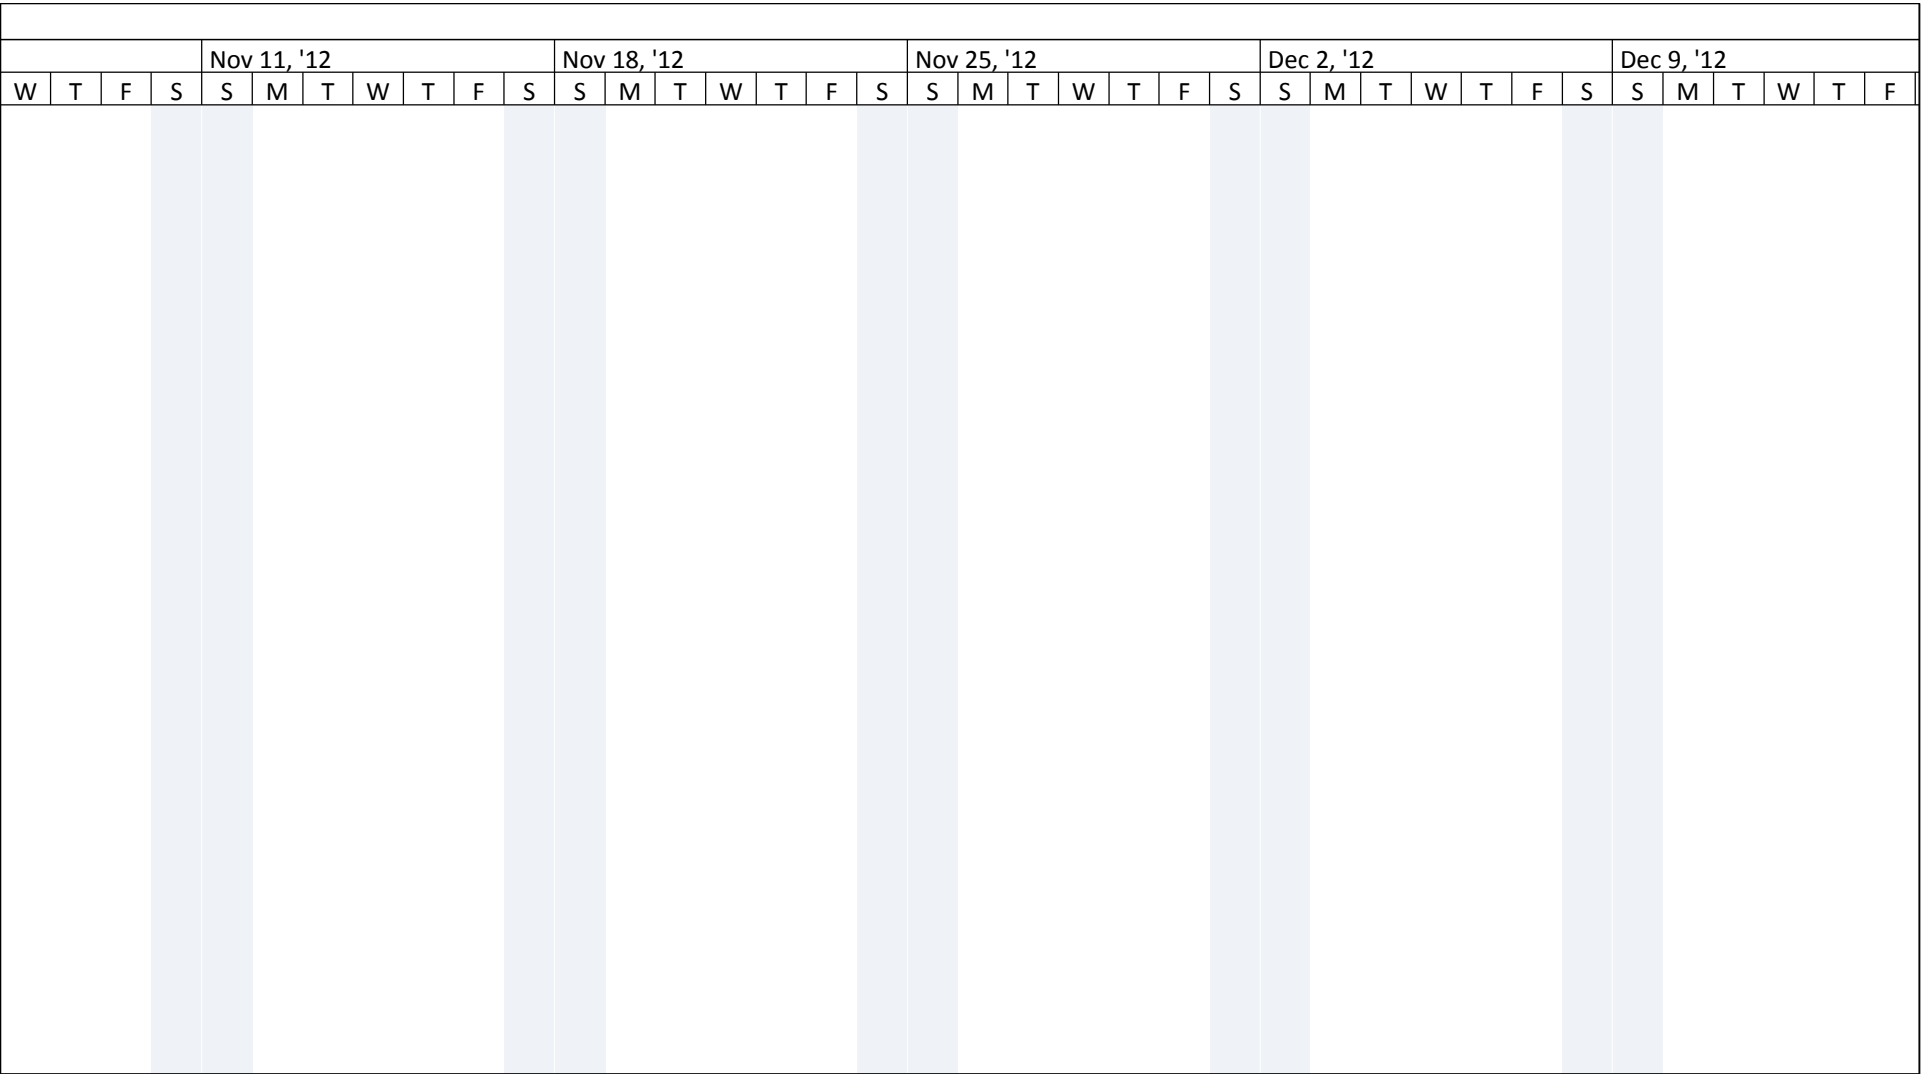

Project: Malware Protection Ove
Date: 2/4/13


Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	

				Nov 11, '12				Nov 18, '12				Nov 25, '12				Dec 2, '12				Dec 9, '12											
W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	



Project: Malware Protection Ove
Date: 2/4/13

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	




Dec 16, '12								Dec 23, '12								Dec 30, '12								Jan 6, '13								Jan 13, '13								Jan 20, '13				
S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M

Project: Malware Protection Over Date: 2/4/13

- | | | | | | |
|-----------------|--|--------------------|--|-----------------------|--|
| Task | | External Milestone | | Manual Summary Rollup | |
| Split | | Inactive Task | | Manual Summary | |
| Milestone | | Inactive Milestone | | Start-only | |
| Summary | | Inactive Summary | | Finish-only | |
| Project Summary | | Manual Task | | Deadline | |
| External Tasks | | Duration-only | | Progress | |



Project: Malware Protection Overdue Date: 2/4/13	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	

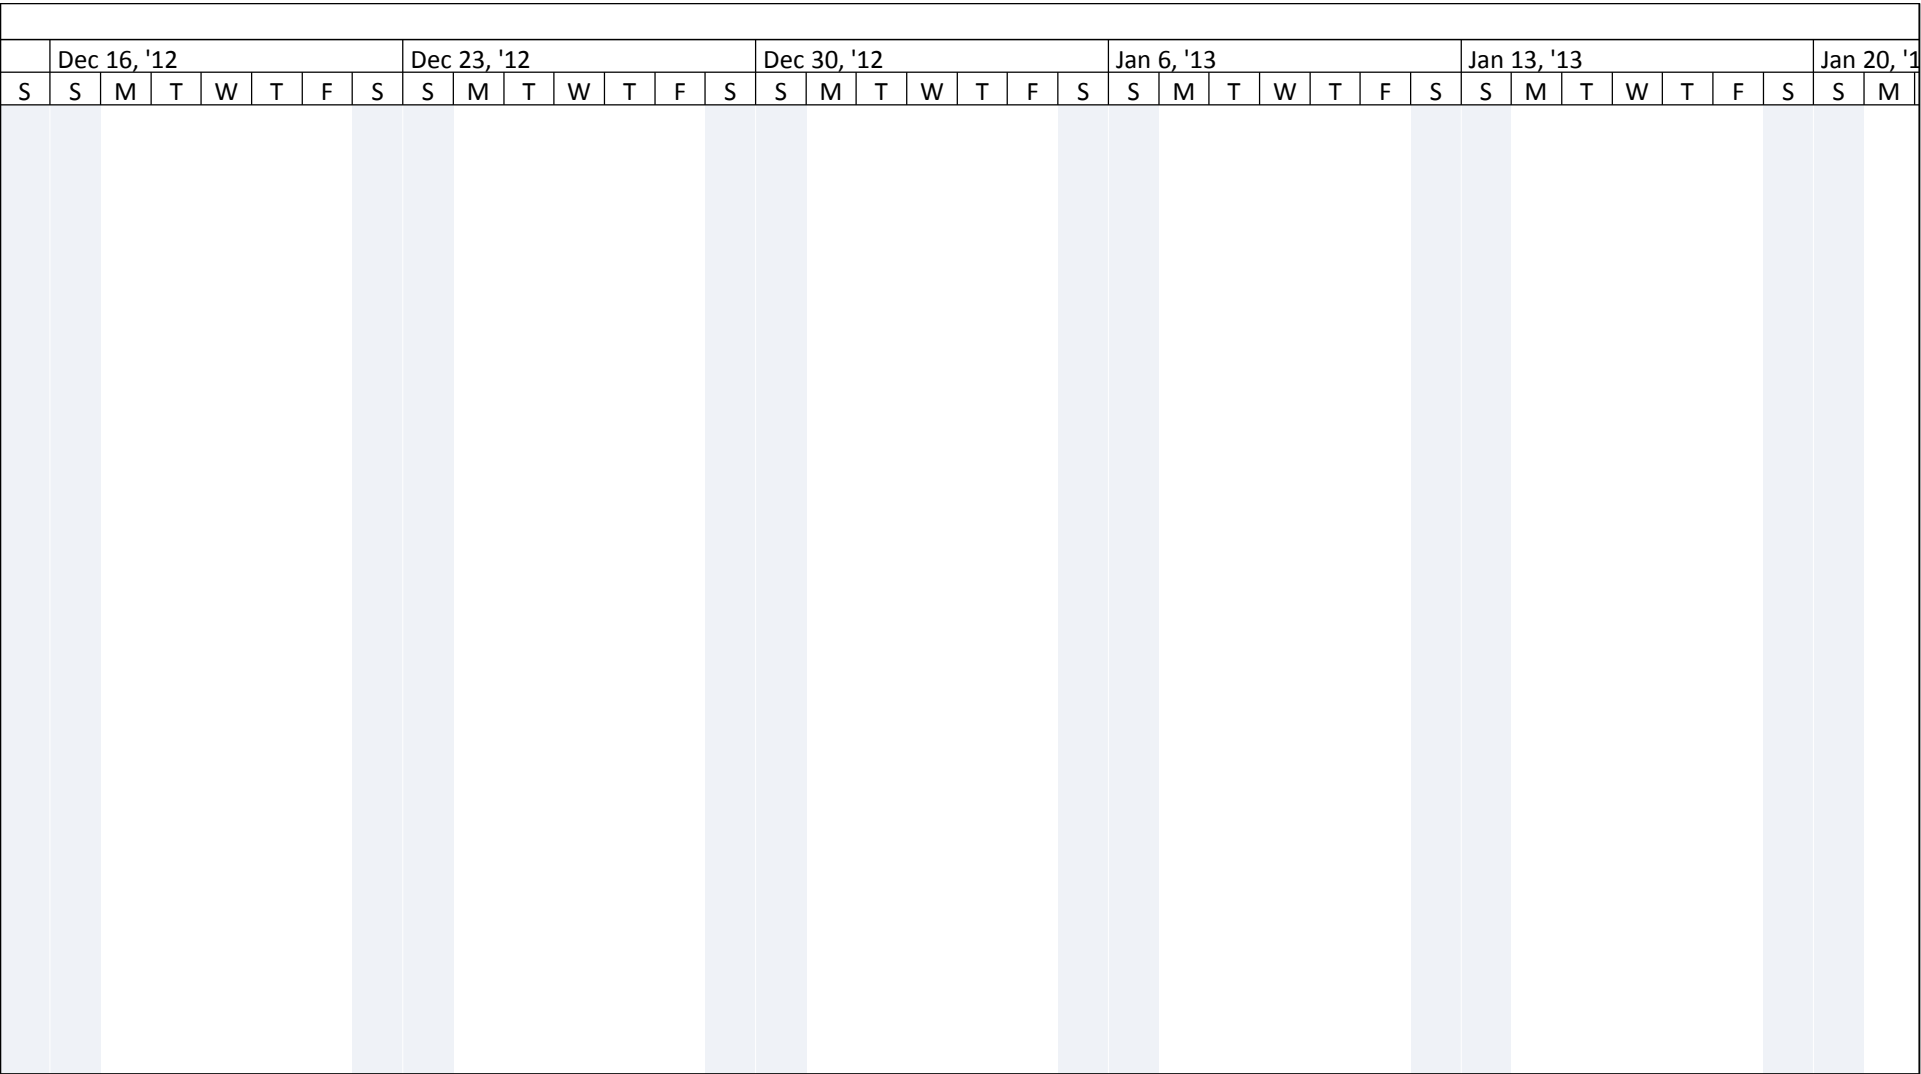

Project: Malware Protection Ove
Date: 2/4/13

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	

Dec 16, '12								Dec 23, '12								Dec 30, '12								Jan 6, '13								Jan 13, '13								Jan 20, '13		
S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M					




Project: Malware Protection Ove
Date: 2/4/13


Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	

3 Jan 27, '13 Feb 3, '13 Feb 10, '13 Feb 17, '13 Feb 24, '13

T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T

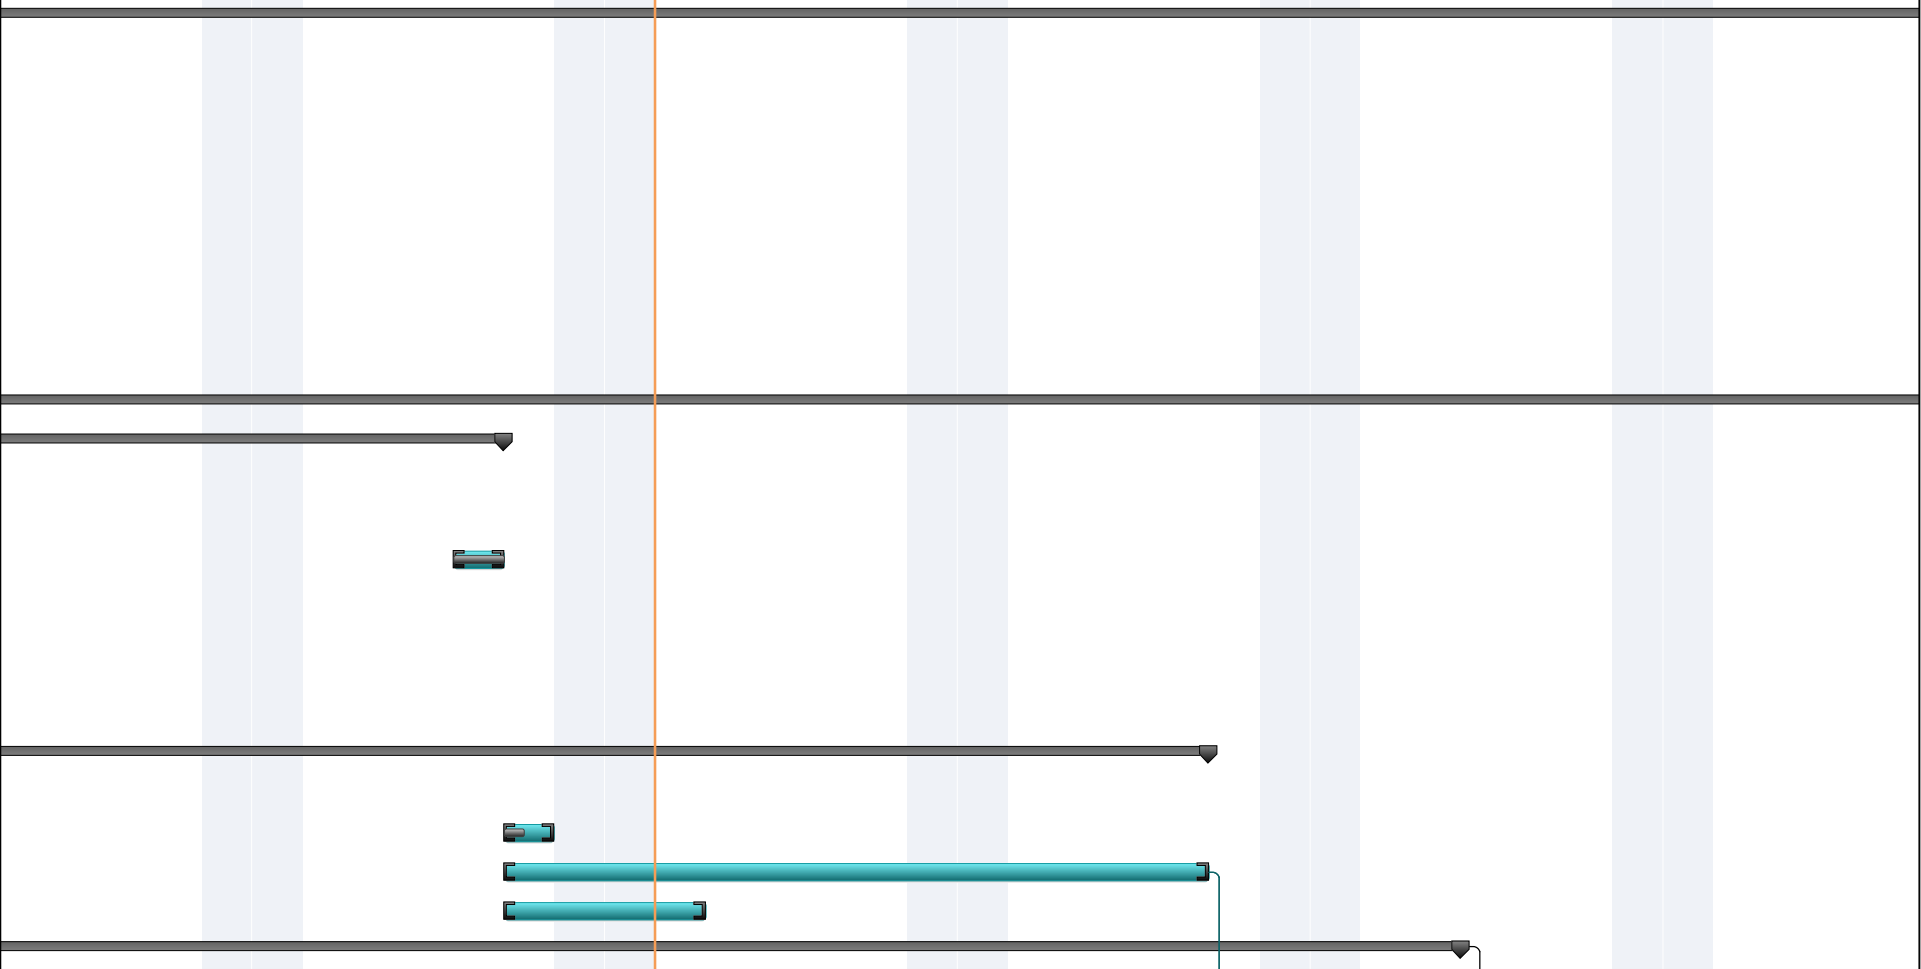


Project: Malware Protection Ove Date: 2/4/13	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	

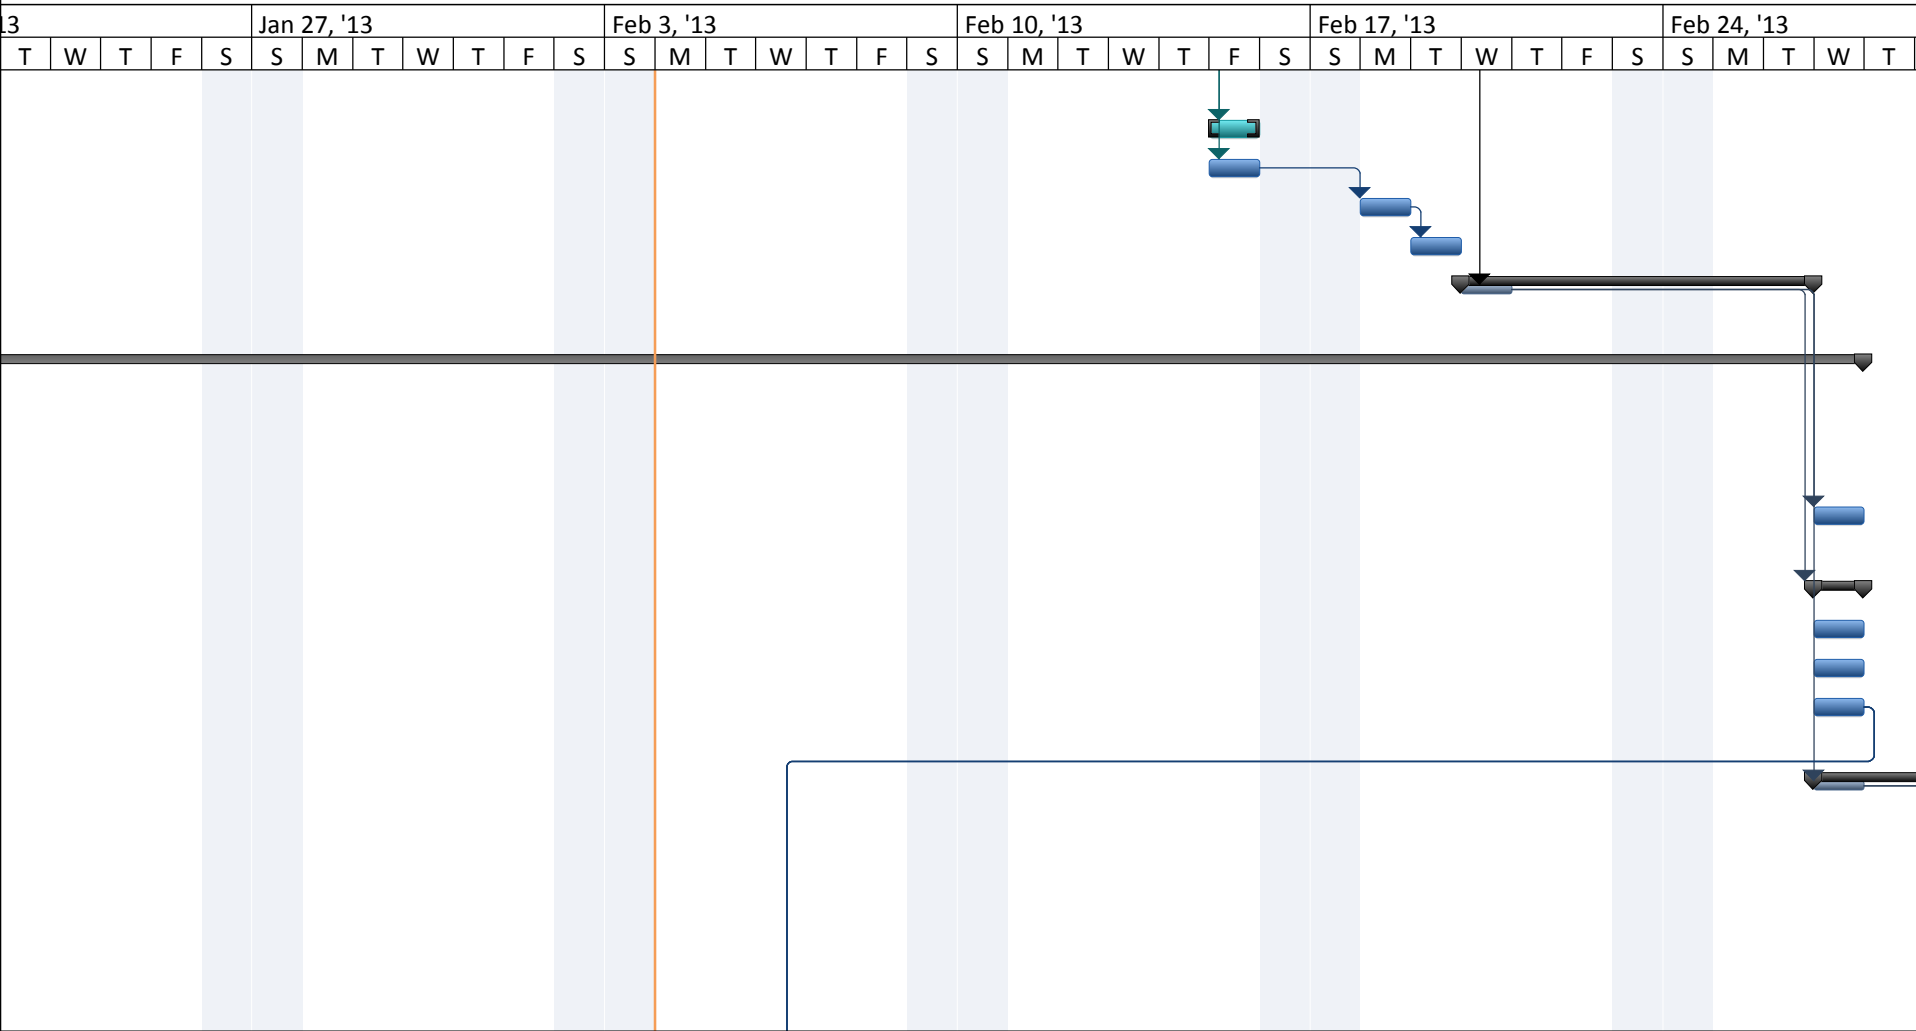


Project: Malware Protection Over
Date: 2/4/13


Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	

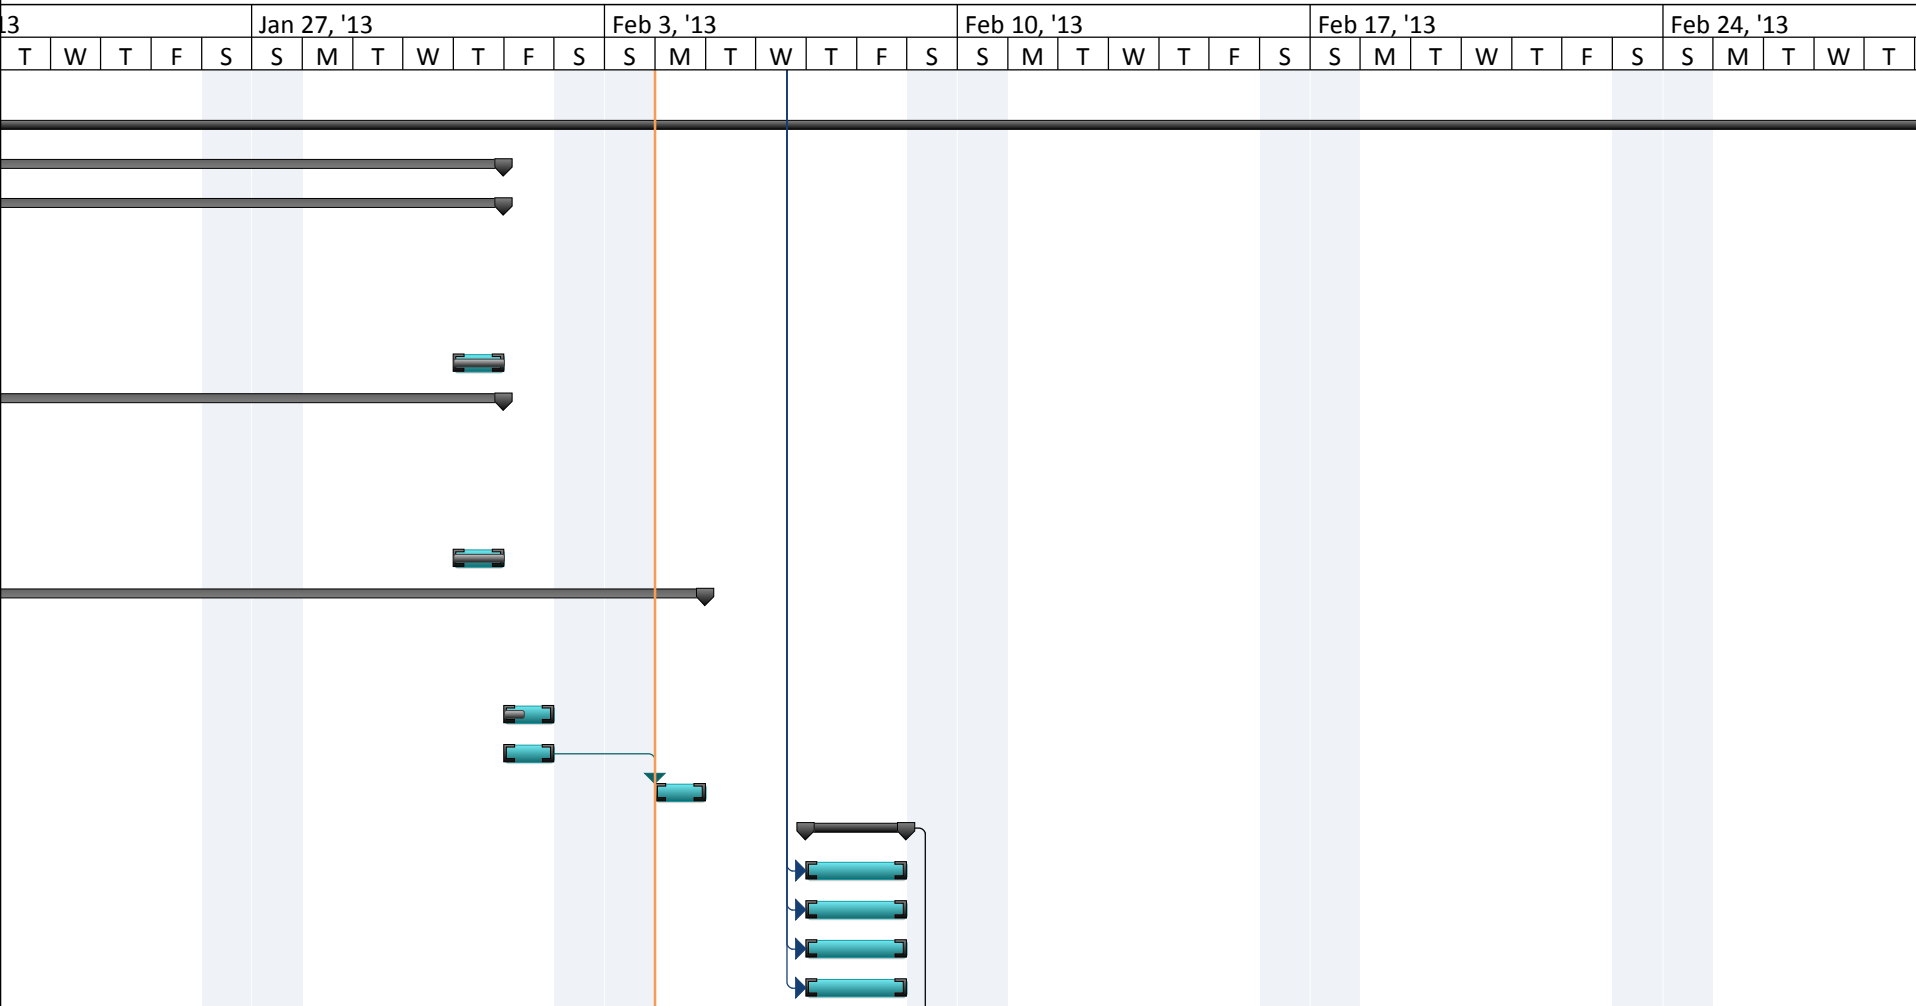

Project: Malware Protection Over Date: 2/4/13	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	

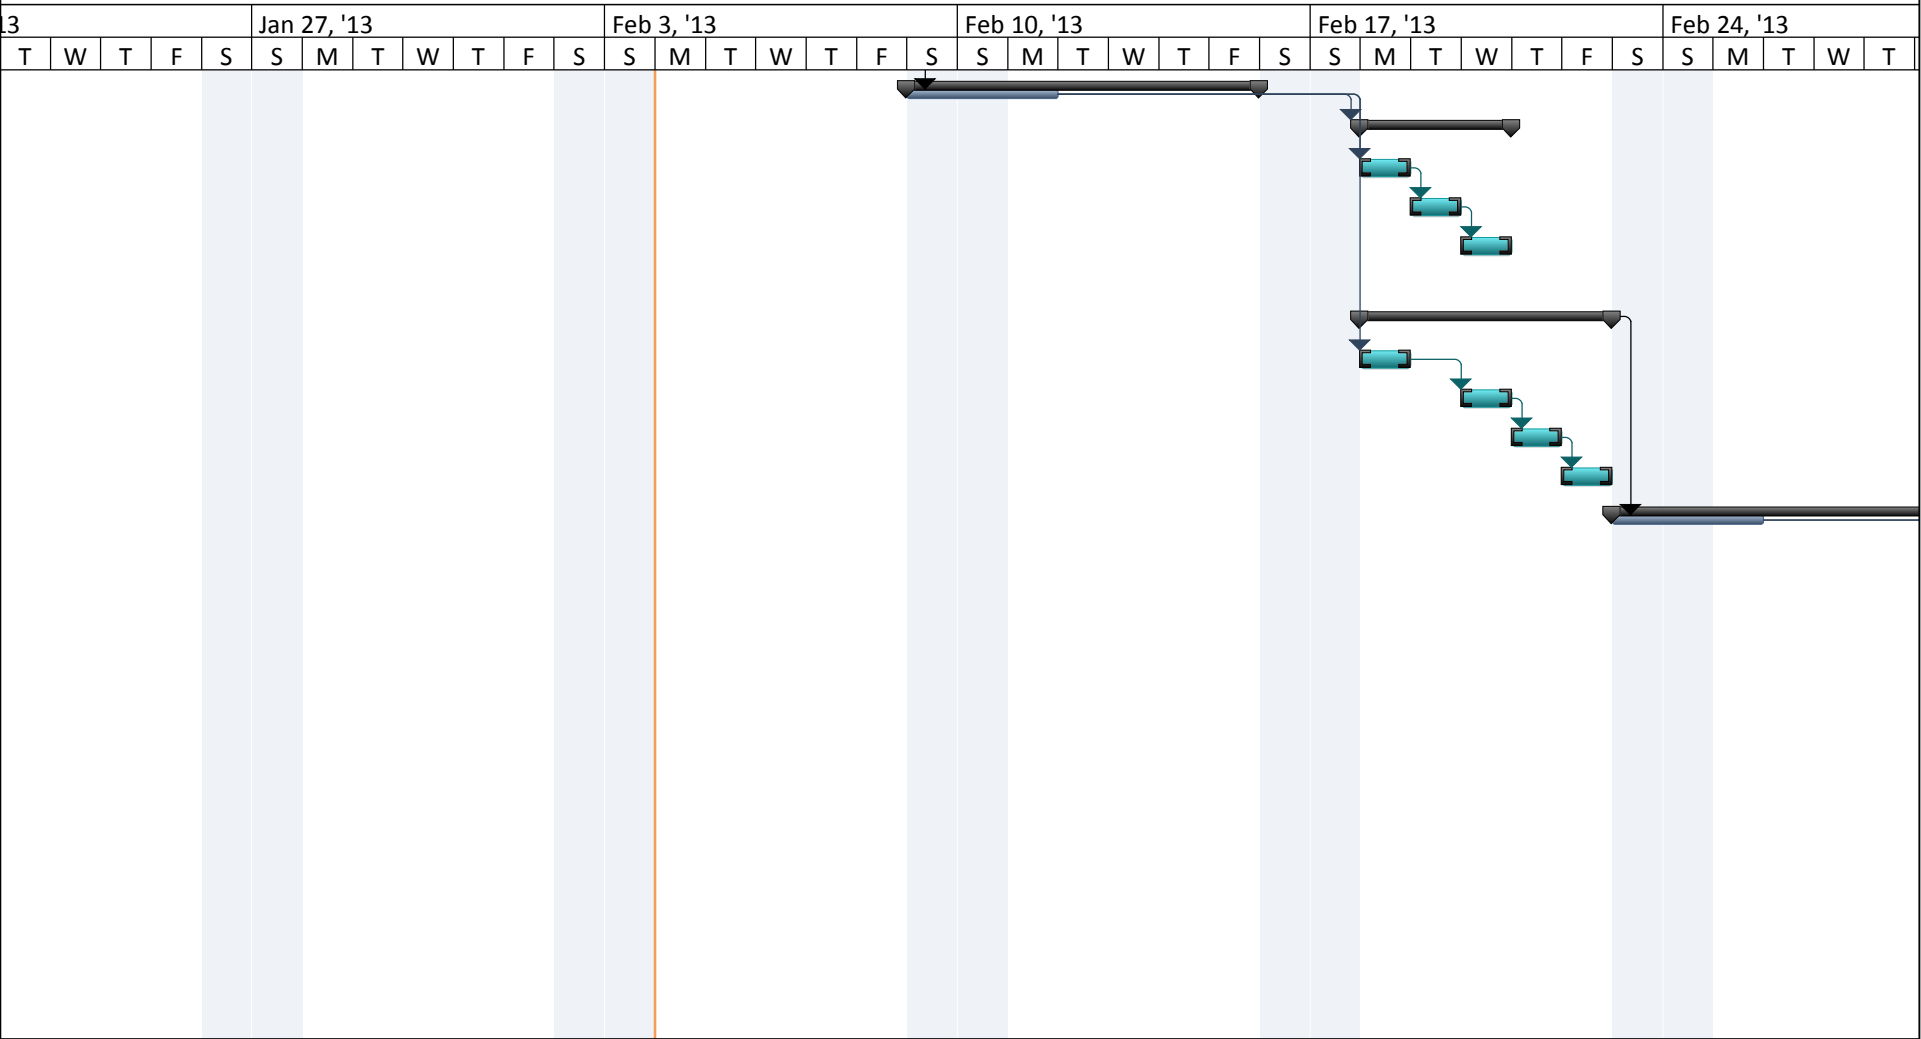


Project: Malware Protection Ove Date: 2/4/13	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	




Project: Malware Protection Ove
Date: 2/4/13

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	

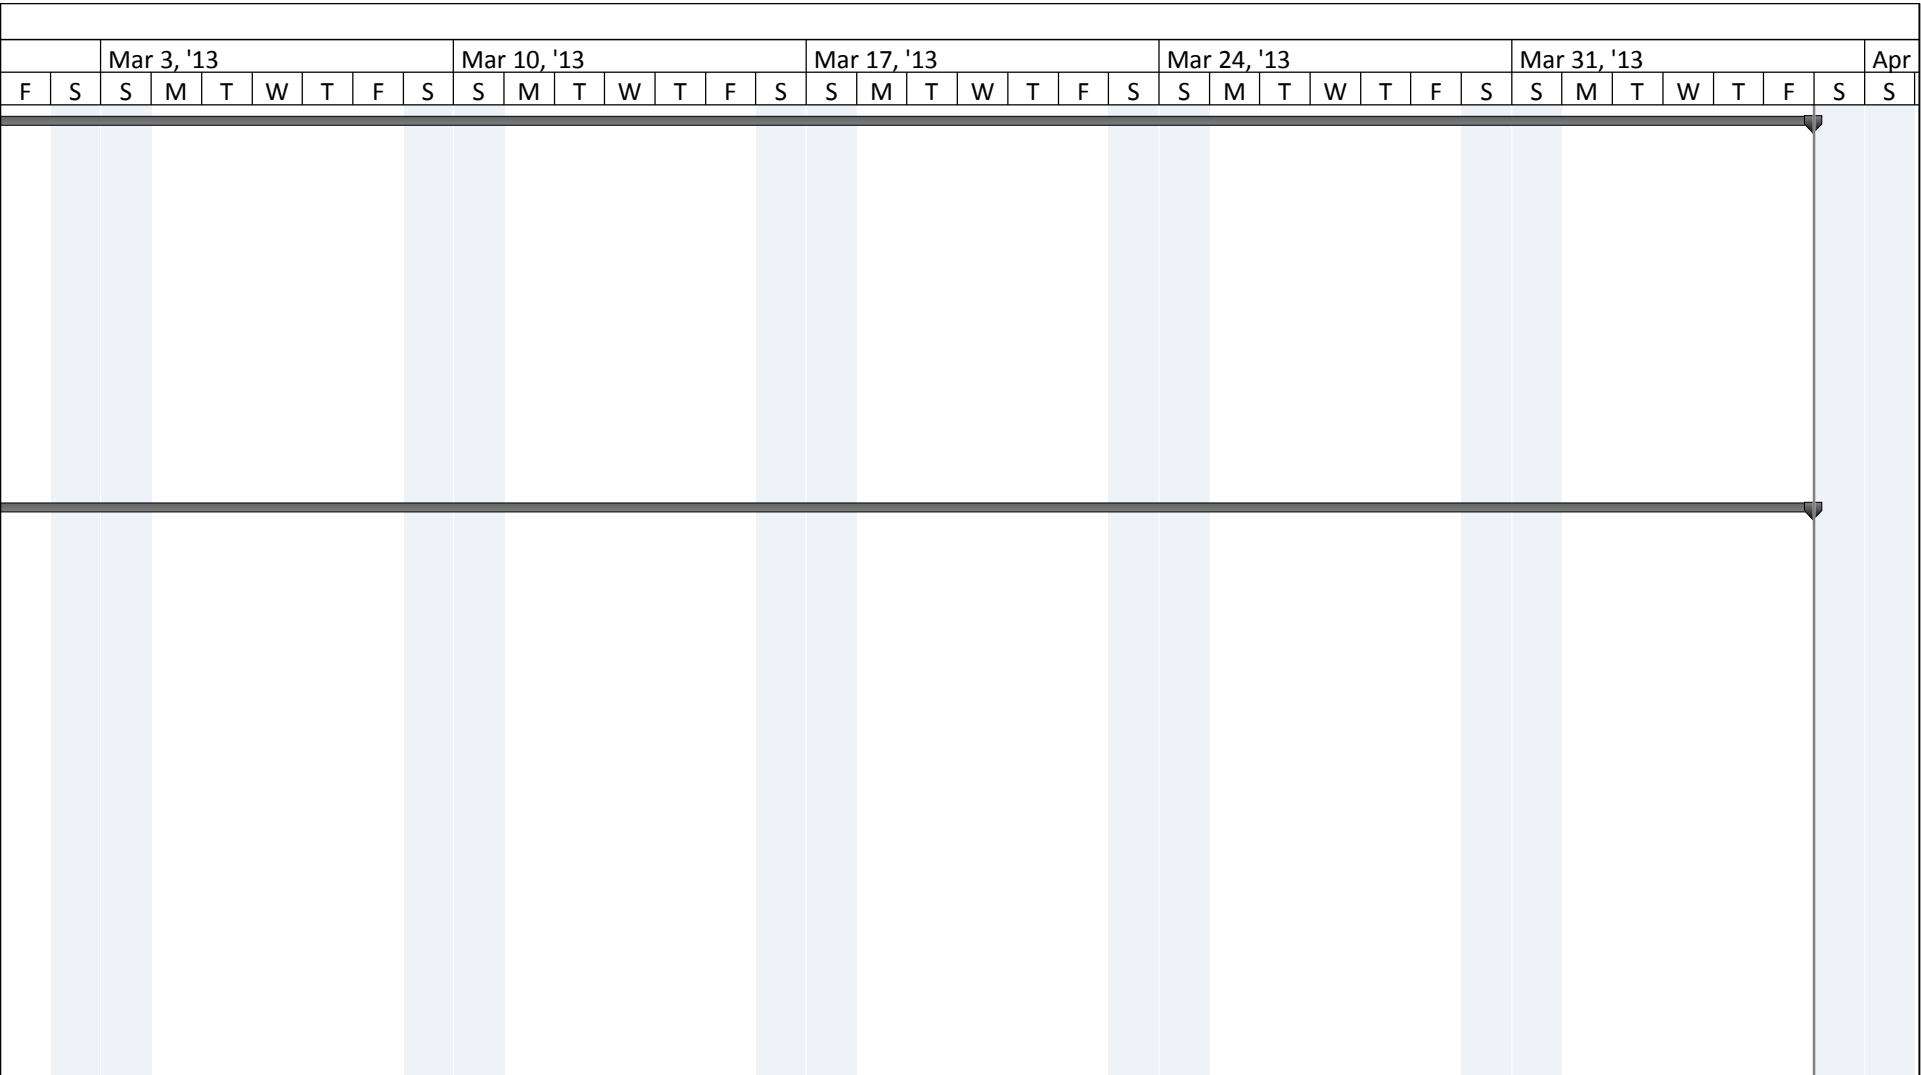


Project: Malware Protection Ove
Date: 2/4/13


Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	

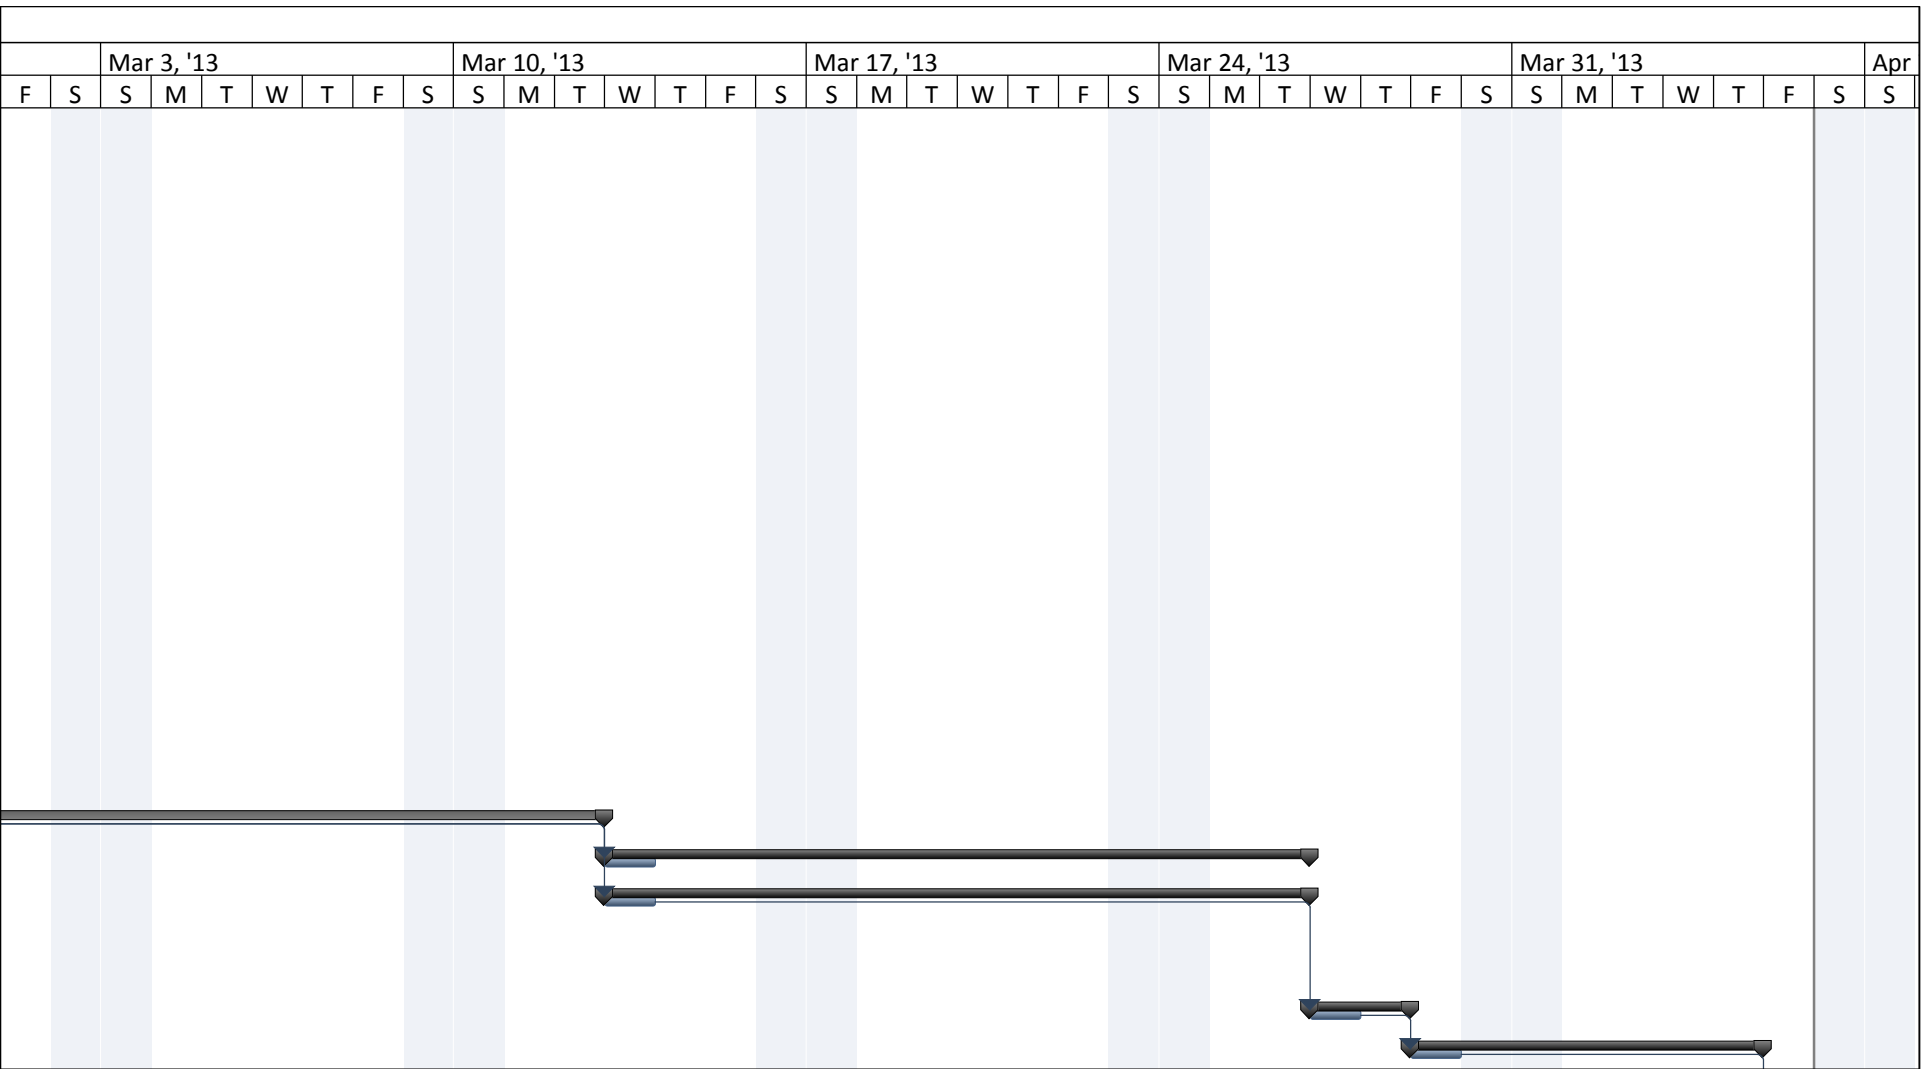


Project: Malware Protection Over Date: 2/4/13	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	

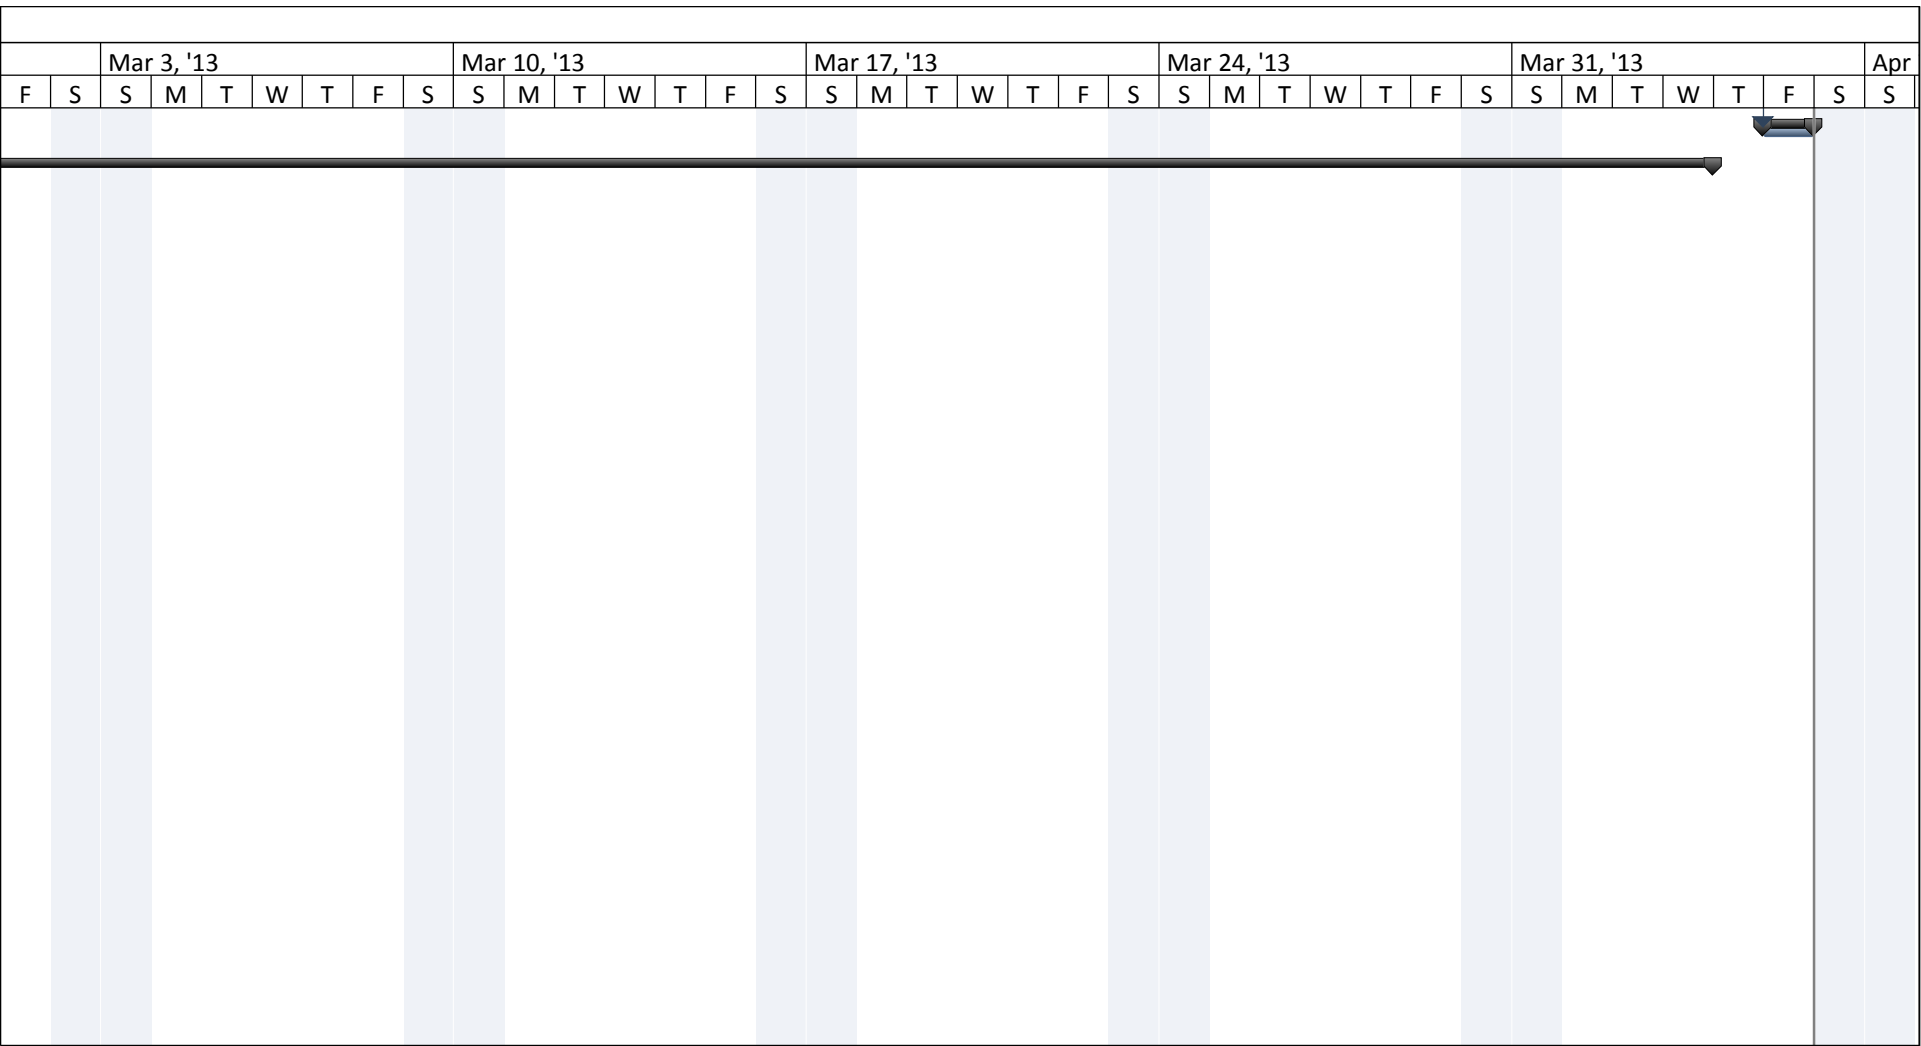

Project: Malware Protection Ove Date: 2/4/13	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	

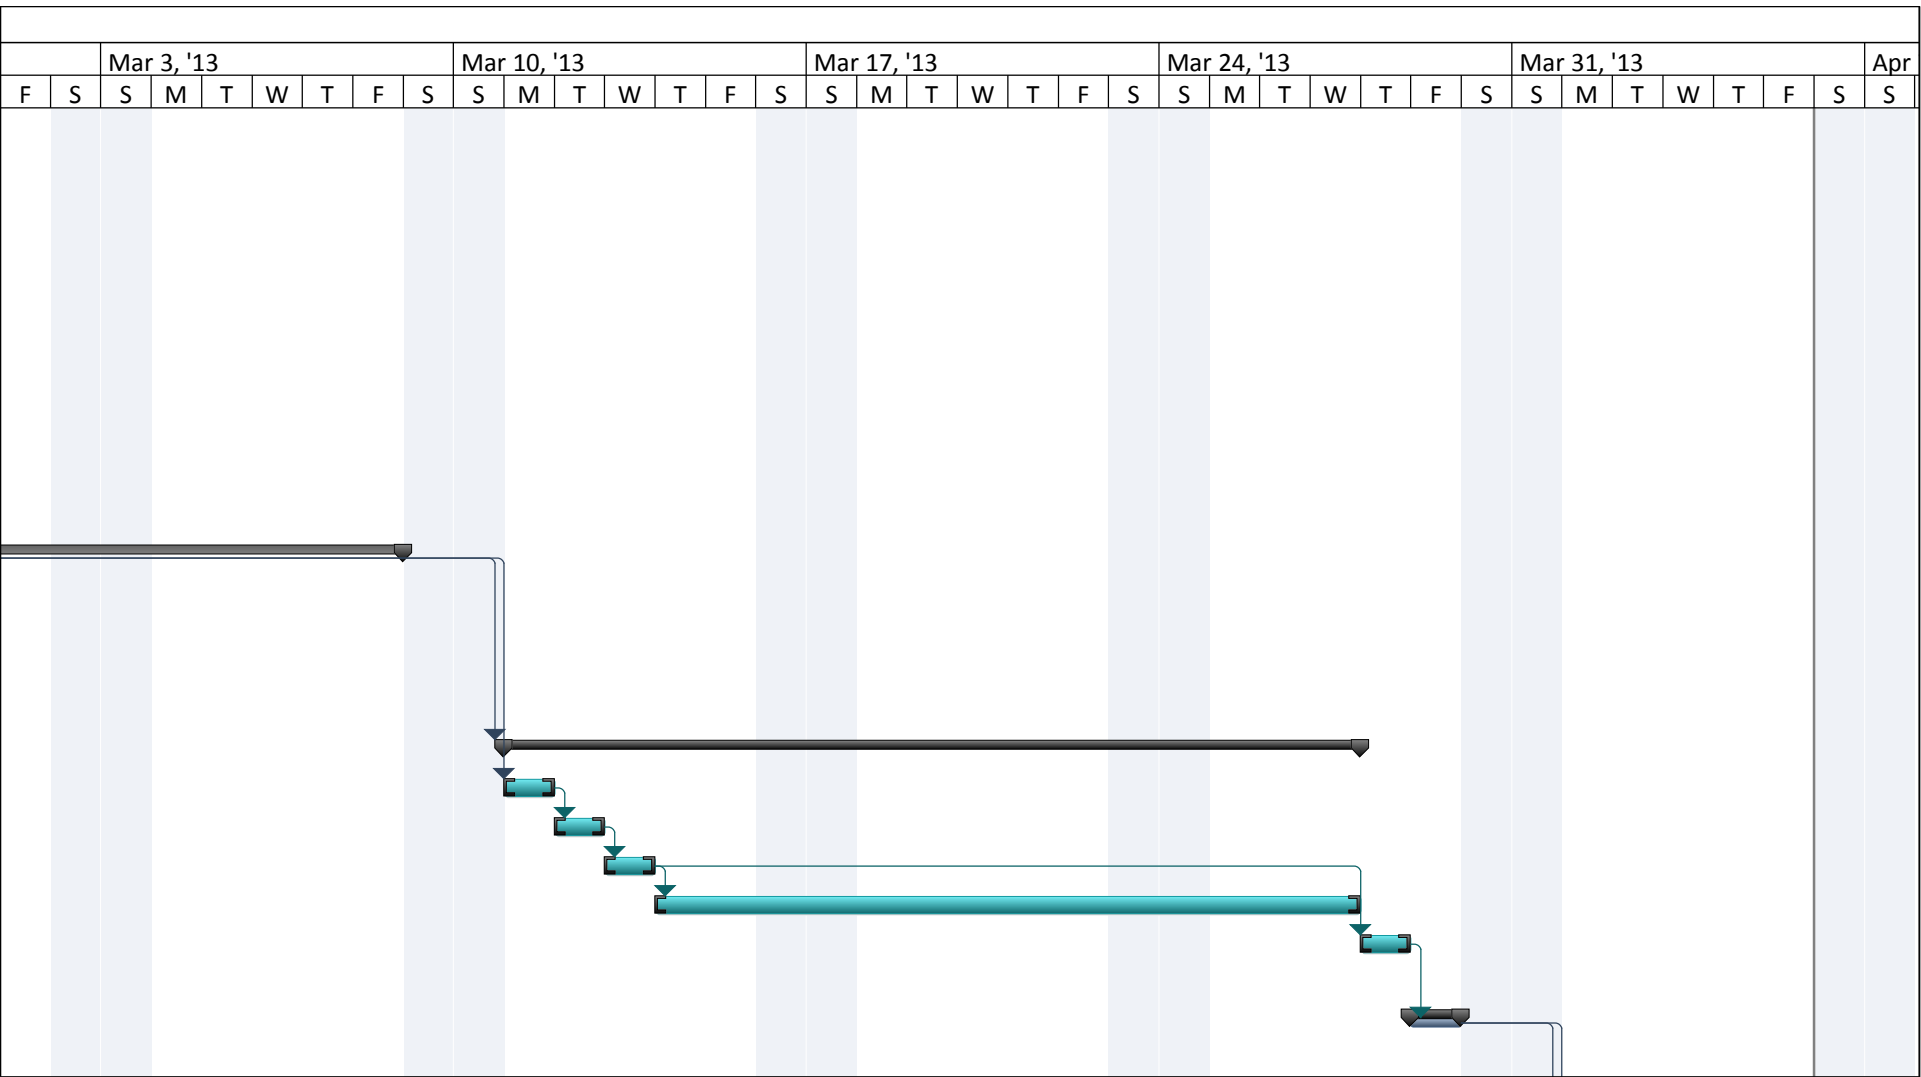

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	

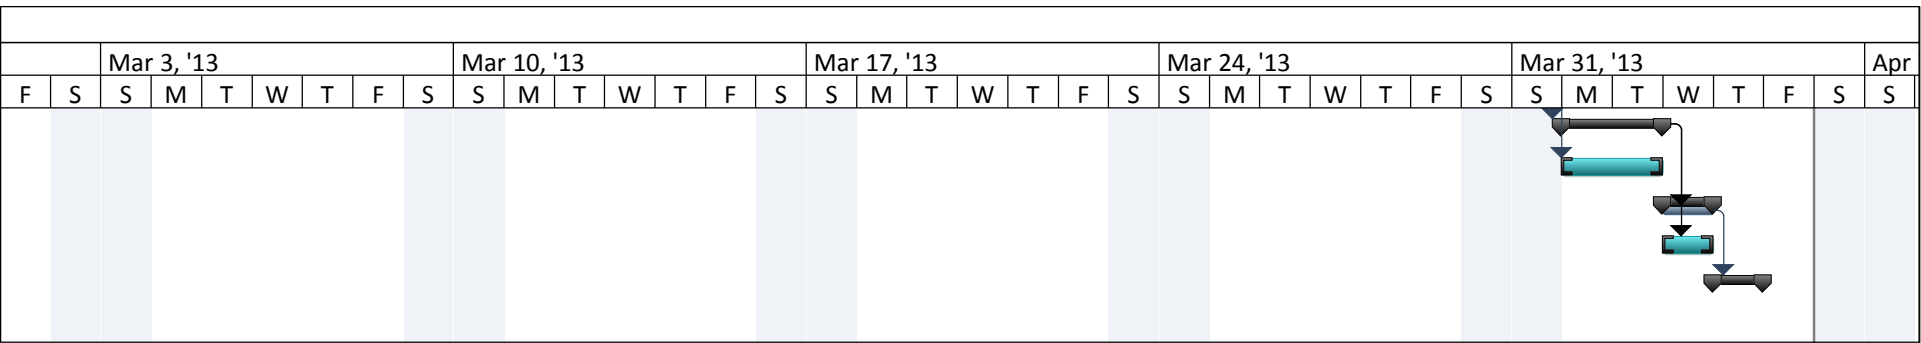

Project: Malware Protection Ove
Date: 2/4/13

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	
