

ID	% Complete	Task Name	Duration	Start	Finish	Predecessors	Resource Names	Nov 4, '12					
								S	S	M	T		
1	20%	<b>Malware Protection Overhaul Project</b>	110 days?	11/5/12	4/5/13								
2	100%	<b>Planning</b>	1 day	11/5/12	11/5/12								
3	100%	Define scope	1 day	11/5/12	11/5/12		Sophie						
4	100%	Review scope with Mark	1 day	11/5/12	11/5/12		Sophie						
5	100%	Kickoff Meeting - include other teams	1 day	11/5/12	11/5/12		Sophie						
6	100%	<b>Communications</b>	1 day?	11/14/12	11/14/12								
7	100%	Initial IT Leader meeting presentation	1 day?	11/14/12	11/14/12		Andrew						
8	100%	Contact IT Leaders to solícite volunteers for pilot	1 day	11/14/12	11/14/12		Tim						
9	100%	Checklist for pilot	1 day	11/14/12	11/14/12		Andrew						
10	16%	<b>Windows Selection</b>	103 days?	11/14/12	4/5/13								
11	50%	<b>System Center 2012 (Forefront) Evaluation</b>	57 days?	11/14/12	1/31/13		Andrew						
12	100%	VM setup	1 day	11/14/12	11/14/12		Richard						
13	100%	Console setup	1 day	11/14/12	11/14/12		Richard						
14	0%	<b>Console and client functionality evaluation</b>			1/31/13								
15	0%	Document pros and cons			1/31/13								
16	75%	<b>ESET Evaluation (v5.0 - Jan 2013)</b>	57 days?	11/14/12	1/31/13		Andrew						
17	100%	VM setup	1 day	11/14/12	11/14/12								
18	100%	Console setup	1 day	11/14/12	11/14/12								
19	100%	Console and client functionality evaluation	1 day	11/14/12	11/14/12								
20	0%	<b>Document pros and cons</b>			1/31/13								
21	7%	<b>Vendor Demo</b>	67 days	11/14/12	2/14/13								
22	100%	Determine invitees	1 day	11/14/12	11/14/12								
23	0%	<b>Determine requirements</b>	1 day	2/1/13	2/1/13								
24	0%	<b>Demo</b>	10 days	2/1/13	2/14/13								

Project: Malware Protection Overhaul Date: 1/4/13	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	

ID	% Complete	Task Name	Duration	Start	Finish	Predecessors	Resource Names	Nov 4, '12				
								S	S	M	T	
25	0%	Team feedback	2 days	2/1/13	2/4/13							
26	<b>20%</b>	<b>Analyze Recommendation and Solution</b>	<b>70 days</b>	<b>11/14/12</b>	<b>2/19/13</b>							
27	100%	Peer school comparion breakdown	1 day	11/14/12	11/14/12		Andrew					
28	0%	Determine any contract/licensing issues	1 day	2/15/13	2/15/13	24						
29	0%	Determine total cost of ownership	1 day	2/15/13	2/15/13	24						
30	0%	Determine benefits and concerns	1 day	2/18/13	2/18/13	29						
31	0%	Determine support process/structure	1 day	2/19/13	2/19/13	30						
32	<b>0%</b>	<b>Sponsor approval</b>	<b>5 days</b>	<b>2/19/13</b>	<b>2/26/13</b>	<b>26</b>						
34	<b>50%</b>	<b>McAfee License</b>	<b>76 days?</b>	<b>11/14/12</b>	<b>2/27/13</b>							
35	100%	Understand current McAfee license constraints	1 day	11/14/12	11/14/12							
36	0%	Adjust McAfee license based on new requirements	1 day?	2/27/13	2/27/13	32						
37	<b>0%</b>	<b>Documentation and communication</b>	<b>1 day?</b>	<b>2/27/13</b>	<b>2/27/13</b>	<b>32</b>						
38	0%	Helpdesk (awareness only)	1 day?	2/27/13	2/27/13							
39	0%	DITR (awareness only)	1 day?	2/27/13	2/27/13							
40	0%	ITLEADERS (awareness and preparing for early adaptors only)	1 day?	2/27/13	2/27/13							
41	<b>0%</b>	<b>Pilot rollout (STAKEHOLDERS)</b>	<b>10 days</b>	<b>2/26/13</b>	<b>3/12/13</b>	<b>32</b>						
47	<b>0%</b>	<b>Procurement</b>	<b>10 days</b>	<b>3/12/13</b>	<b>3/26/13</b>	<b>41</b>						
52	<b>0%</b>	<b>EARLY ADOPTERS</b>	<b>10 days</b>	<b>3/12/13</b>	<b>3/26/13</b>	<b>41</b>						
57	0%	Final Checkpoint: Present all feedback including beta rollout feedback to Sponsor	1 day?	11/14/12	11/14/12							
58	<b>0%</b>	<b>General Communications</b>	<b>2 days</b>	<b>3/26/13</b>	<b>3/28/13</b>	<b>52</b>						
60	<b>0%</b>	<b>Prep Helpdesk for full rollout support</b>	<b>5 days</b>	<b>3/28/13</b>	<b>4/4/13</b>	<b>58</b>						

Project: Malware Protection Over Date: 1/4/13

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	

ID	% Complete	Task Name	Duration	Start	Finish	Predecessors	Resource Names	Nov 4, '12			
								S	S	M	T
62	0%	<b>Full rollout (COMMUNITY)</b>	1 day	4/4/13	4/5/13	60					
64	16%	<b>MAC Selection</b>	101 days?	11/14/12	4/3/13						
65	75%	<b>Evaluation</b>	47 days?	11/28/12	1/31/13						
66	75%	<b>Sophos Evaluation</b>	47 days?	11/28/12	1/31/13		Andrew				
67	100%	VM setup	1 day	11/28/12	11/28/12						
68	100%	Console setup	1 day	12/5/12	12/5/12						
69	100%	Console and client functionality evaluation	1 day	11/28/12	11/28/12						
70	0%	<b>Document Pros and cons</b>			1/31/13						
71	75%	<b>ESET Evaluation (v5.0 - Jan 2013)</b>	42 days?	12/5/12	1/31/13		Andrew				
72	100%	VM setup	1 day	12/5/12	12/5/12						
73	100%	Console setup	1 day	12/5/12	12/5/12						
74	100%	Console and client functionality evaluation	1 day	12/5/12	12/5/12						
75	0%	<b>Document pros and cons</b>			1/31/13						
76	40%	<b>Vendor Demo</b>	59 days?	11/14/12	2/4/13						
77	100%	Determine which vendor(s) to demo	1 day	11/14/12	11/14/12						
78	100%	Determine invitees	1 day	11/14/12	11/14/12						
79	0%	Determine requirements			2/1/13						
80	0%	Demo	1 day?	2/1/13	2/1/13						
81	0%	Team feedback	1 day	2/4/13	2/4/13	80					
82	0%	<b>Analyze Recommendation and Solution</b>	2 days	2/7/13	2/8/13						
83	0%	Determine any contract/licensing issues	2 days	2/7/13	2/8/13	40					
84	0%	Determine total cost of ownership	2 days	2/7/13	2/8/13	40					
85	0%	Determine benefits and concerns	2 days	2/7/13	2/8/13	40					
86	0%	Determine support process/structure	2 days	2/7/13	2/8/13	40					

Project: Malware Protection Over Date: 1/4/13

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	

ID	% Complete	Task Name	Duration	Start	Finish	Predecessors	Resource Names	Nov 4, '12			
								S	S	M	T
87	0%	<b>Sponsor approval</b>	5 days	2/8/13	2/15/13	82					
89	0%	<b>Documentation and communication</b>	3 days	2/18/13	2/20/13	87					
90	0%	Helpdesk (awareness only)	1 day	2/18/13	2/18/13	87					
91	0%	DITR (awareness only)	1 day	2/19/13	2/19/13	90					
92	0%	ITLEADERS (awareness and preparing for early adaptors only)	1 day	2/20/13	2/20/13	91					
93	0%	<b>Pilot rollout (STAKEHOLDERS)</b>	5 days	2/18/13	2/22/13						
94	0%	Determine pilot rollout team	1 day	2/18/13	2/18/13	87					
95	0%	Determine timelines	1 day	2/20/13	2/20/13	94					
96	0%	determine pilot rollout strategy	1 day	2/21/13	2/21/13	95					
97	0%	Collect feedback	1 day	2/22/13	2/22/13	96					
98	0%	<b>Procurement</b>	10 days	2/22/13	3/8/13	93					
99	0%	Negotiate pricing									
100	0%	Contract agreement and signature									
101	0%	Purchase									
102	0%	Reminder: adjust McAfee contract									
103	0%	<b>EARLY ADOPTERS</b>	13 days	3/11/13	3/27/13	98					
104	0%	Determine early adopters participants	1 day	3/11/13	3/11/13	98					
105	0%	Determine timelines	1 day	3/12/13	3/12/13	104					
106	0%	determine beta rollout strategy	1 day	3/13/13	3/13/13	105					
107	0%	collect feedback	10 days	3/14/13	3/27/13	106					
108	0%	Final Checkpoint: Present all feedback including beta rollout feedback to Sponsor	1 day?	3/28/13	3/28/13	106					
109	0%	<b>General Communications</b>	1 day	3/28/13	3/29/13	108					
110	0%	to community									

Project: Malware Protection Over Date: 1/4/13

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	

ID	% Complete	Task Name	Duration	Start	Finish	Predecessors	Resource Names	Nov 4, '12			
								S	S	M	T
								111	0%	<b>Prep Helpdesk for full rollout support</b>	<b>2 days</b>
112	0%	any additional training/documentation	2 days	4/1/13	4/2/13	109					
113	0%	<b>Full rollout (COMMUNITY)</b>	<b>1 day</b>	<b>4/2/13</b>	<b>4/3/13</b>	<b>111</b>					
114	0%	Provide software to SWRT for distribution	1 day	4/3/13	4/3/13	111					
115	0%	<b>Project Wrapup</b>	<b>1 day?</b>	<b>4/3/13</b>	<b>4/4/13</b>	<b>113</b>					
116	0%	closeout project									

Project: Malware Protection Ove Date: 1/4/13	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	

				Nov 11, '12				Nov 18, '12				Nov 25, '12				Dec 2, '12				Dec 9, '12											
W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S

ophie  
ophie  
ophie



Andrew

Tim

Andrew


Richard

Richard



Project: Malware Protection Ove  
Date: 1/4/13

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	

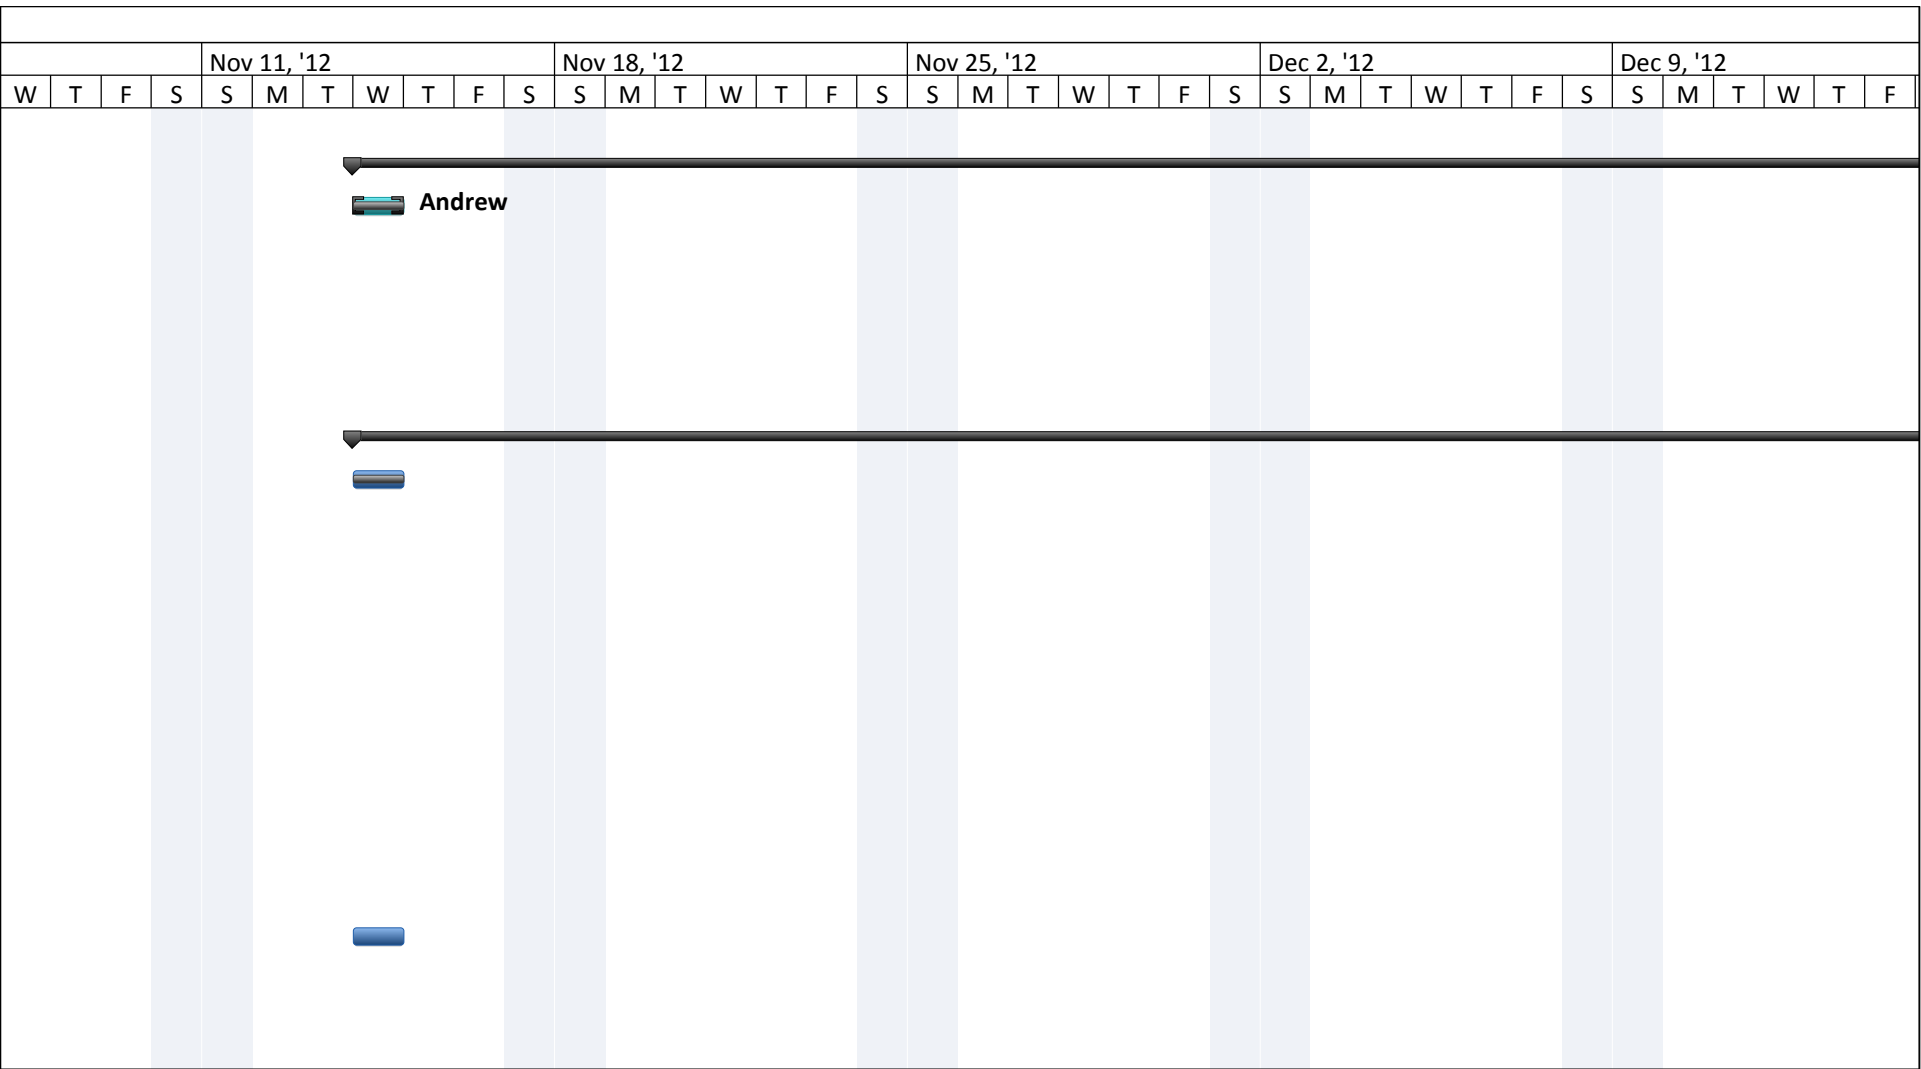


Andrew




Project: Malware Protection Over  
Date: 1/4/13

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	

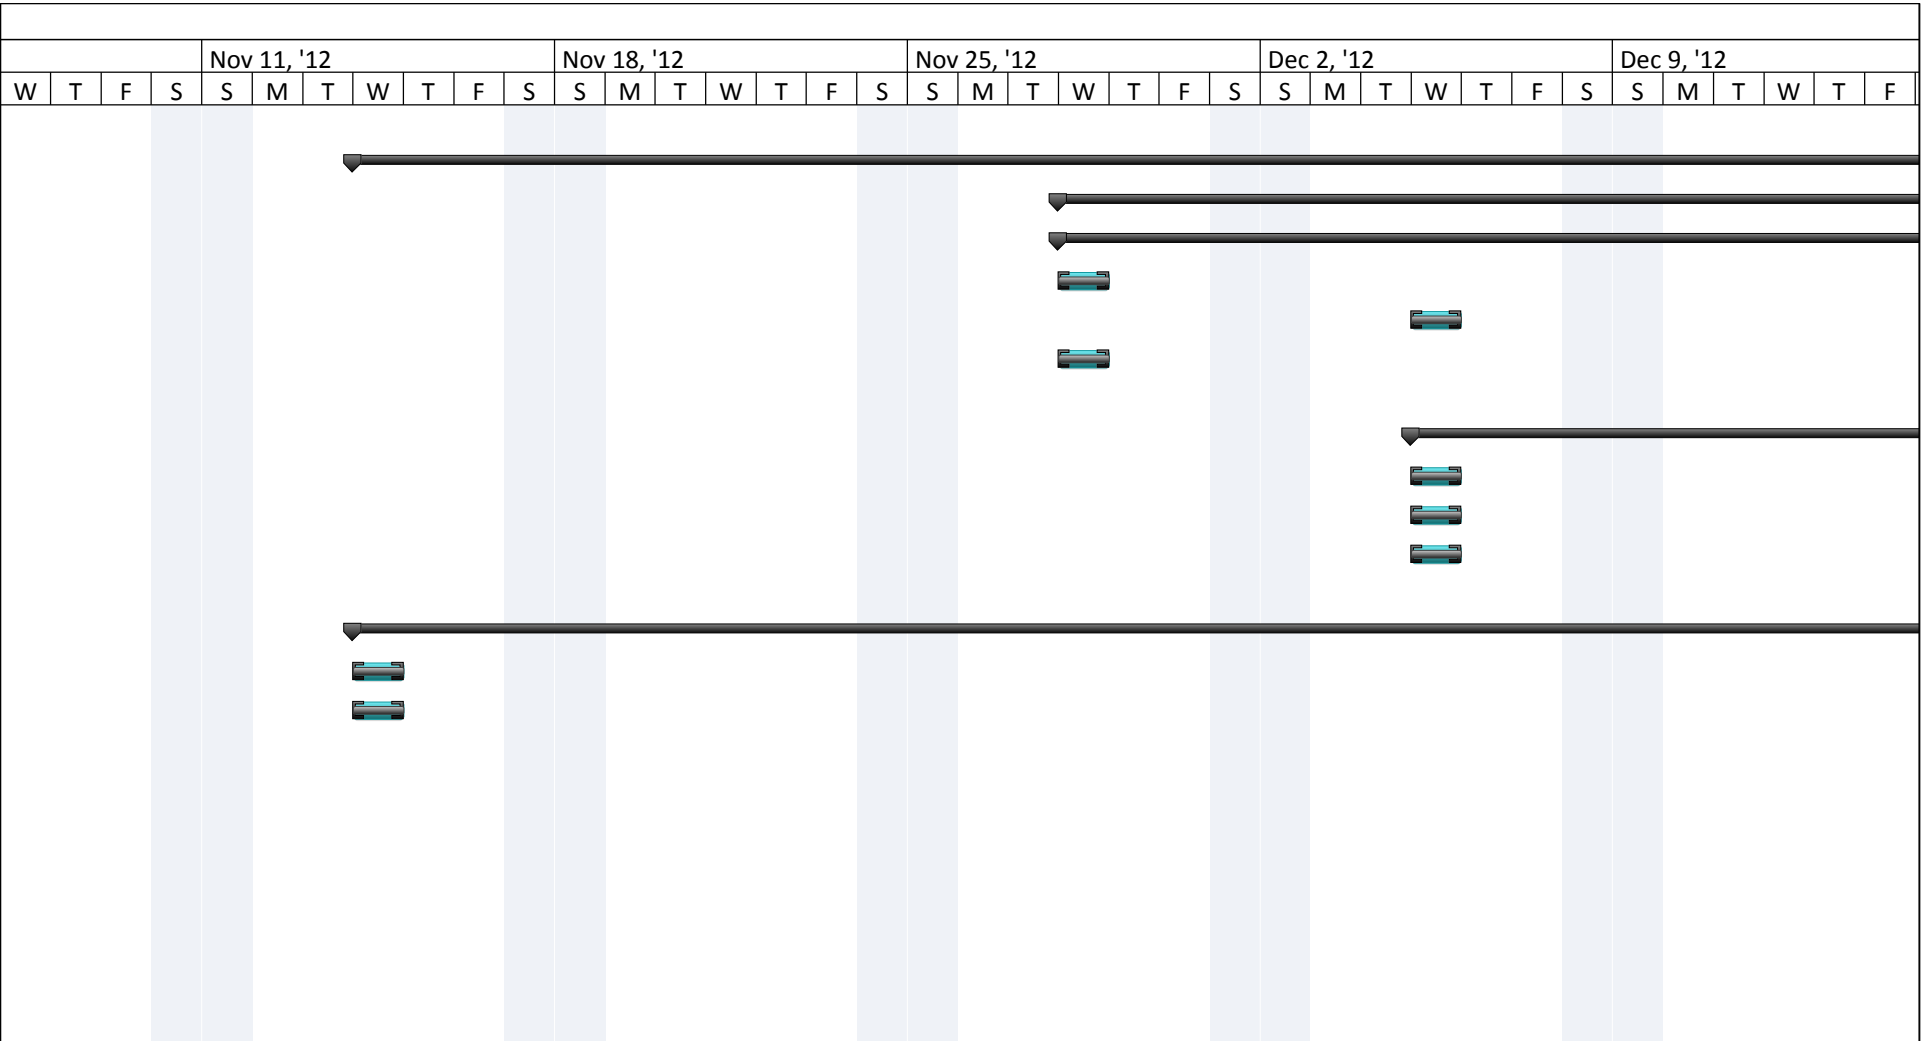

Project: Malware Protection Over Date: 1/4/13	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	



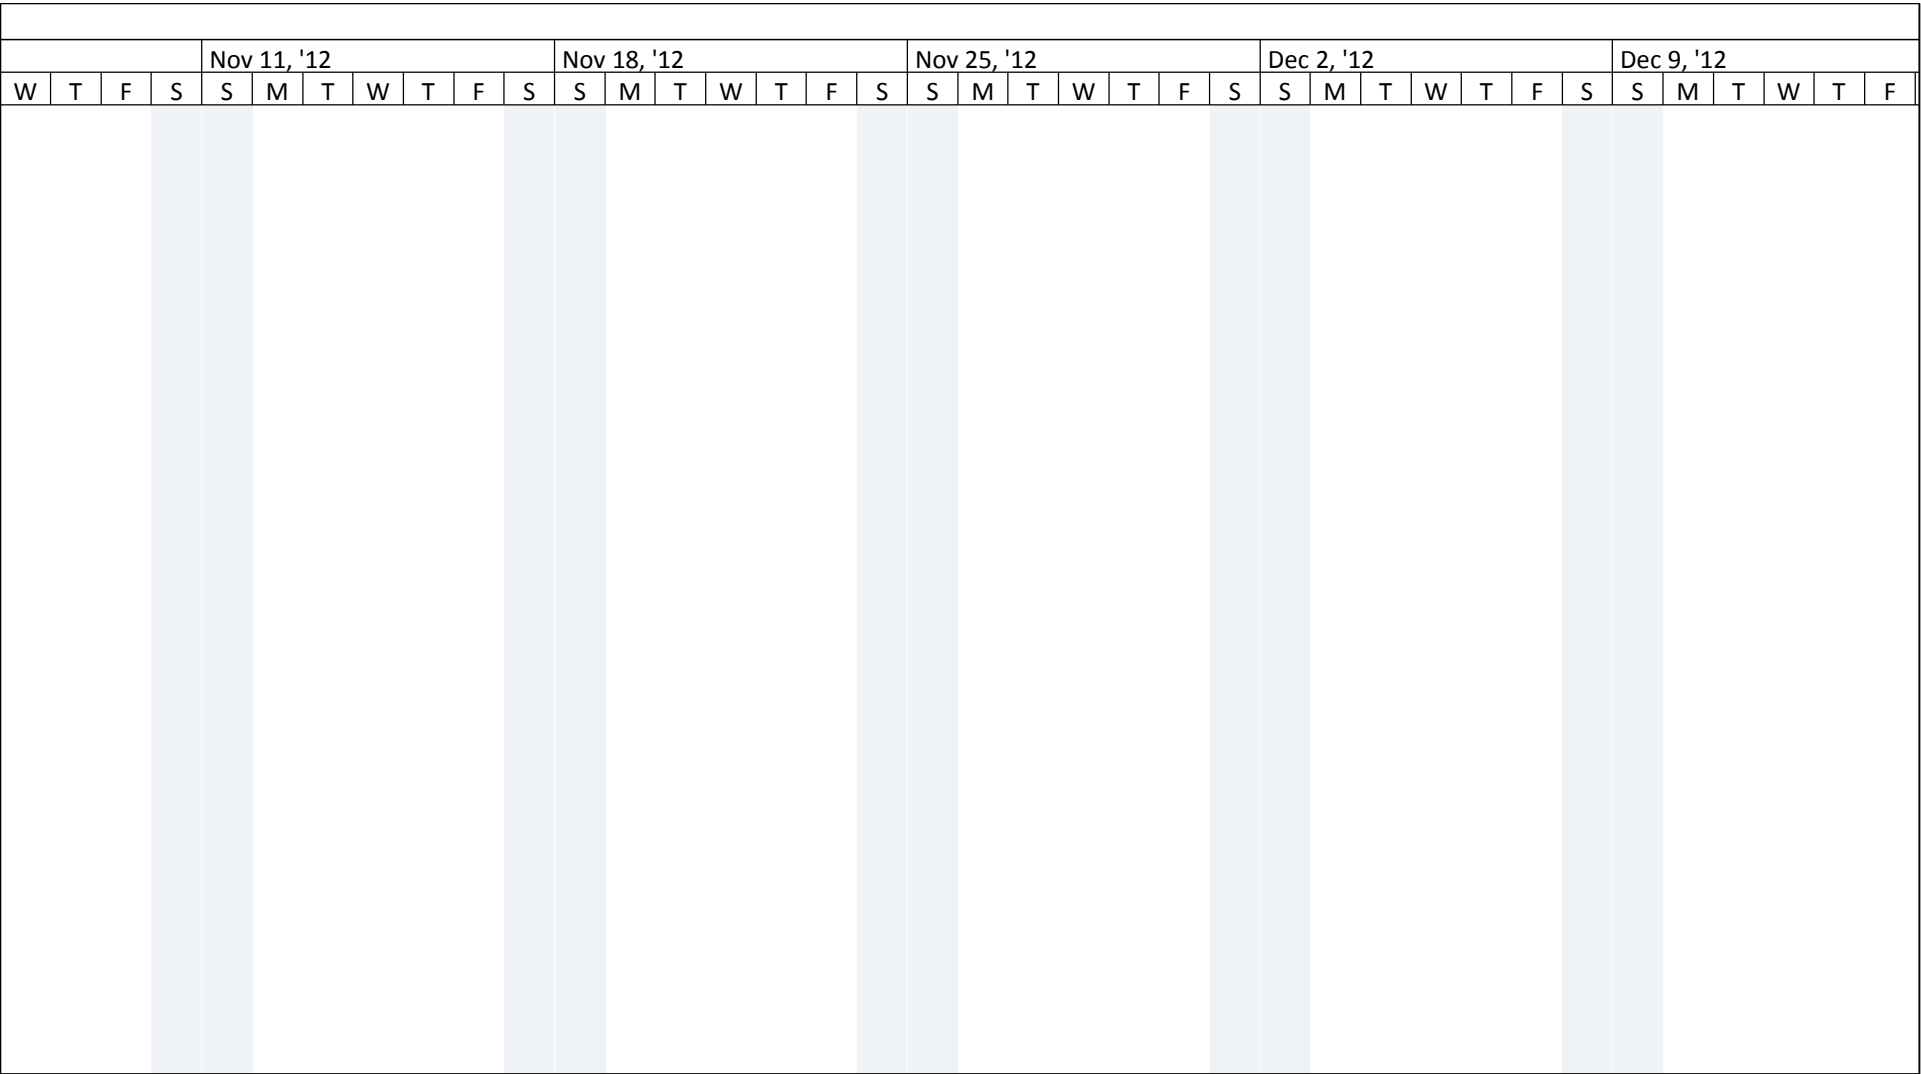

Project: Malware Protection Ove  
Date: 1/4/13


Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	

				Nov 11, '12				Nov 18, '12				Nov 25, '12				Dec 2, '12				Dec 9, '12												
W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F		




Project: Malware Protection Ove  
Date: 1/4/13

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	

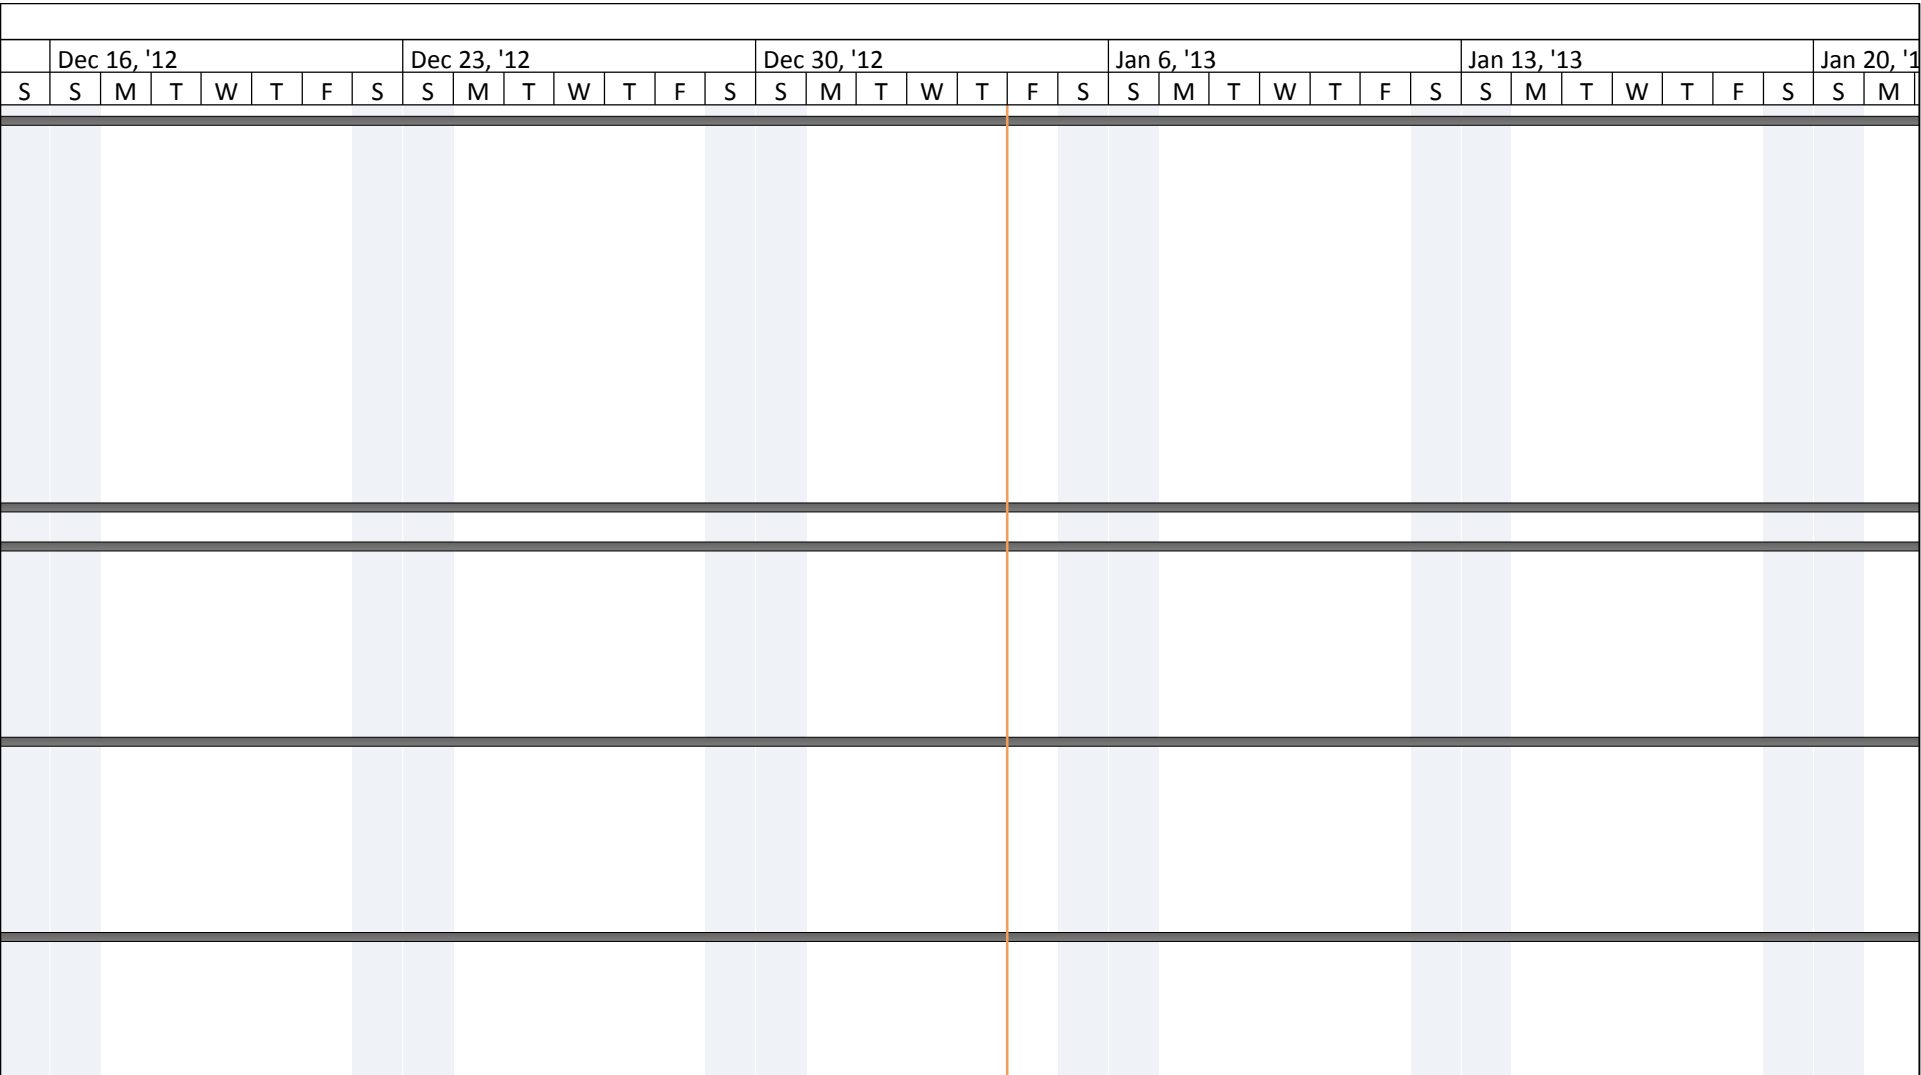


Project: Malware Protection Overdue  
Date: 1/4/13

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	

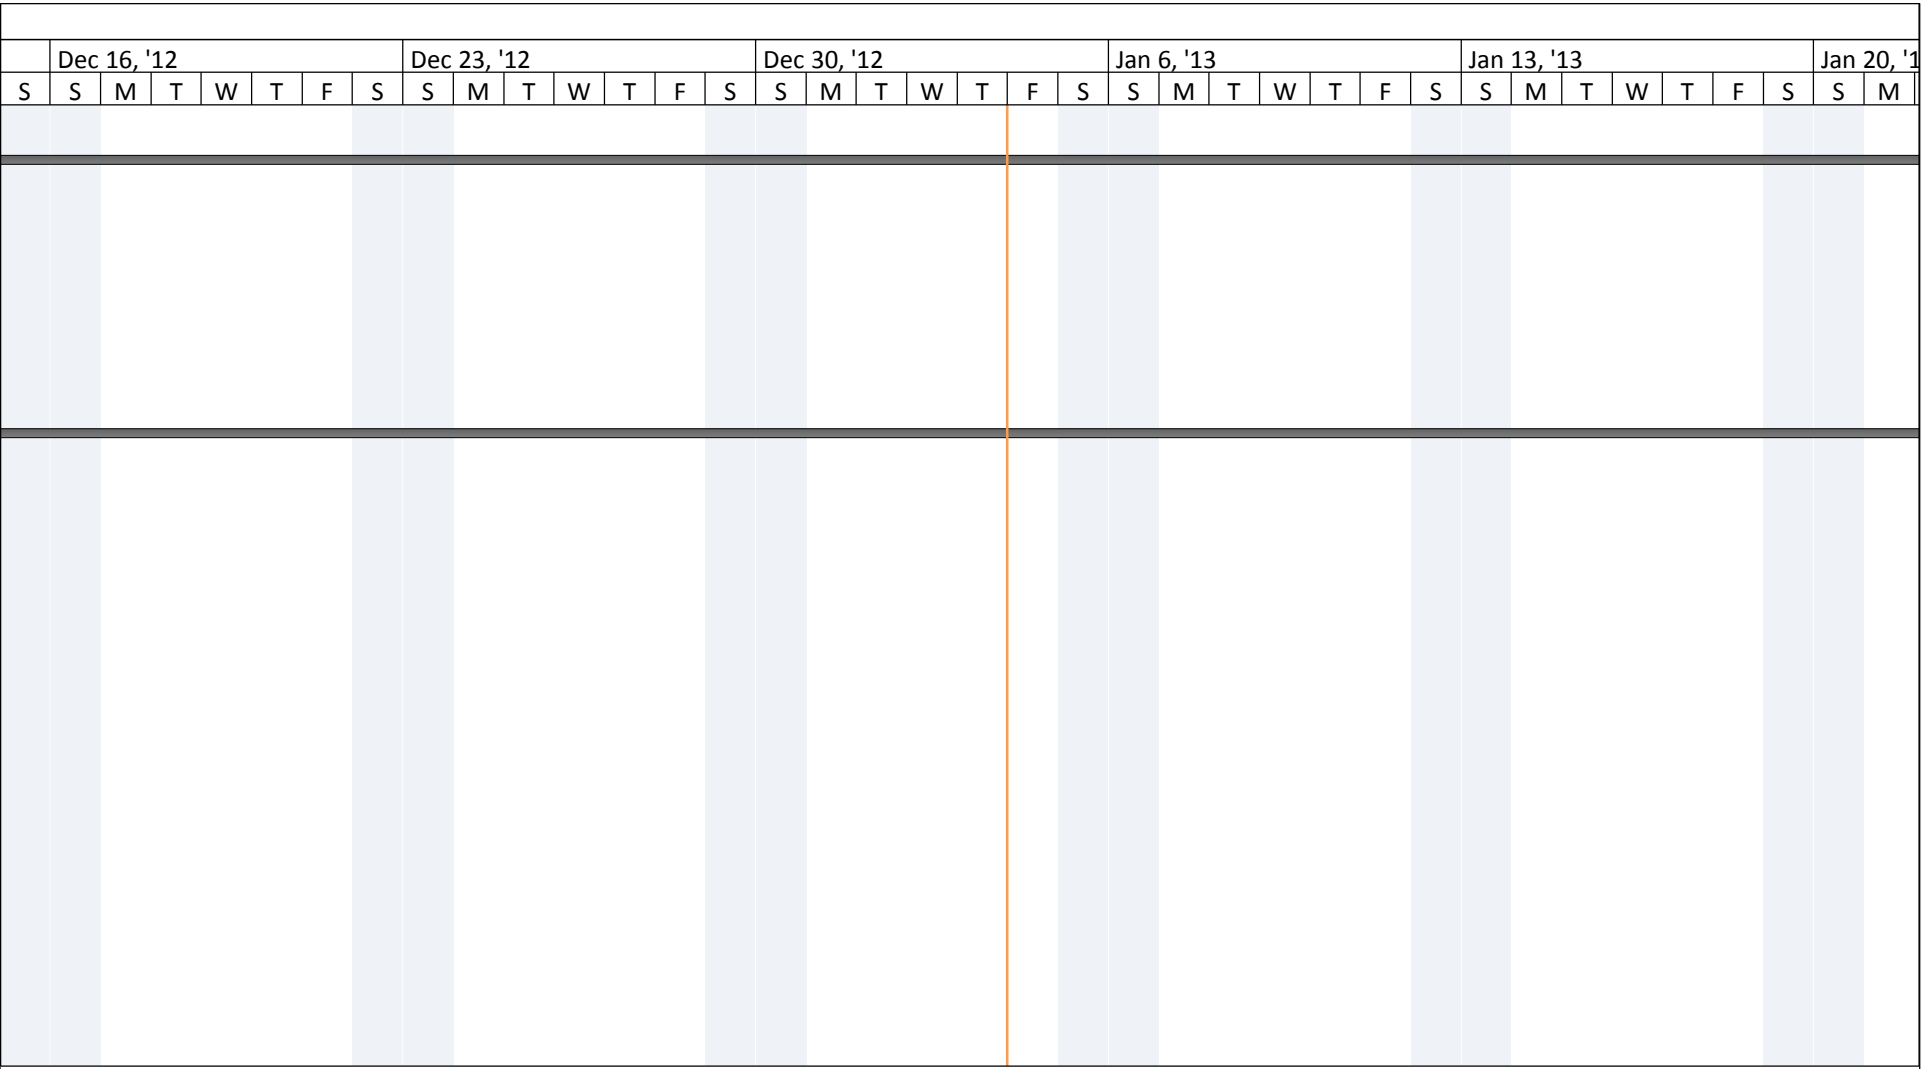


Project: Malware Protection Ove  
Date: 1/4/13

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	

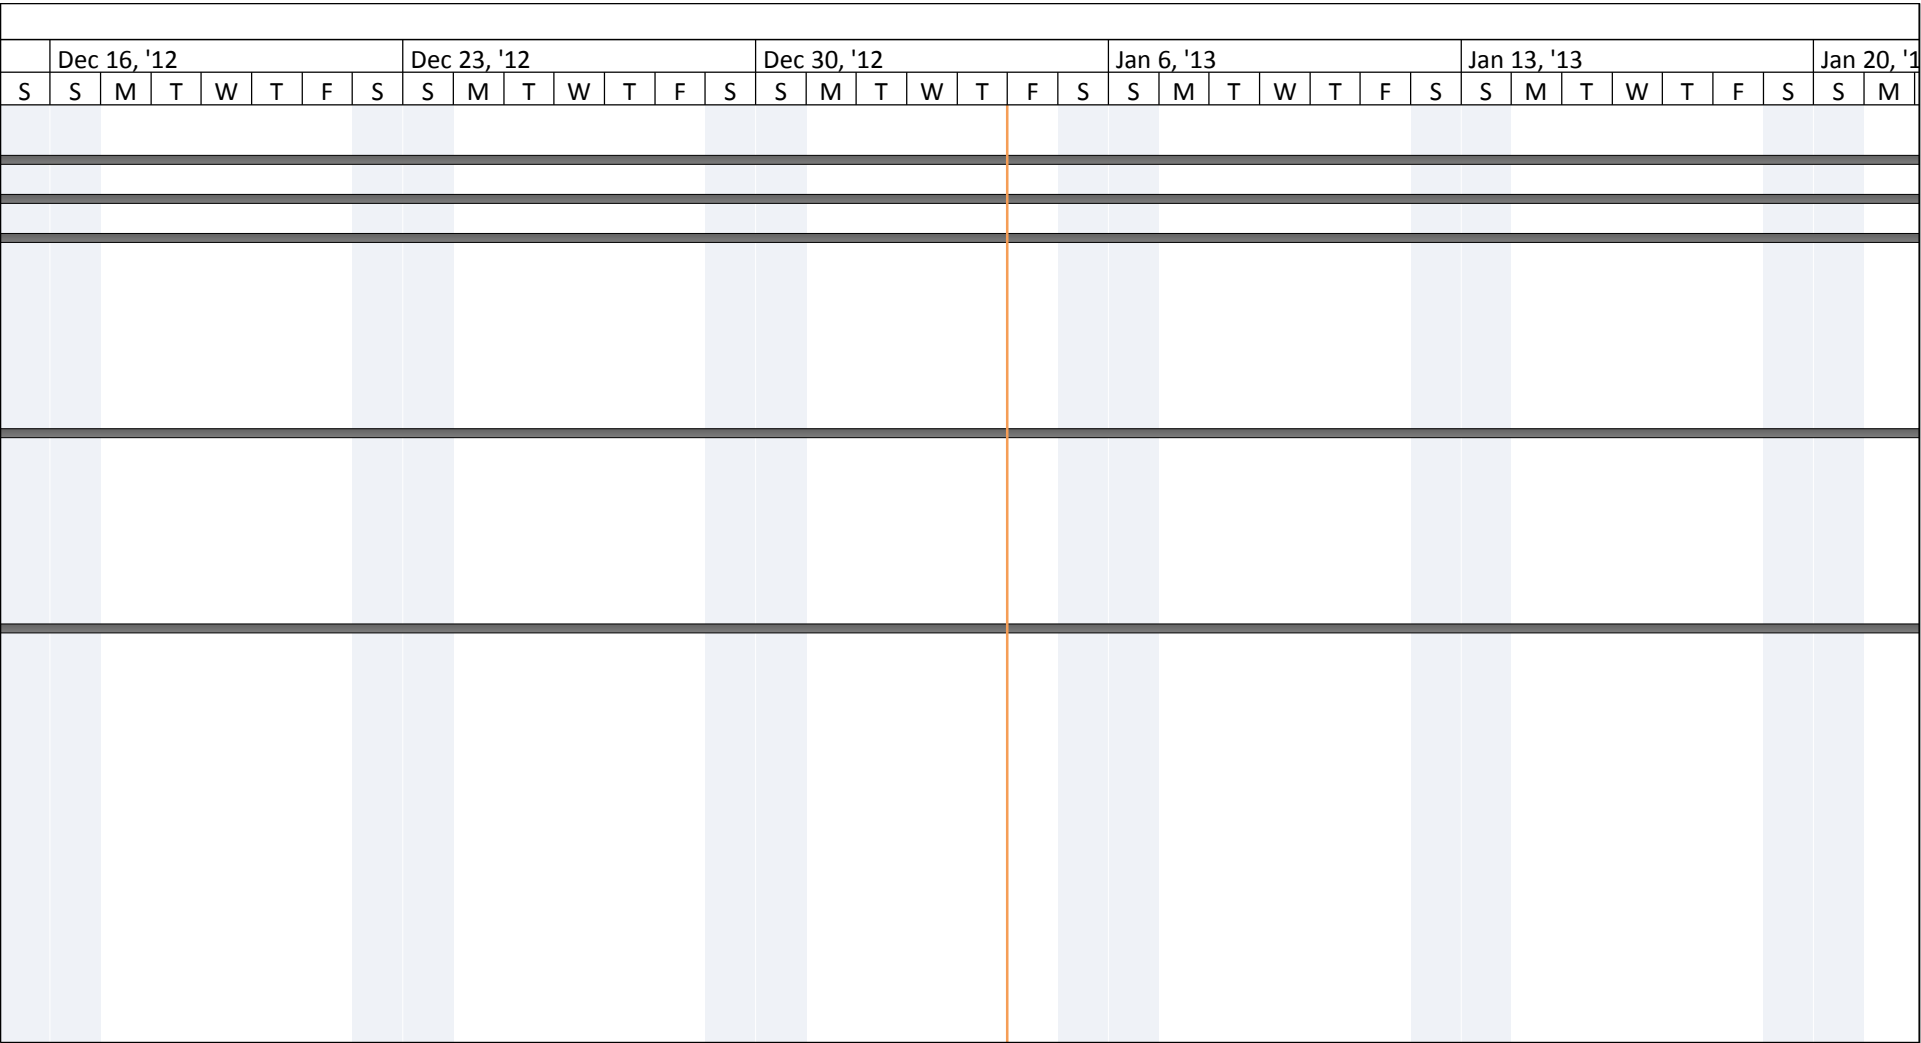


Project: Malware Protection Over Date: 1/4/13

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	

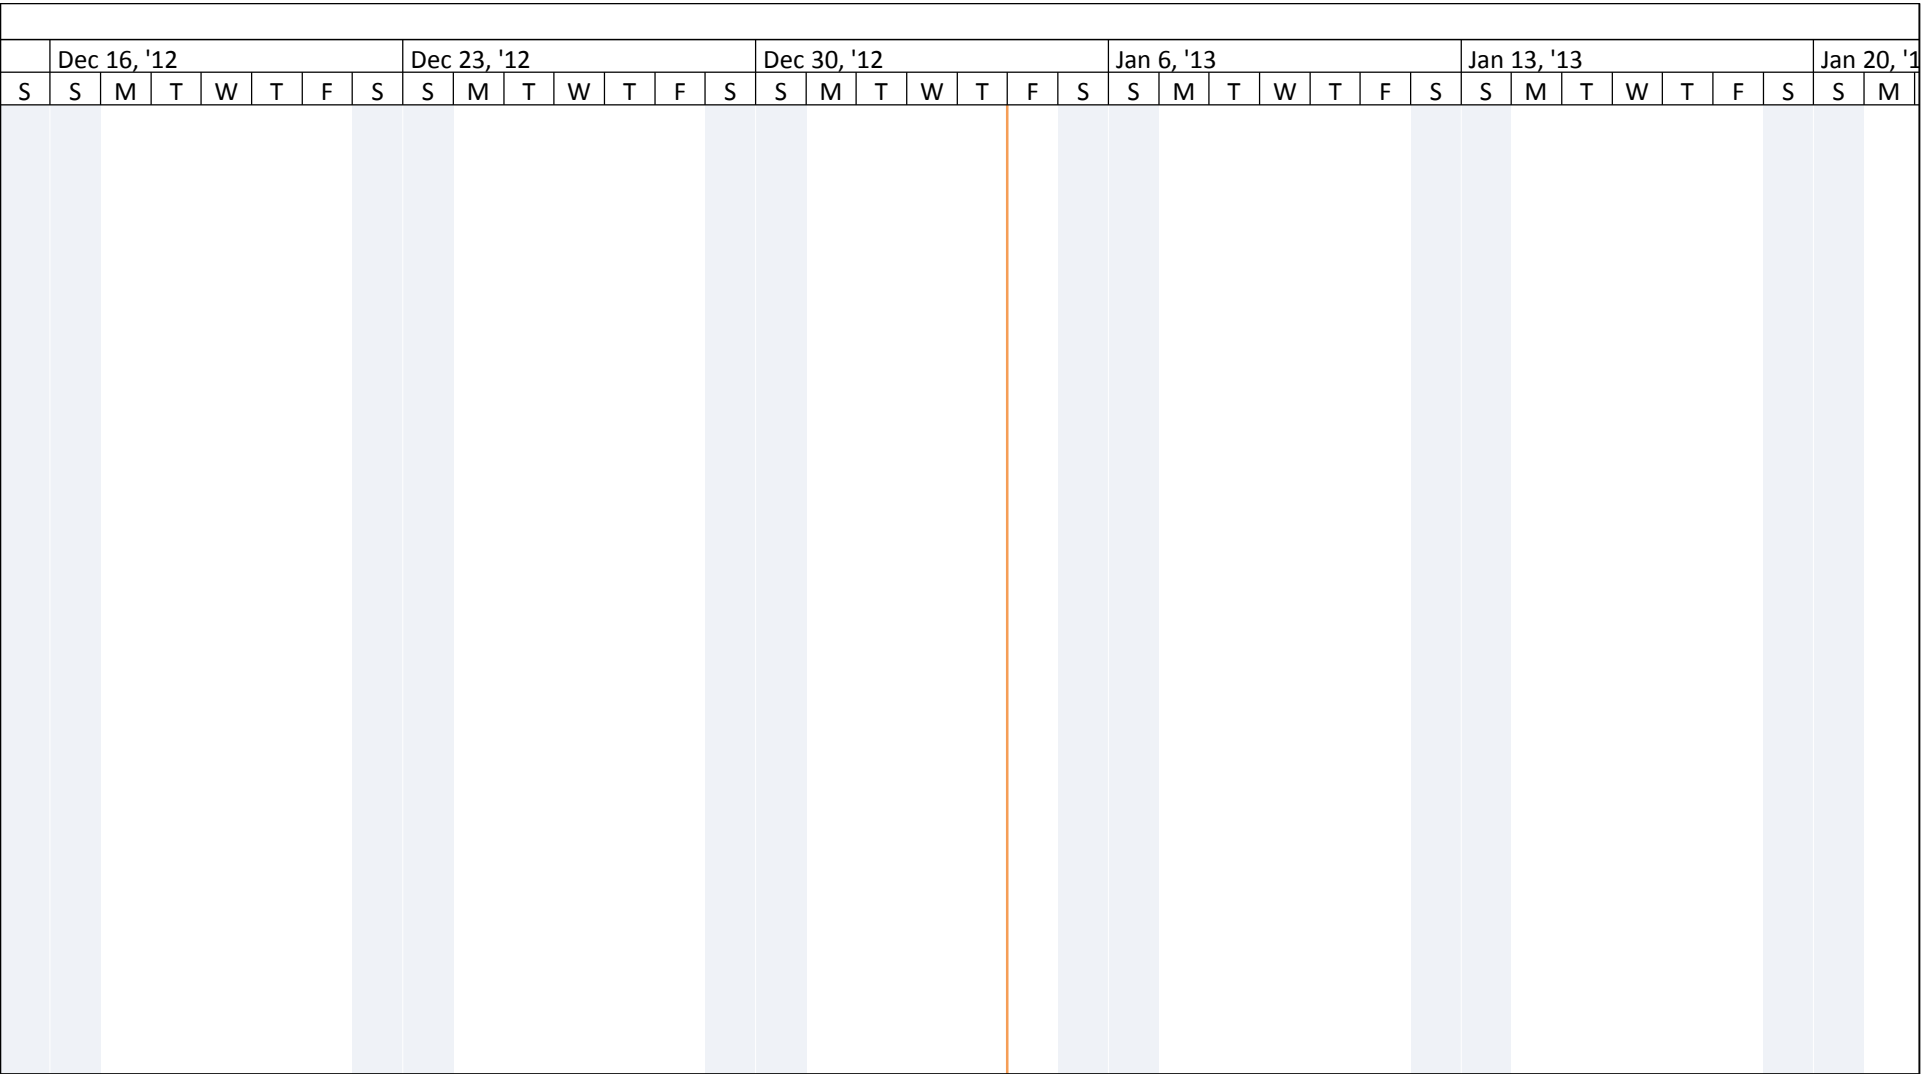

Project: Malware Protection Ove  
Date: 1/4/13

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	




Project: Malware Protection Ove  
Date: 1/4/13

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	

3 Jan 27, '13 Feb 3, '13 Feb 10, '13 Feb 17, '13 Feb 24, '13


T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T

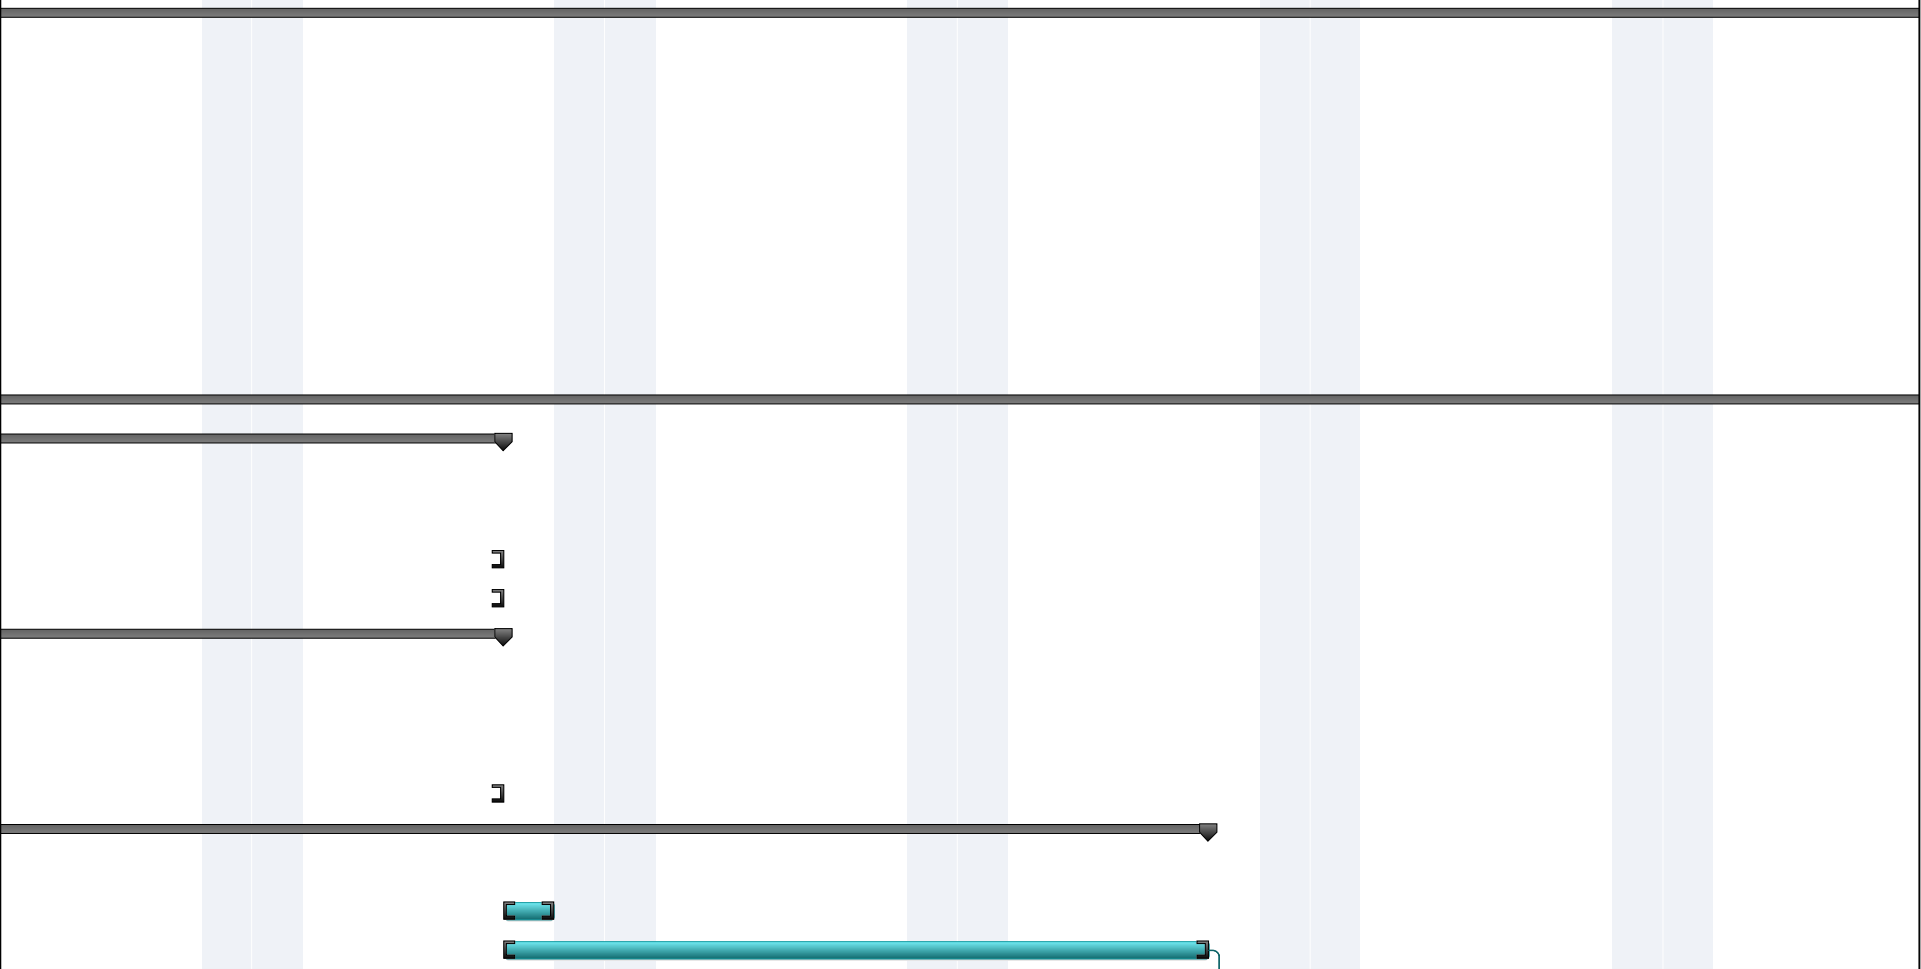


Project: Malware Protection Ove  
Date: 1/4/13

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	



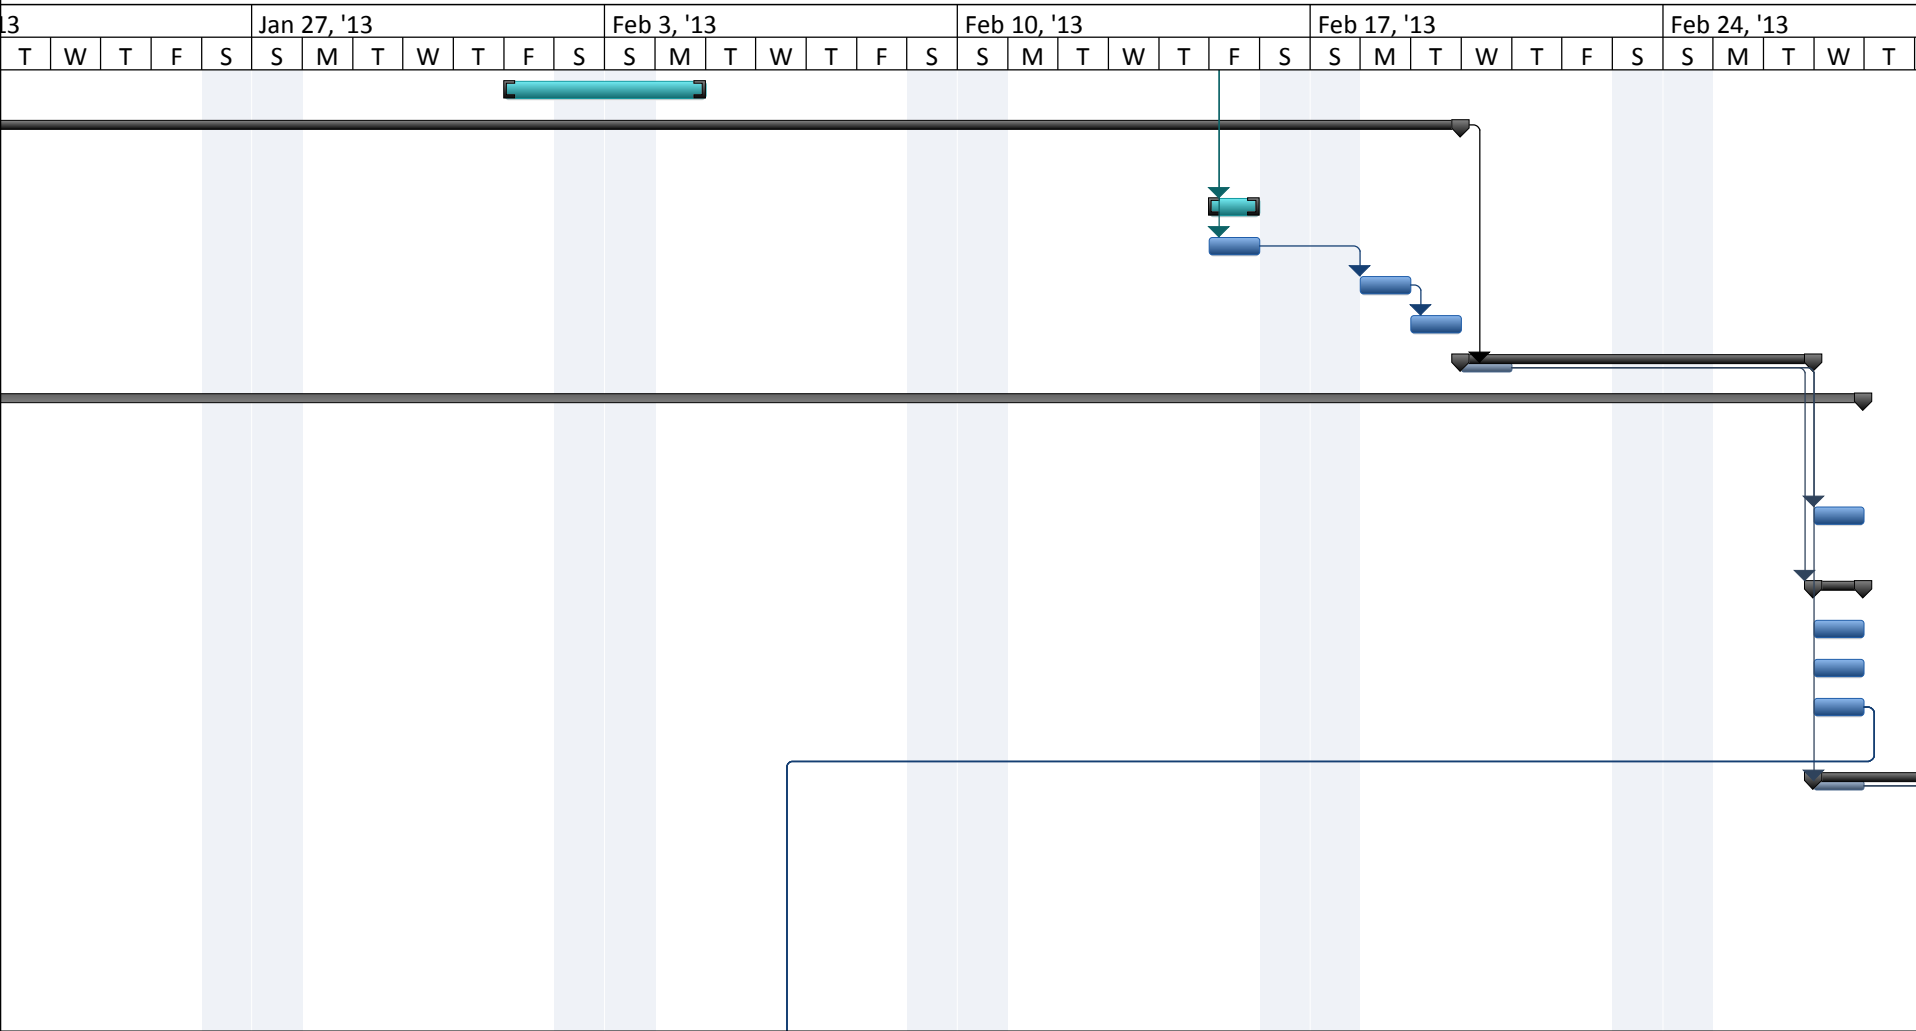


Project: Malware Protection Overdue Date: 1/4/13	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	

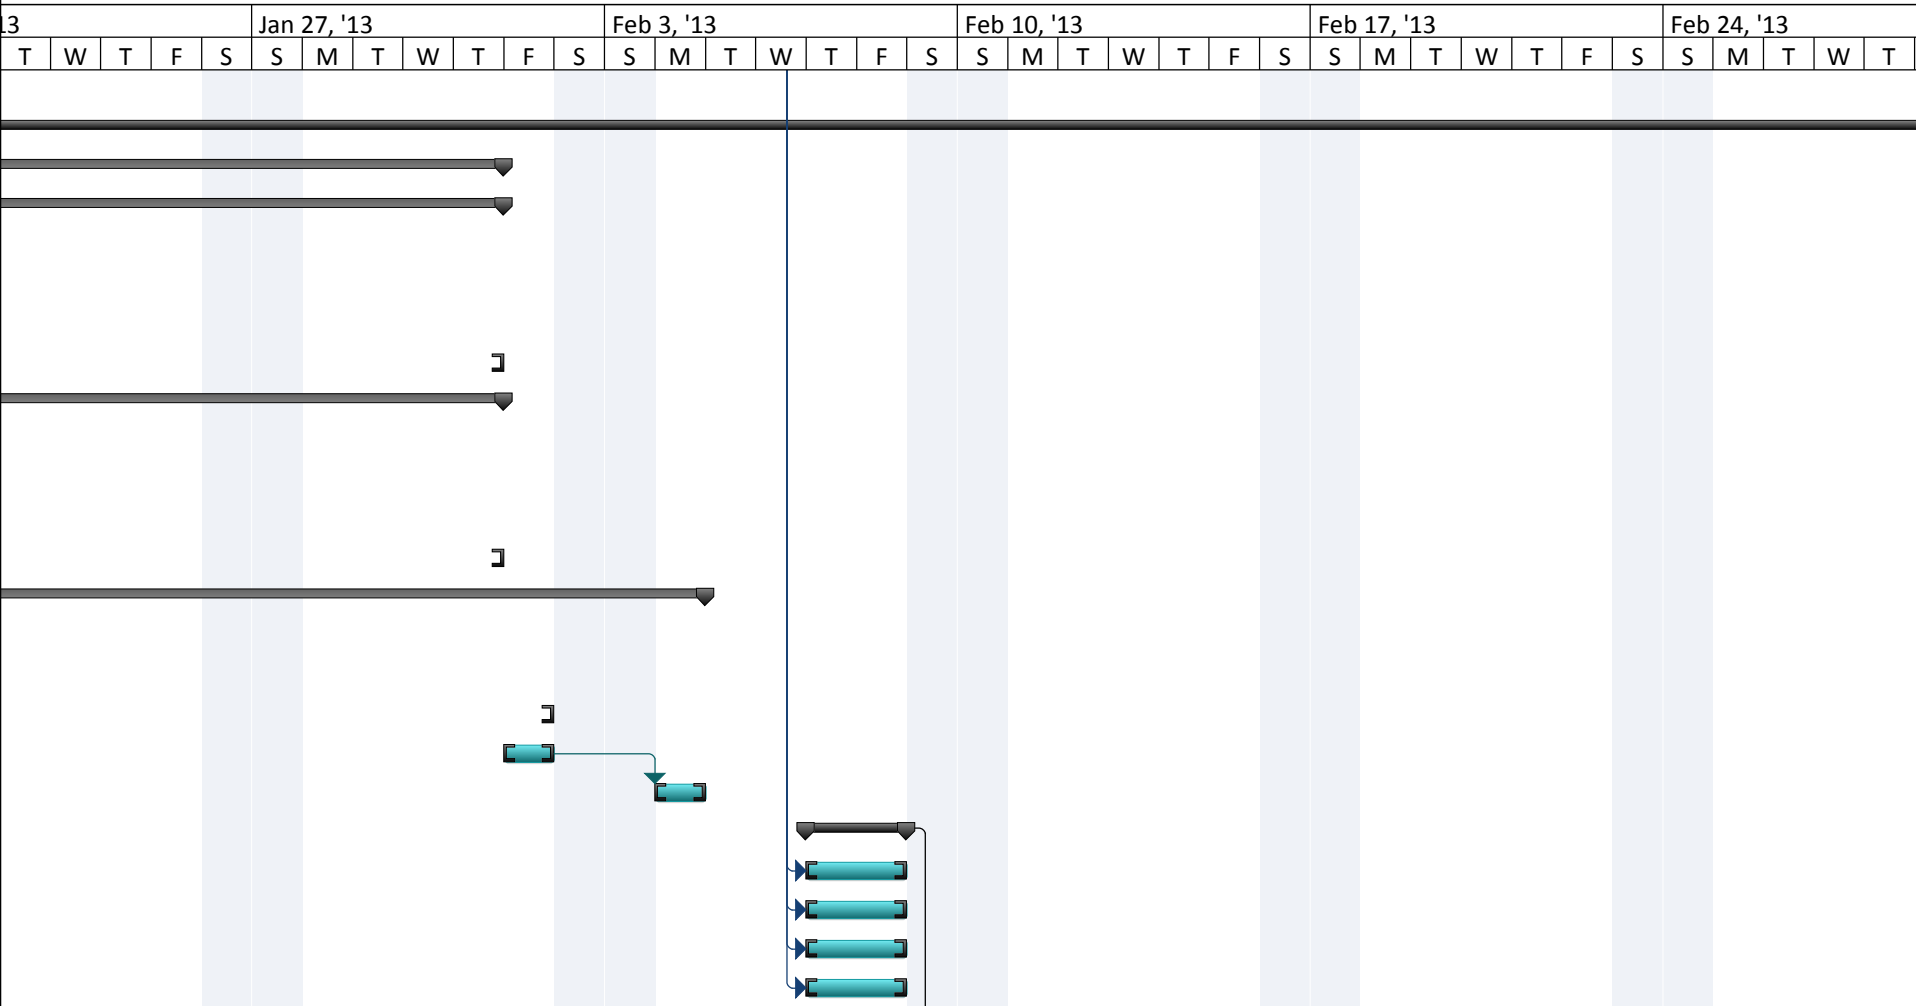

Project: Malware Protection Ove  
Date: 1/4/13

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	

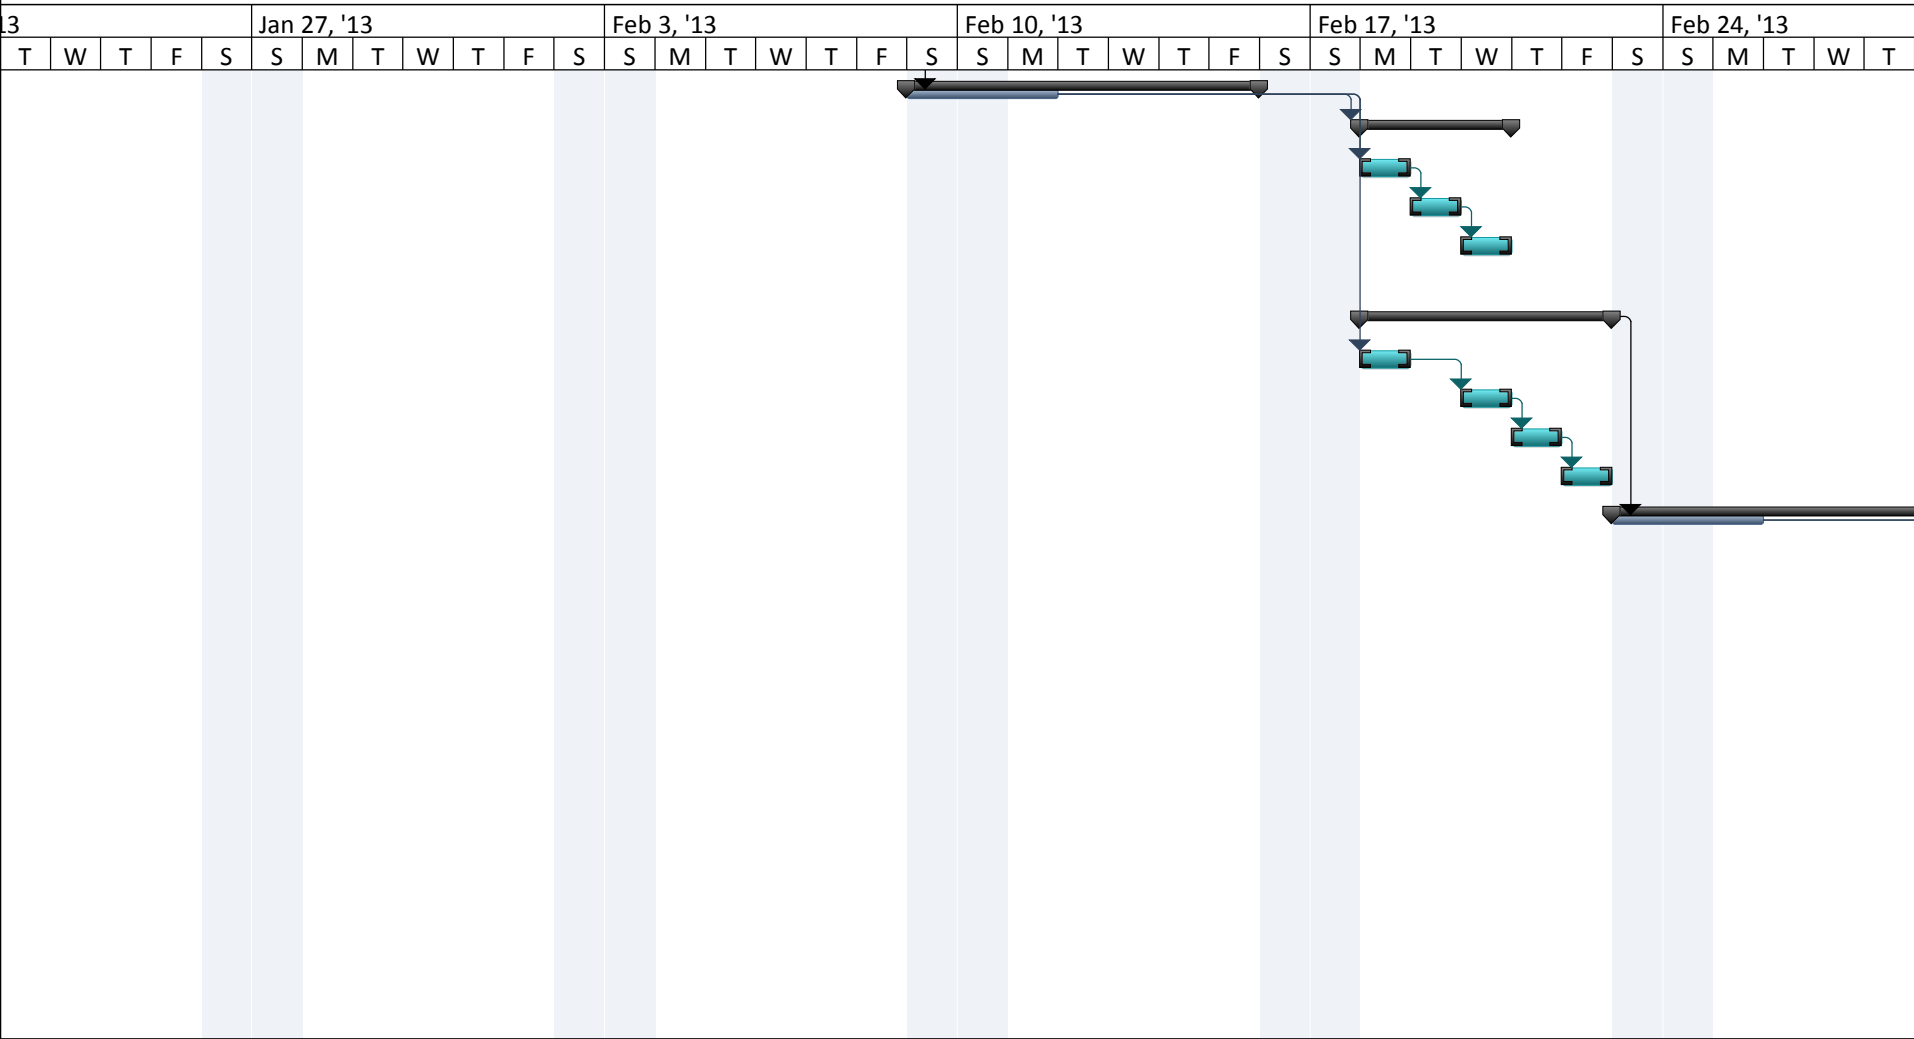

Project: Malware Protection Ove  
Date: 1/4/13


Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	

3					Jan 27, '13					Feb 3, '13					Feb 10, '13					Feb 17, '13					Feb 24, '13												
T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T




Project: Malware Protection Ove  
Date: 1/4/13


Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	

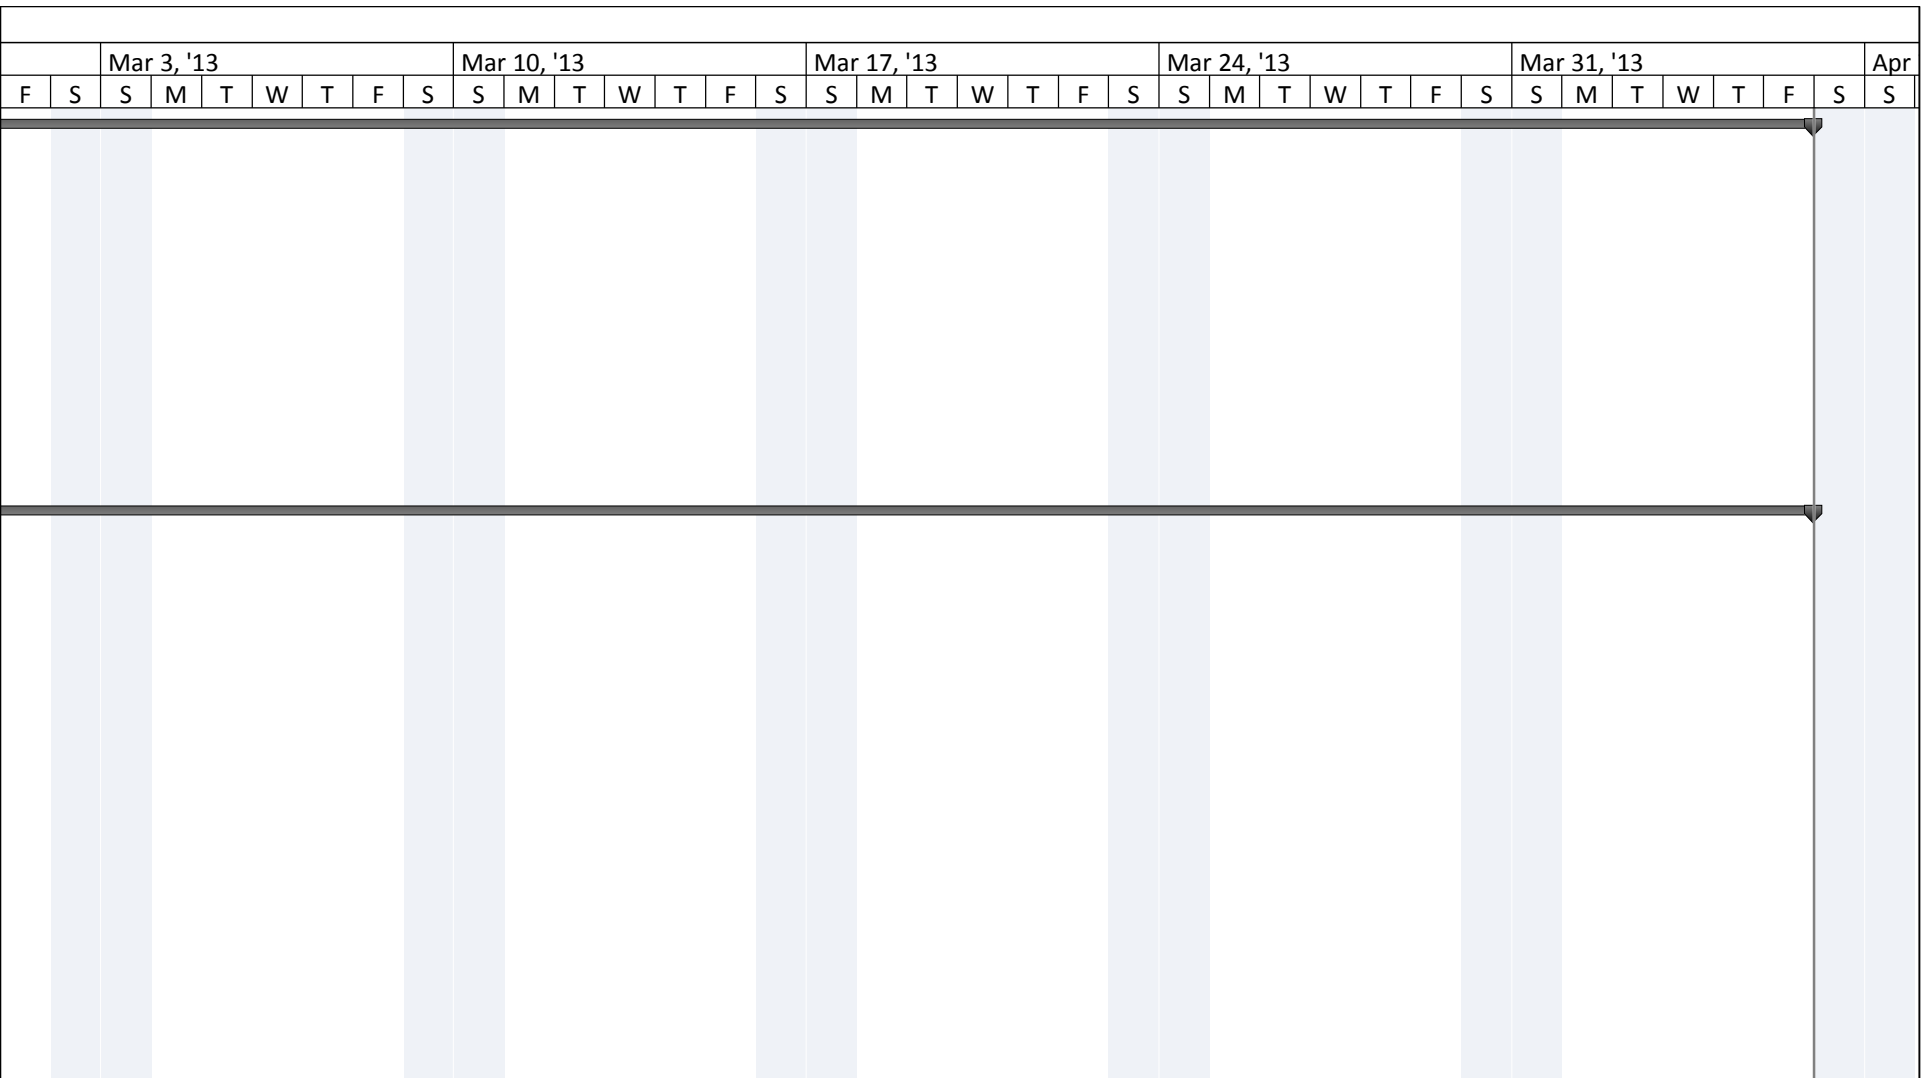


Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	

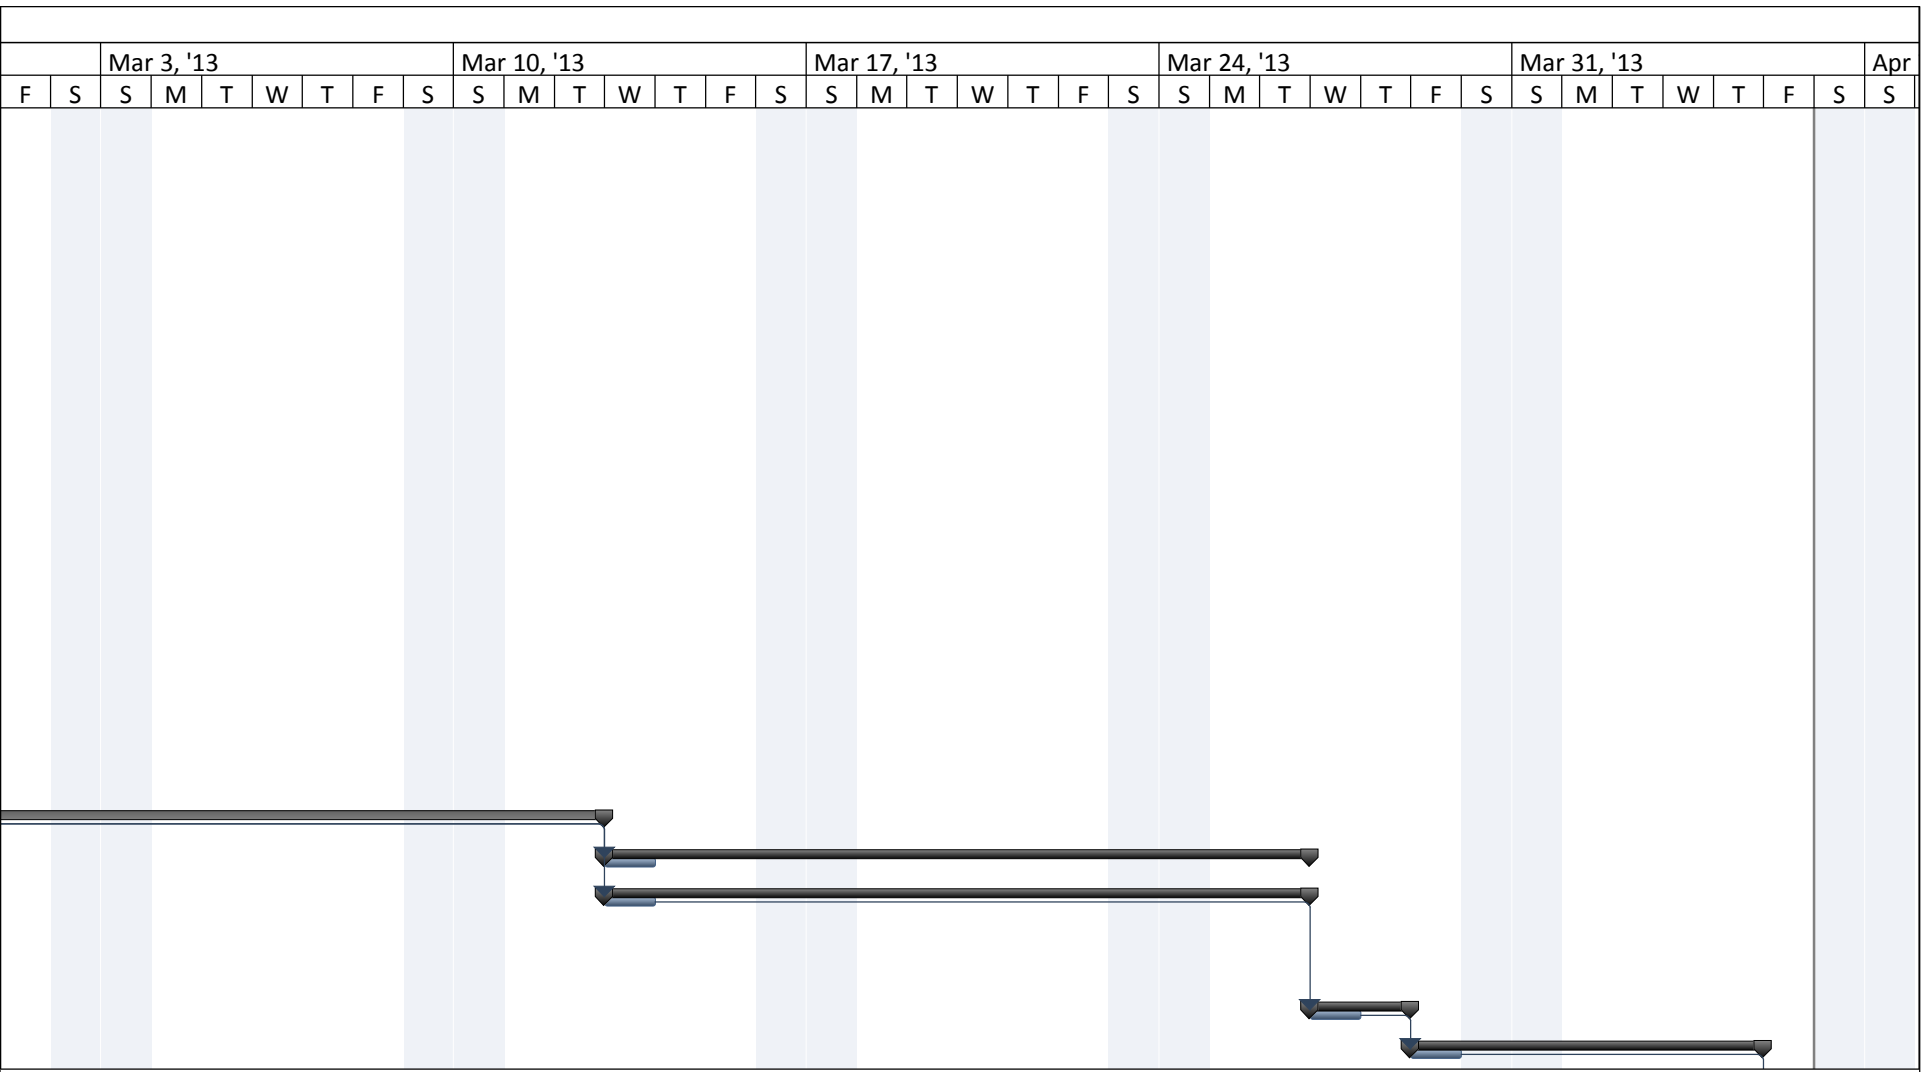

Project: Malware Protection Overdue Date: 1/4/13	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	

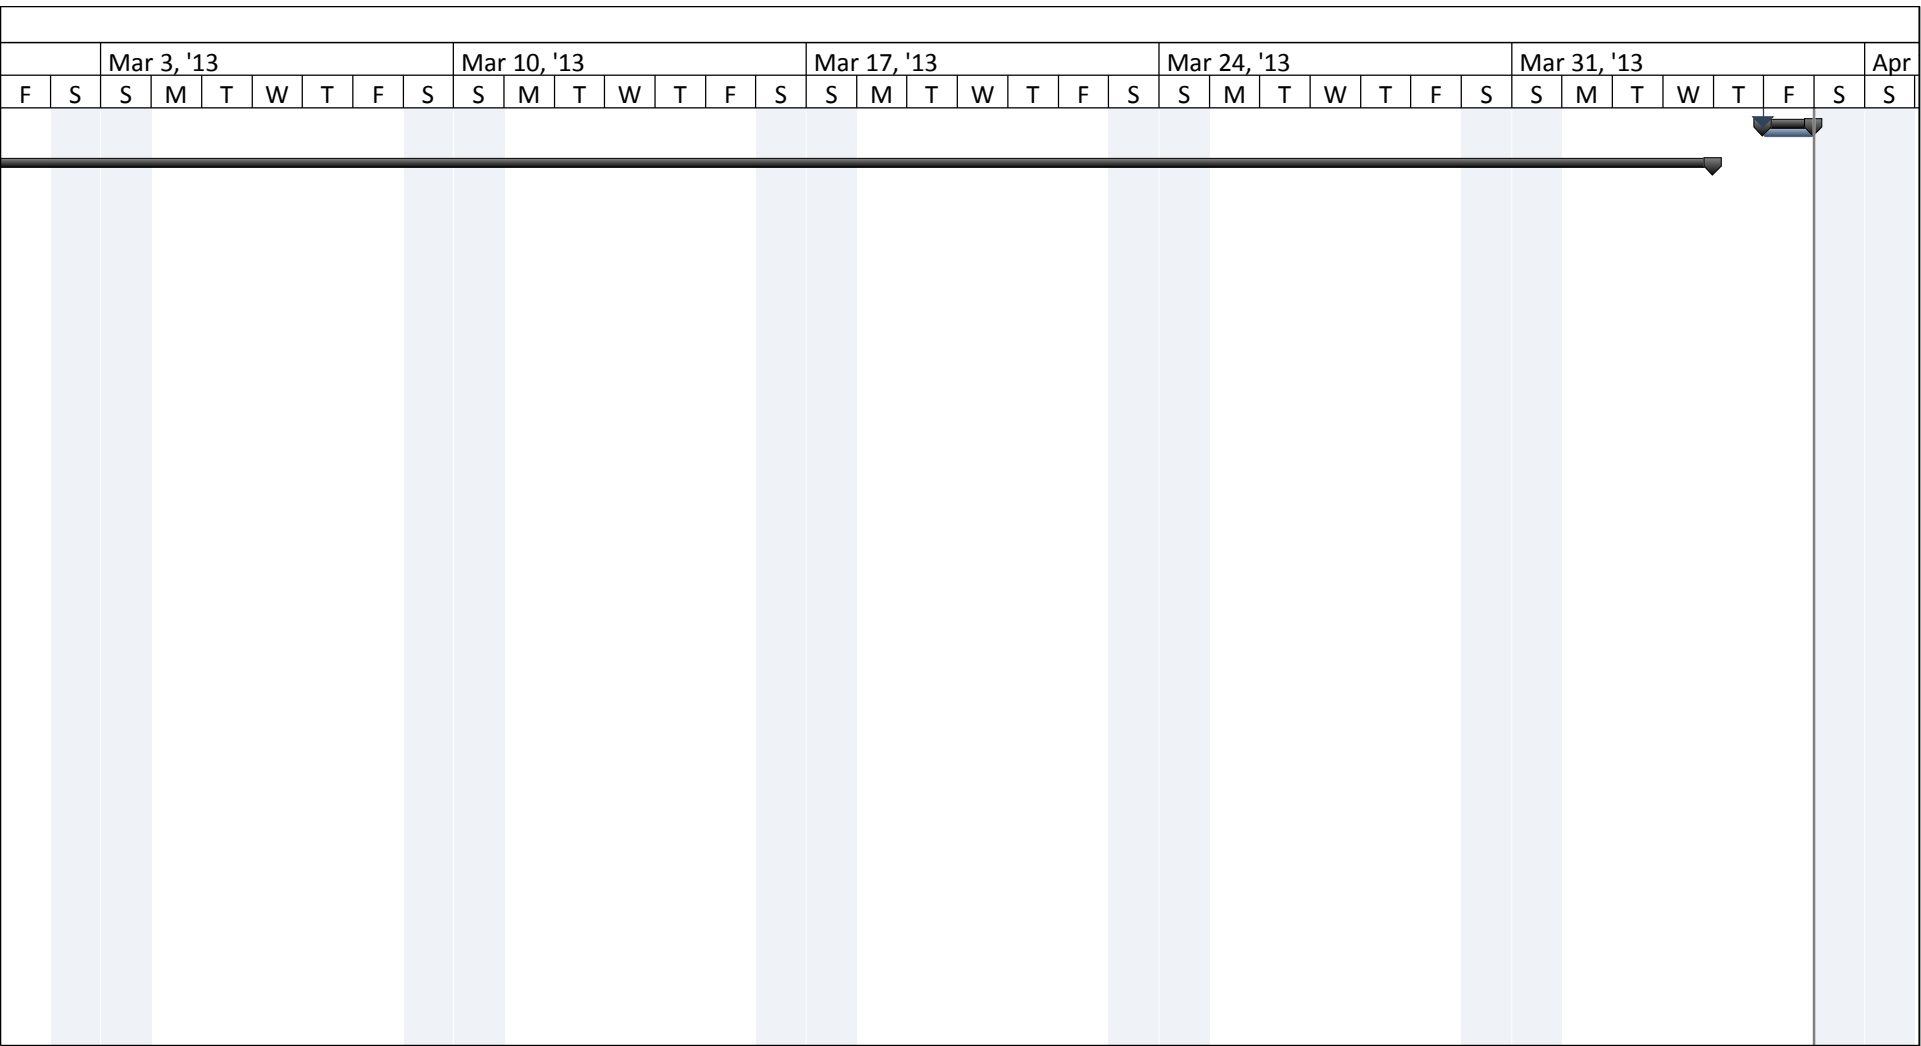


Project: Malware Protection Ove Date: 1/4/13	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	

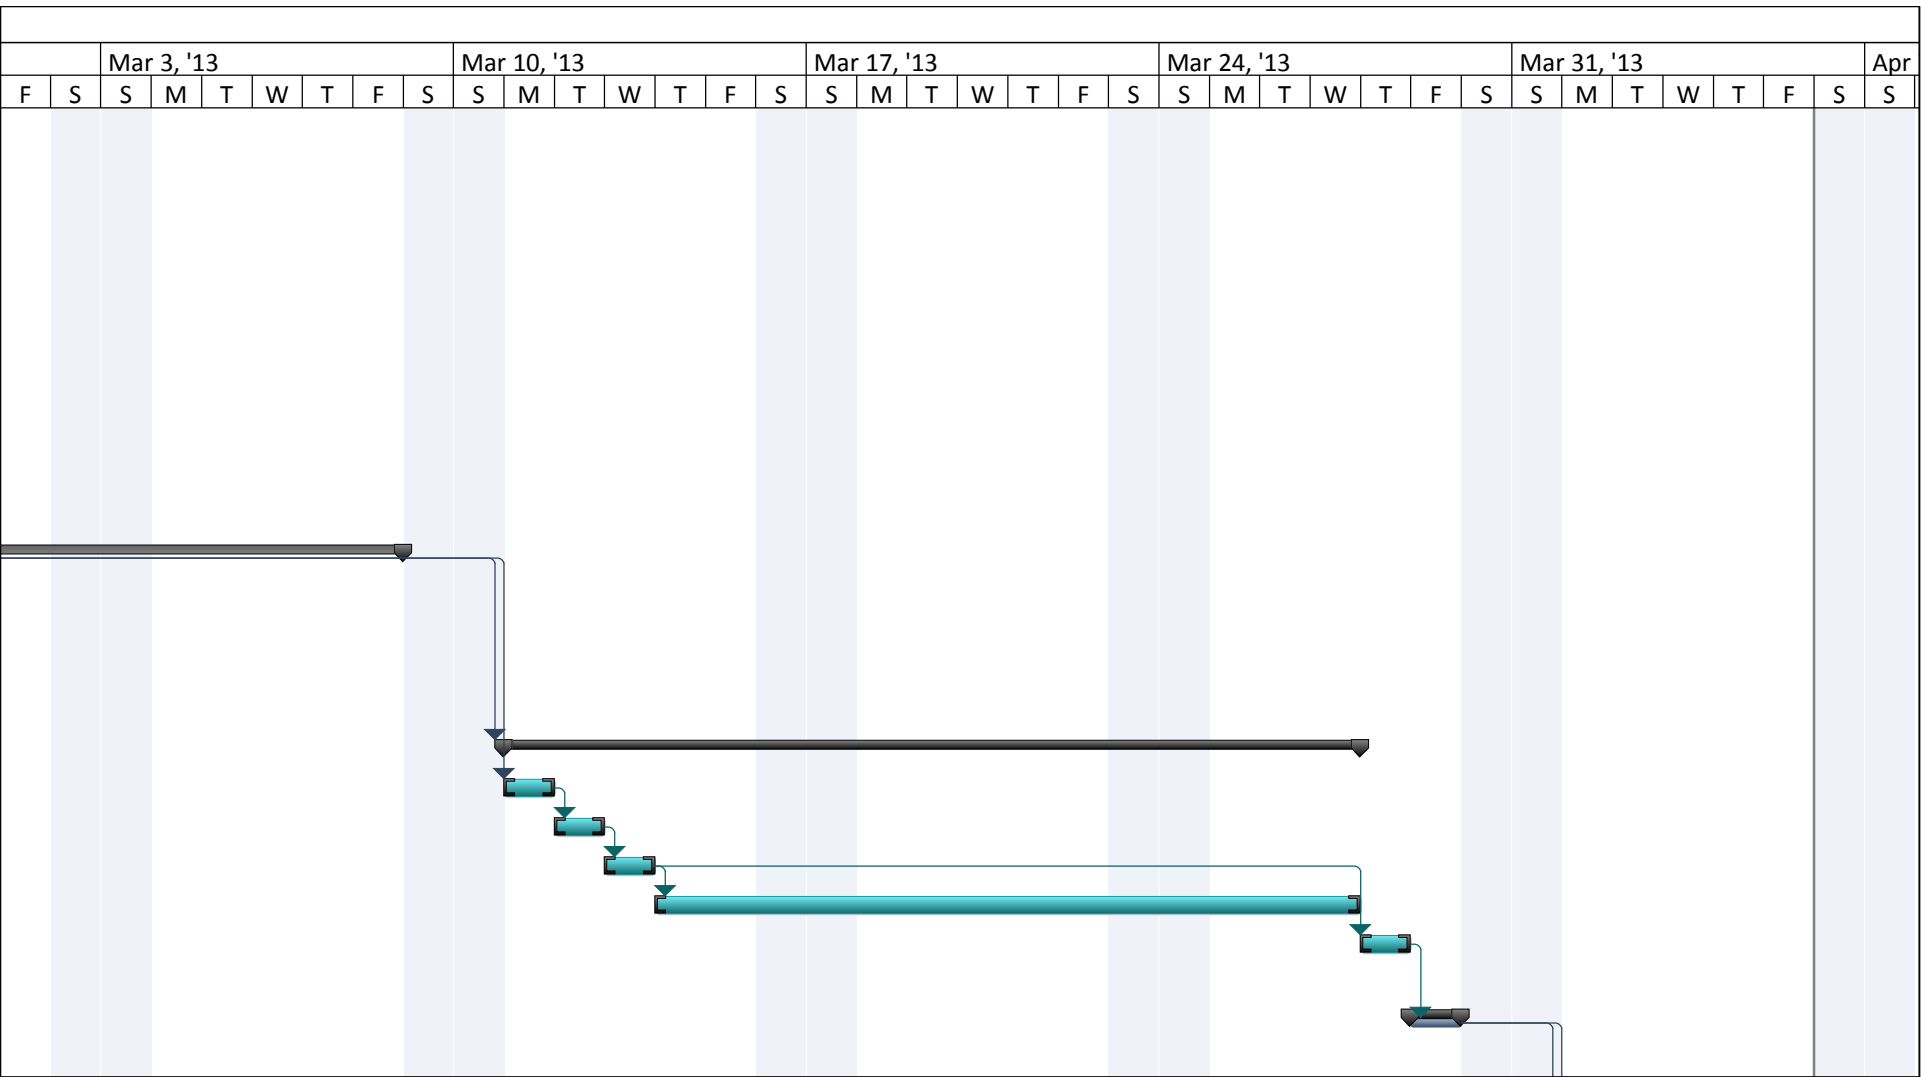

Project: Malware Protection Ove  
Date: 1/4/13

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	



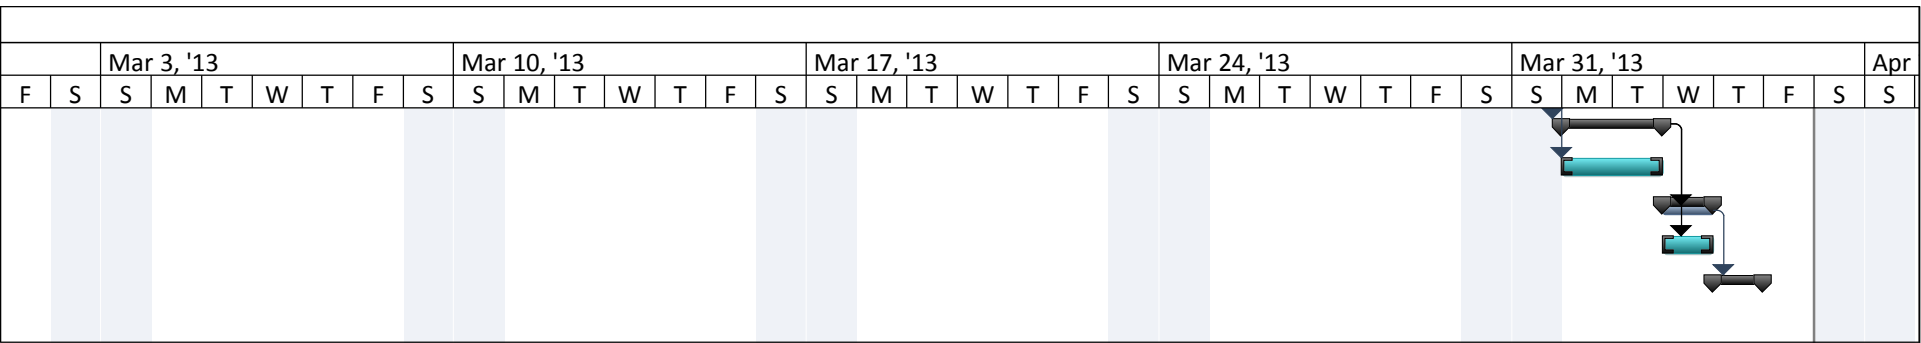

Project: Malware Protection Ove  
Date: 1/4/13

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	
