

ID	% Complete	Task Name	Duration	Start	Finish	Predecessors	Nov 4, '12							Nov 11,		
							S	S	M	T	W	T	F	S	S	M
							1	55%	Malware Protection Overhaul Project	162 days?	11/5/12	6/18/13				
2	100%	Planning	1 day	11/5/12	11/5/12											
6	100%	Communications	1 day?	11/14/12	11/14/12											
10	100%	Vendor Selection	126 days	11/14/12	5/8/13											
11	100%	Sophos Evaluation	47 days	11/28/12	1/31/13											
16	100%	ESET Evaluation (v5.0 - Jan 2013)	42 days	12/5/12	1/31/13											
21	100%	System Center 2012 (Forefront) Evaluation	57 days	11/14/12	1/31/13											
25	100%	ESET Evaluation (v5.0 - Jan 2013)	1 day	11/14/12	11/14/12											
29	100%	Vendor Demo	67 days	11/14/12	2/14/13											
34	100%	Analyze Recommendation and Solution	70 days	11/14/12	2/19/13											
40	100%	Sponsor approval	5 days	2/19/13	2/26/13	34										
41	100%	Approval from sponsor	1 day	5/8/13	5/8/13											
42	50%	McAfee License	126 days?	11/14/12	5/8/13											
43	100%	Understand current McAfee license constraints	1 day	11/14/12	11/14/12											
44	50%	Understand what the license needs are	1 day	5/8/13	5/8/13											
45	0%	Adjust McAfee license based on new requirements	1 day?	2/27/13	2/27/13	40										
46	0%	Documentation and communication	1 day?	5/9/13	5/9/13	41										
47	0%	Helpdesk (awareness only)	1 day?	5/9/13	5/9/13											
48	0%	DITR (awareness only)	1 day?	5/9/13	5/9/13											
49	0%	ITLEADERS (awareness and preparing for early adaptors only)	1 day?	5/9/13	5/9/13											
50	0%	Full Integration Testing	10 days	2/26/13	3/12/13											
51	0%	Setup	2 days	5/9/13	5/10/13											

Project: Malware Protection Overhaul Date: 5/9/13	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	

ID	% Comple	Task Name	Duration	Start	Finish	Predecessors														
							Nov 4, '12							Nov 11,						
							S	S	M	T	W	T	F	S	S	M				
52	0%	Determine pilot rollout team	1 day?	5/9/13	5/9/13															
53	0%	Determine timelines	1 day?	5/9/13	5/9/13	41														
54	0%	determine pilot rollout strategy	1 day?	5/9/13	5/9/13	41														
55	0%	Pilot rollout (STAKEHOLDERS)	10 days	5/10/13	5/23/13	54														
56	0%	Collect feedback	1 day?	5/24/13	5/24/13	55														
57	0%	Checkpoint: Present feedback to Sponsor	3 days	5/27/13	5/29/13	56														
58	0%	Procurement	17 days?	5/9/13	5/31/13															
59	0%	Negotiate pricing	1 day?	5/9/13	5/9/13	41														
60	0%	Contract agreement and signature	1 day?	5/30/13	5/30/13	57														
61	0%	Purchase	1 day?	5/31/13	5/31/13	60														
62	0%	Reminder: adjust McAfee contract	1 day?	5/31/13	5/31/13	60														
63	50%	communicate new solution deployment and maintenance to impacted stakeholders	142.1 days?	11/14/12	5/31/13															
64	100%	identify current teams impacted by this change & communicate to them new product and new maintenance structure	1 day	11/14/12	5/31/13	60														
65	0%	planning meeting																		
66	0%	Setup for distribution	1 day?	5/31/13	6/3/13															
67	0%	Assist teams in setting up for distribution	1 day?	5/31/13	6/3/13	64														
68	0%	General Communications	8.9 days?	6/3/13	6/13/13	66														
69	0%	to community	1 day?	6/3/13	6/4/13															
70	0%	IT Partners presentation	1 day?	6/13/13	6/13/13															
71	0%	Prep Helpdesk for full rollout support	1 day?	6/14/13	6/14/13	68														
72	0%	any additional training/documentation	1 day?	6/14/13	6/14/13															
73	0%	Full rollout (COMMUNITY)	1 day?	6/17/13	6/17/13	72														

Project: Malware Protection Over Date: 5/9/13


Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	

ID	% Complete	Task Name	Duration	Start	Finish	Predecessors														
							Nov 4, '12										Nov 11,			
							S	S	M	T	W	T	F	S	S	M				
74	0%	Provide software to SWRT for distribution	1 day?	6/17/13	6/17/13	72														
75	0%	Project Wrapup	1 day?	6/18/13	6/18/13	74														
76	0%	closeout project	1 day?	6/18/13	6/18/13															
77	0%	Post project support	0 days	6/17/13	6/17/13	71														

Project: Malware Protection Ove
Date: 5/9/13


Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	

'12 Nov 18, '12 Nov 25, '12 Dec 2, '12 Dec 9, '12 Dec 16, '12 Dec 23, '12

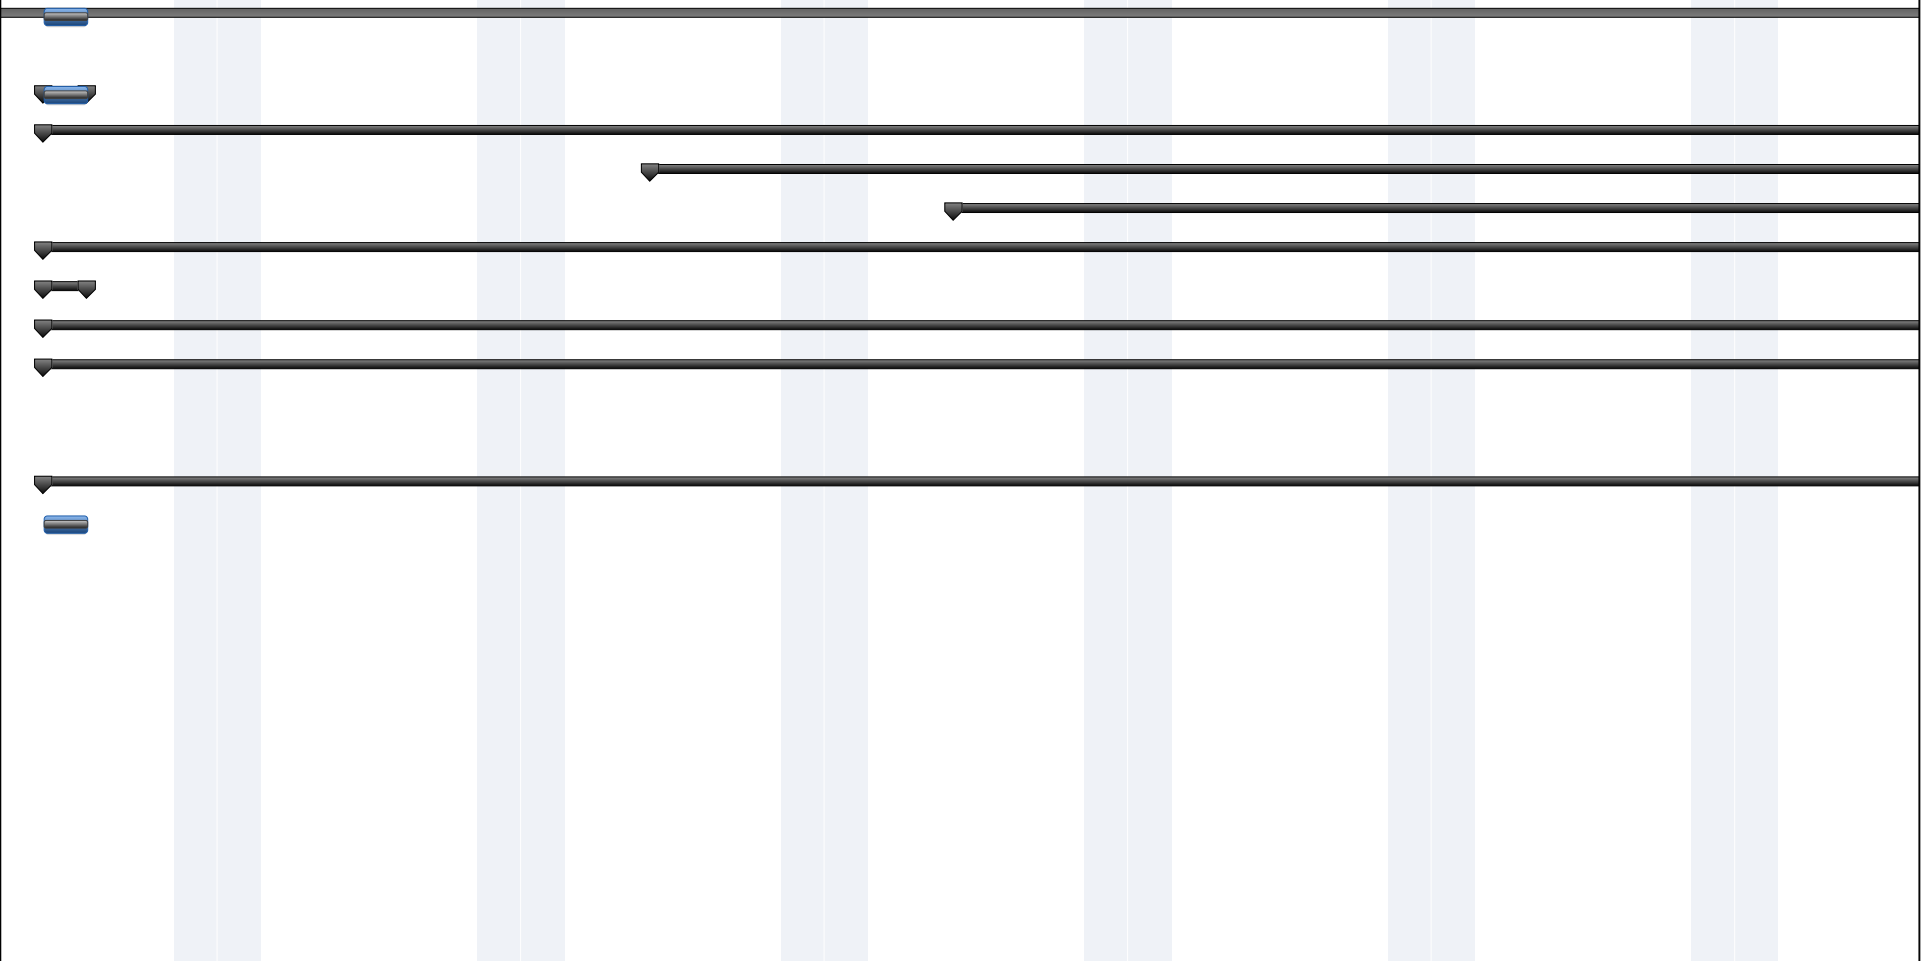

Project: Malware Protection Ove
Date: 5/9/13

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	

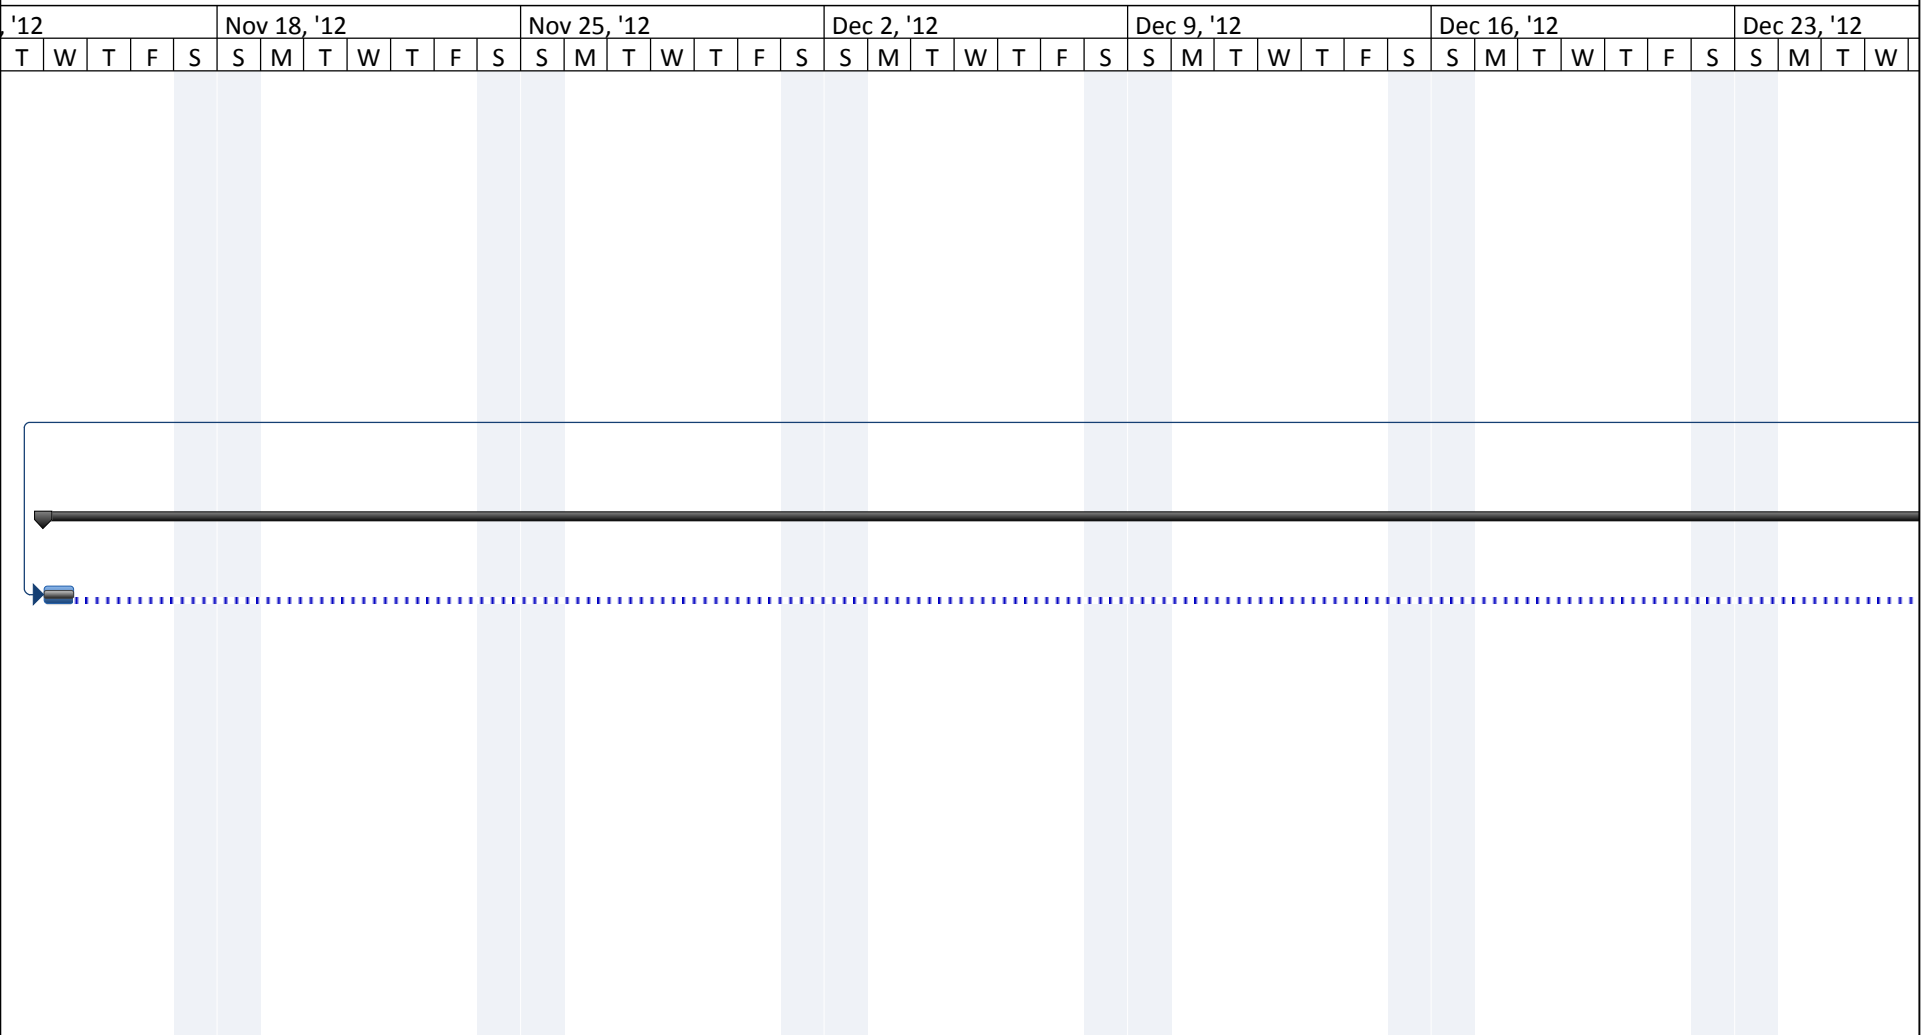

Project: Malware Protection Ove
Date: 5/9/13


Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	

'12					Nov 18, '12					Nov 25, '12					Dec 2, '12					Dec 9, '12					Dec 16, '12					Dec 23, '12													
T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W



Project: Malware Protection Ove
Date: 5/9/13

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	

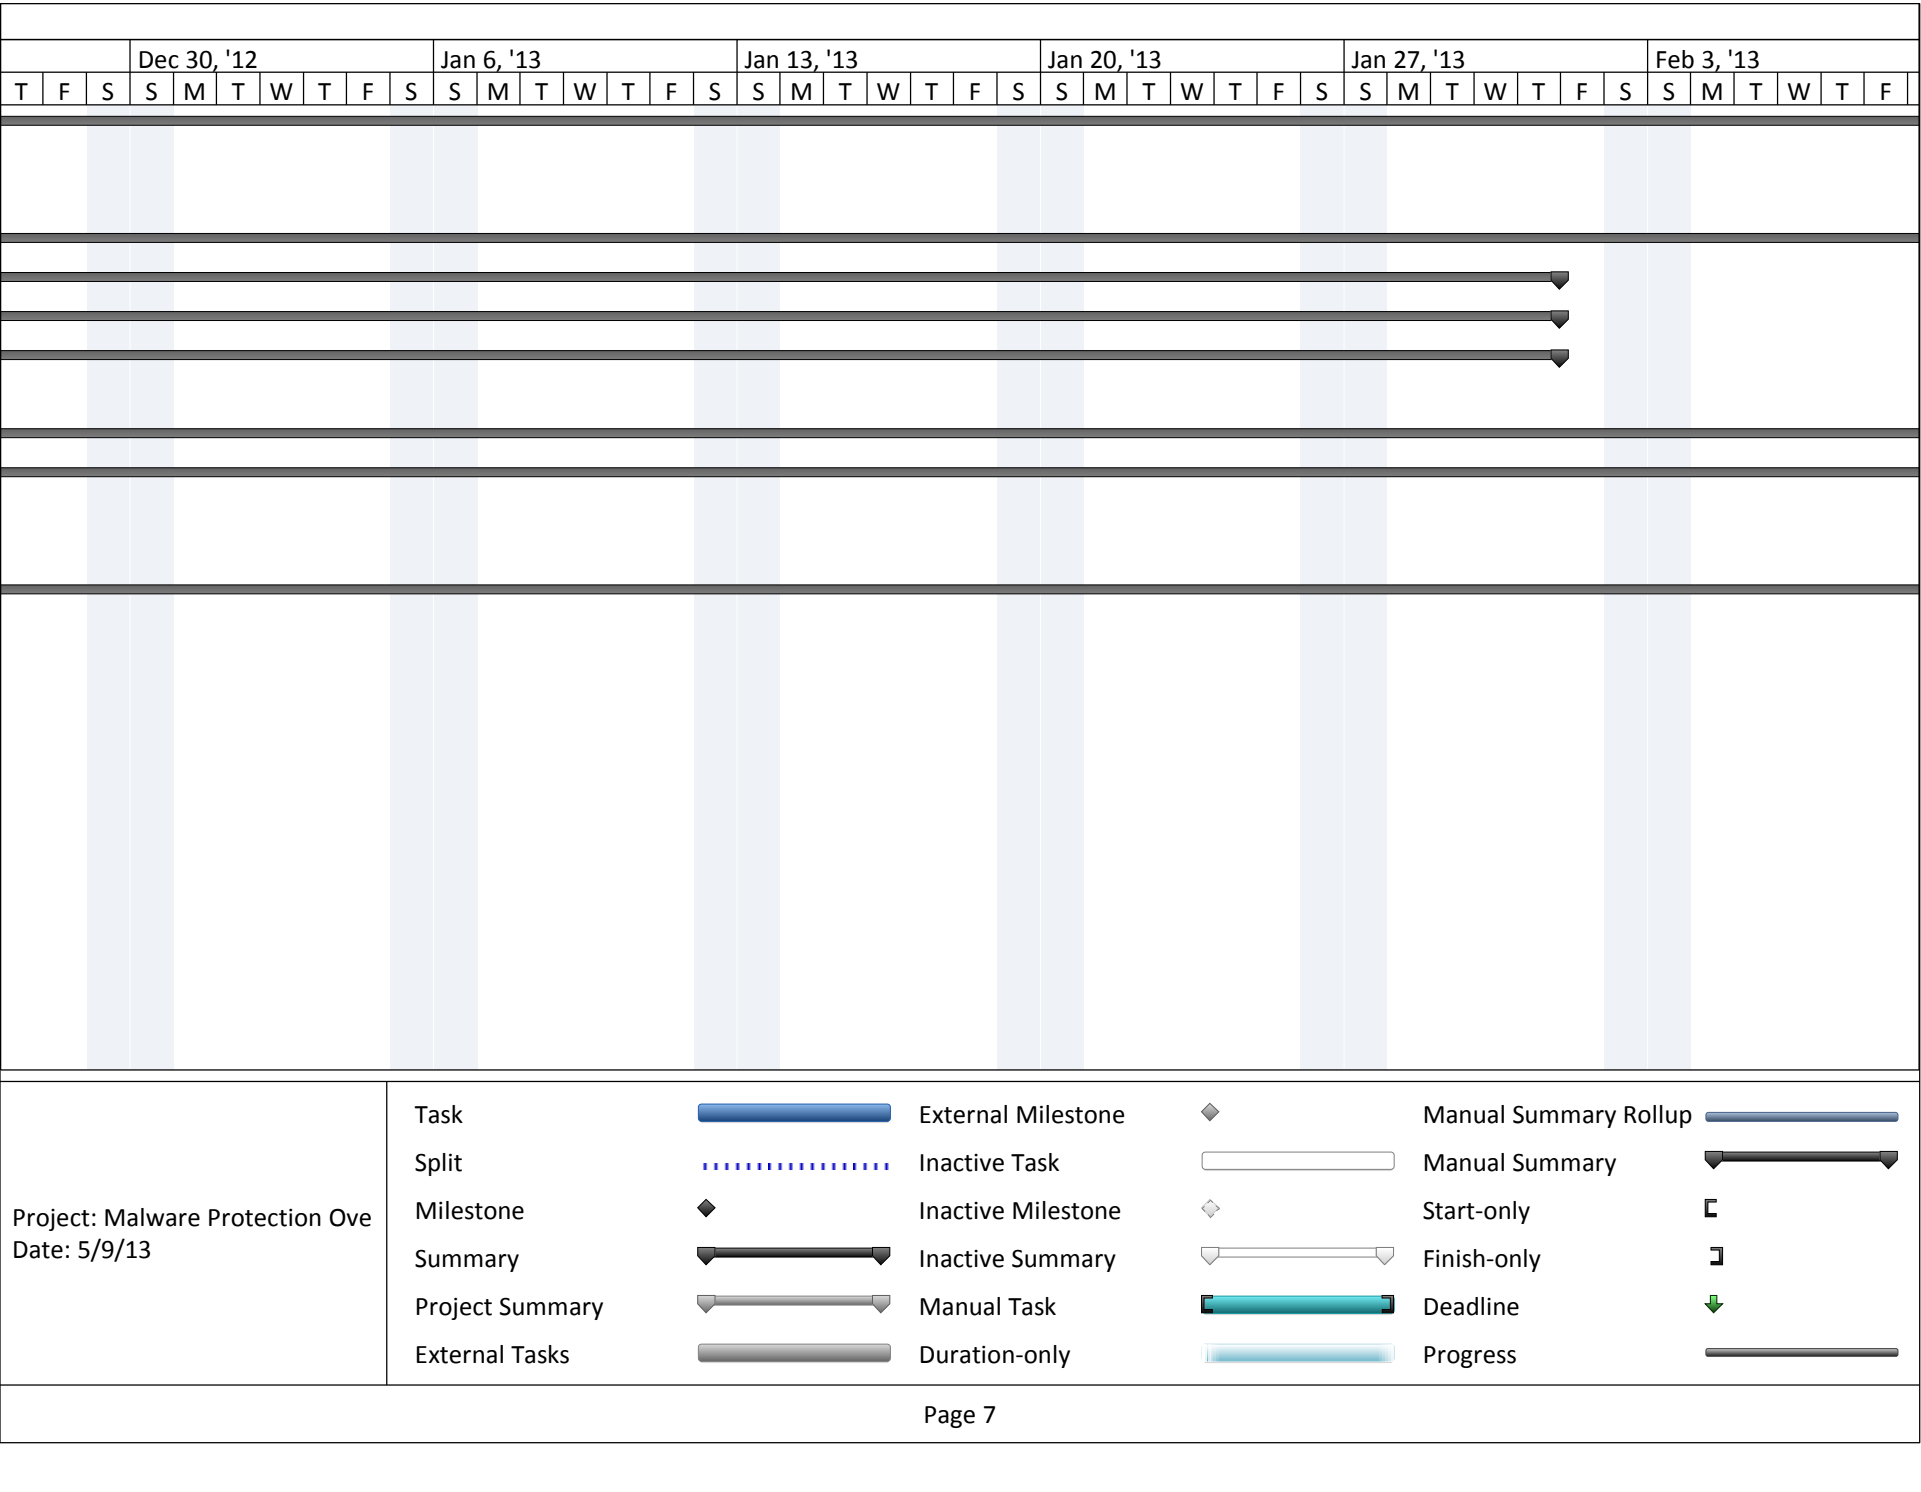

Dec 30, '12

Jan 6, '13


Jan 13, '13

Jan 20, '13

Jan 27, '13


Feb 3, '13

T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F

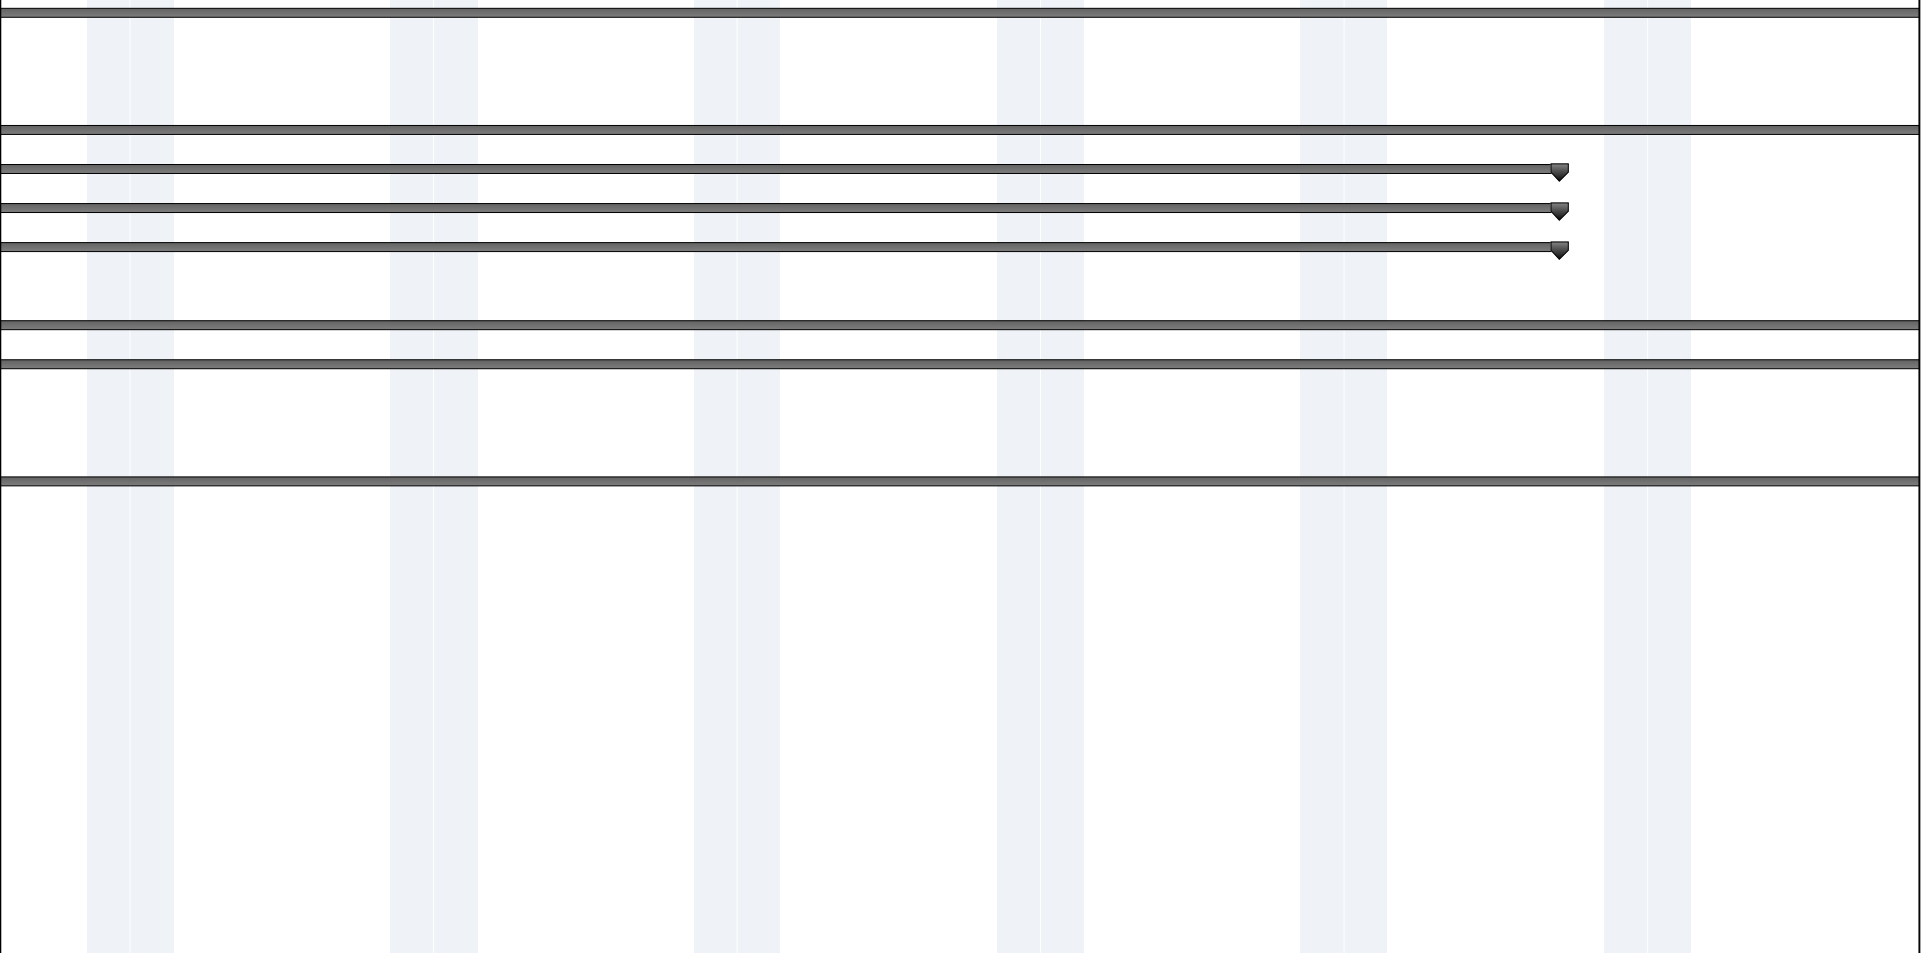

Project: Malware Protection Ove
Date: 5/9/13

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	

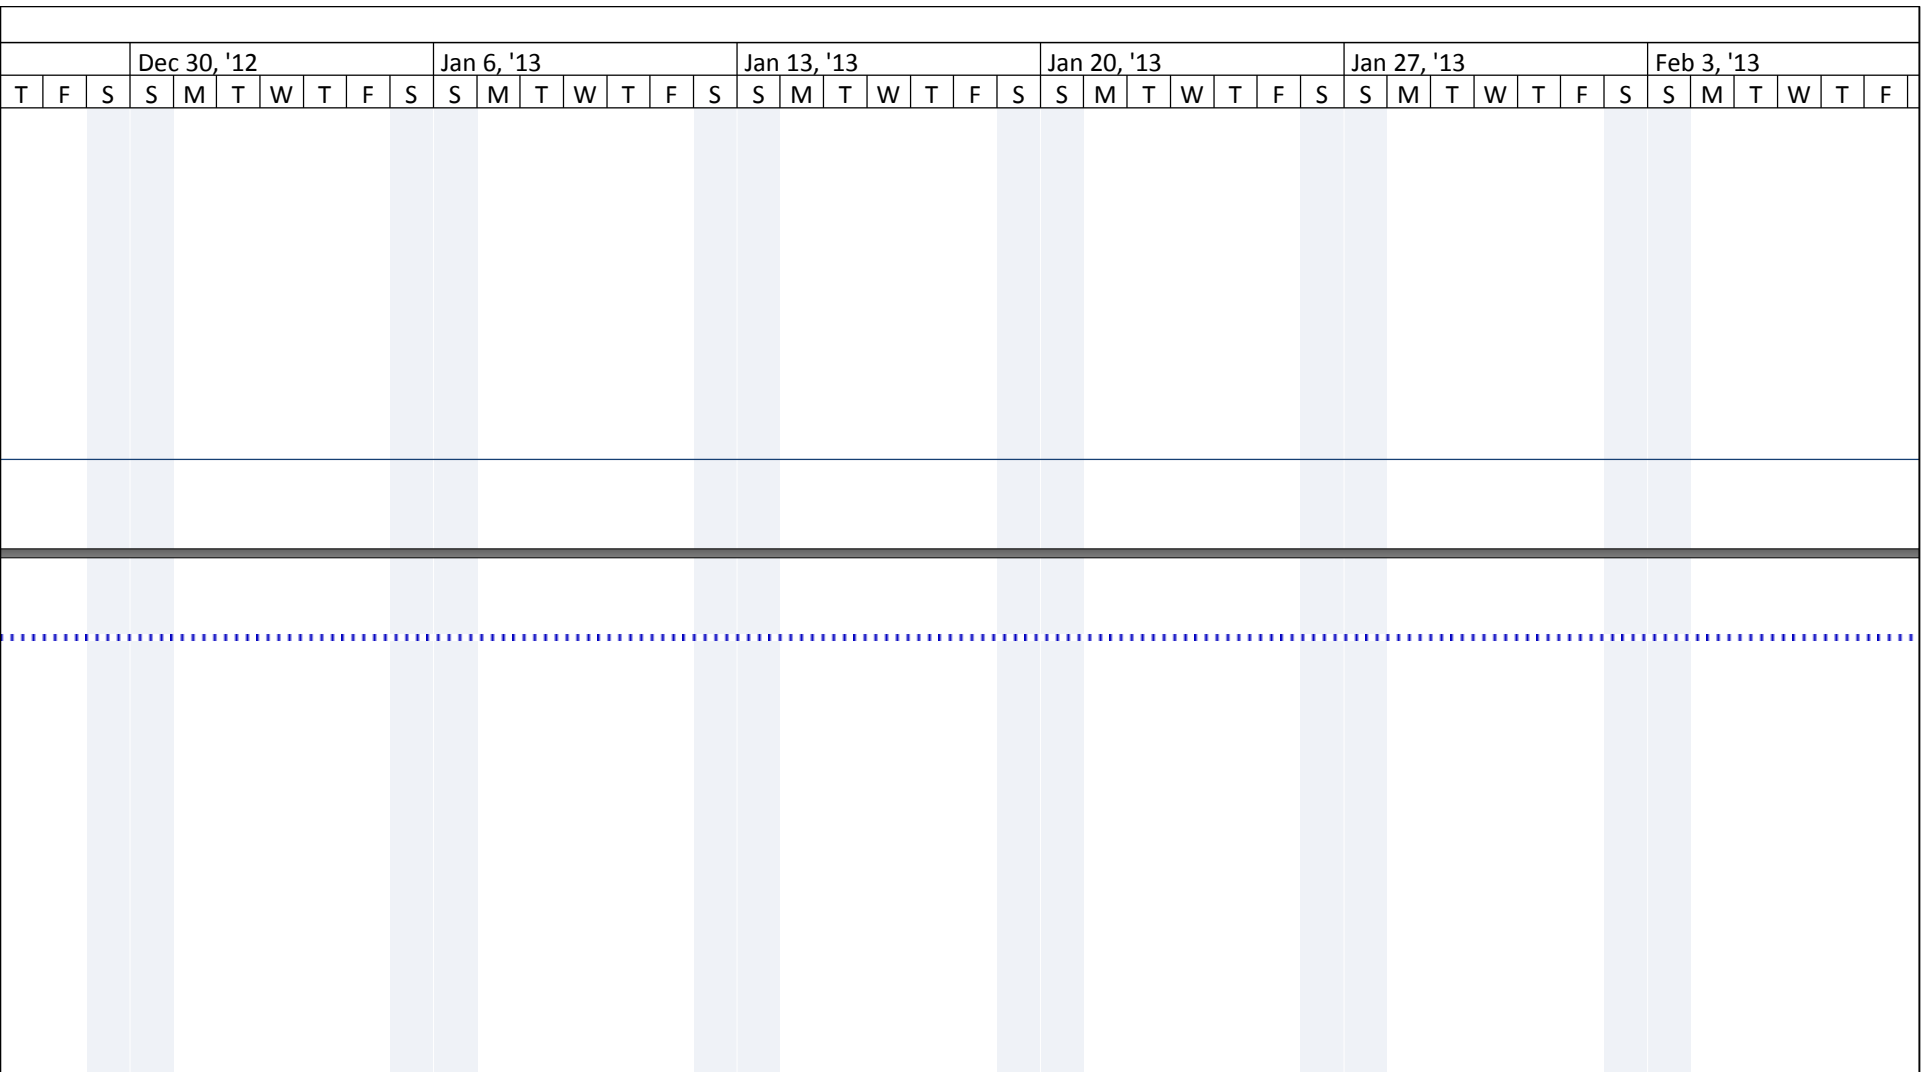

Project: Malware Protection Ove
Date: 5/9/13


Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	


			Dec 30, '12				Jan 6, '13					Jan 13, '13					Jan 20, '13					Jan 27, '13					Feb 3, '13										
T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	



Project: Malware Protection Ove
Date: 5/9/13

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	

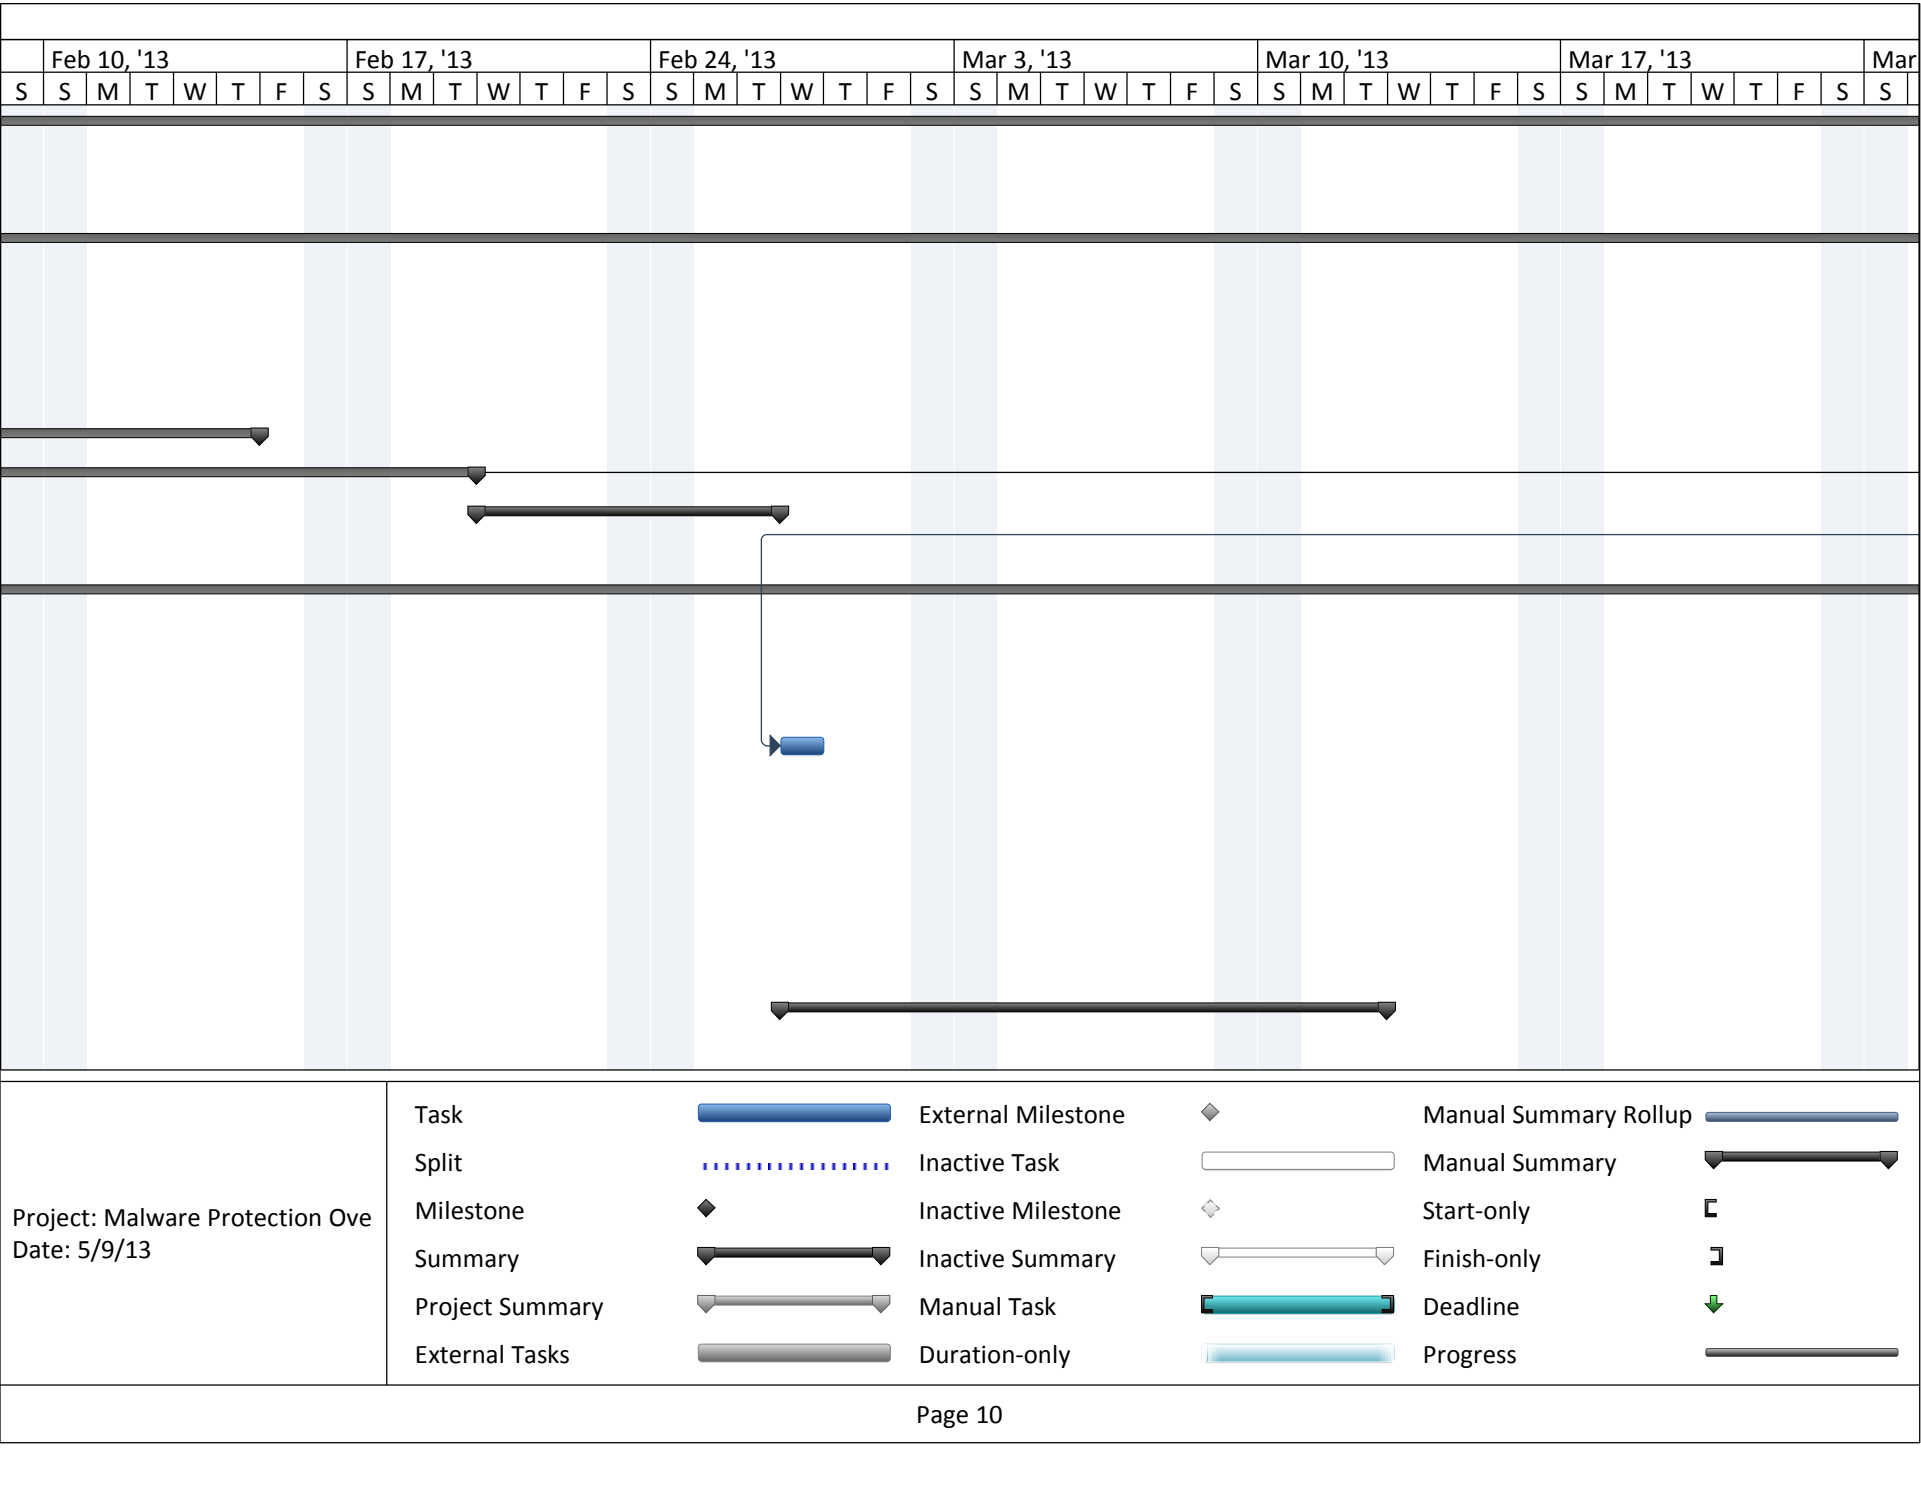

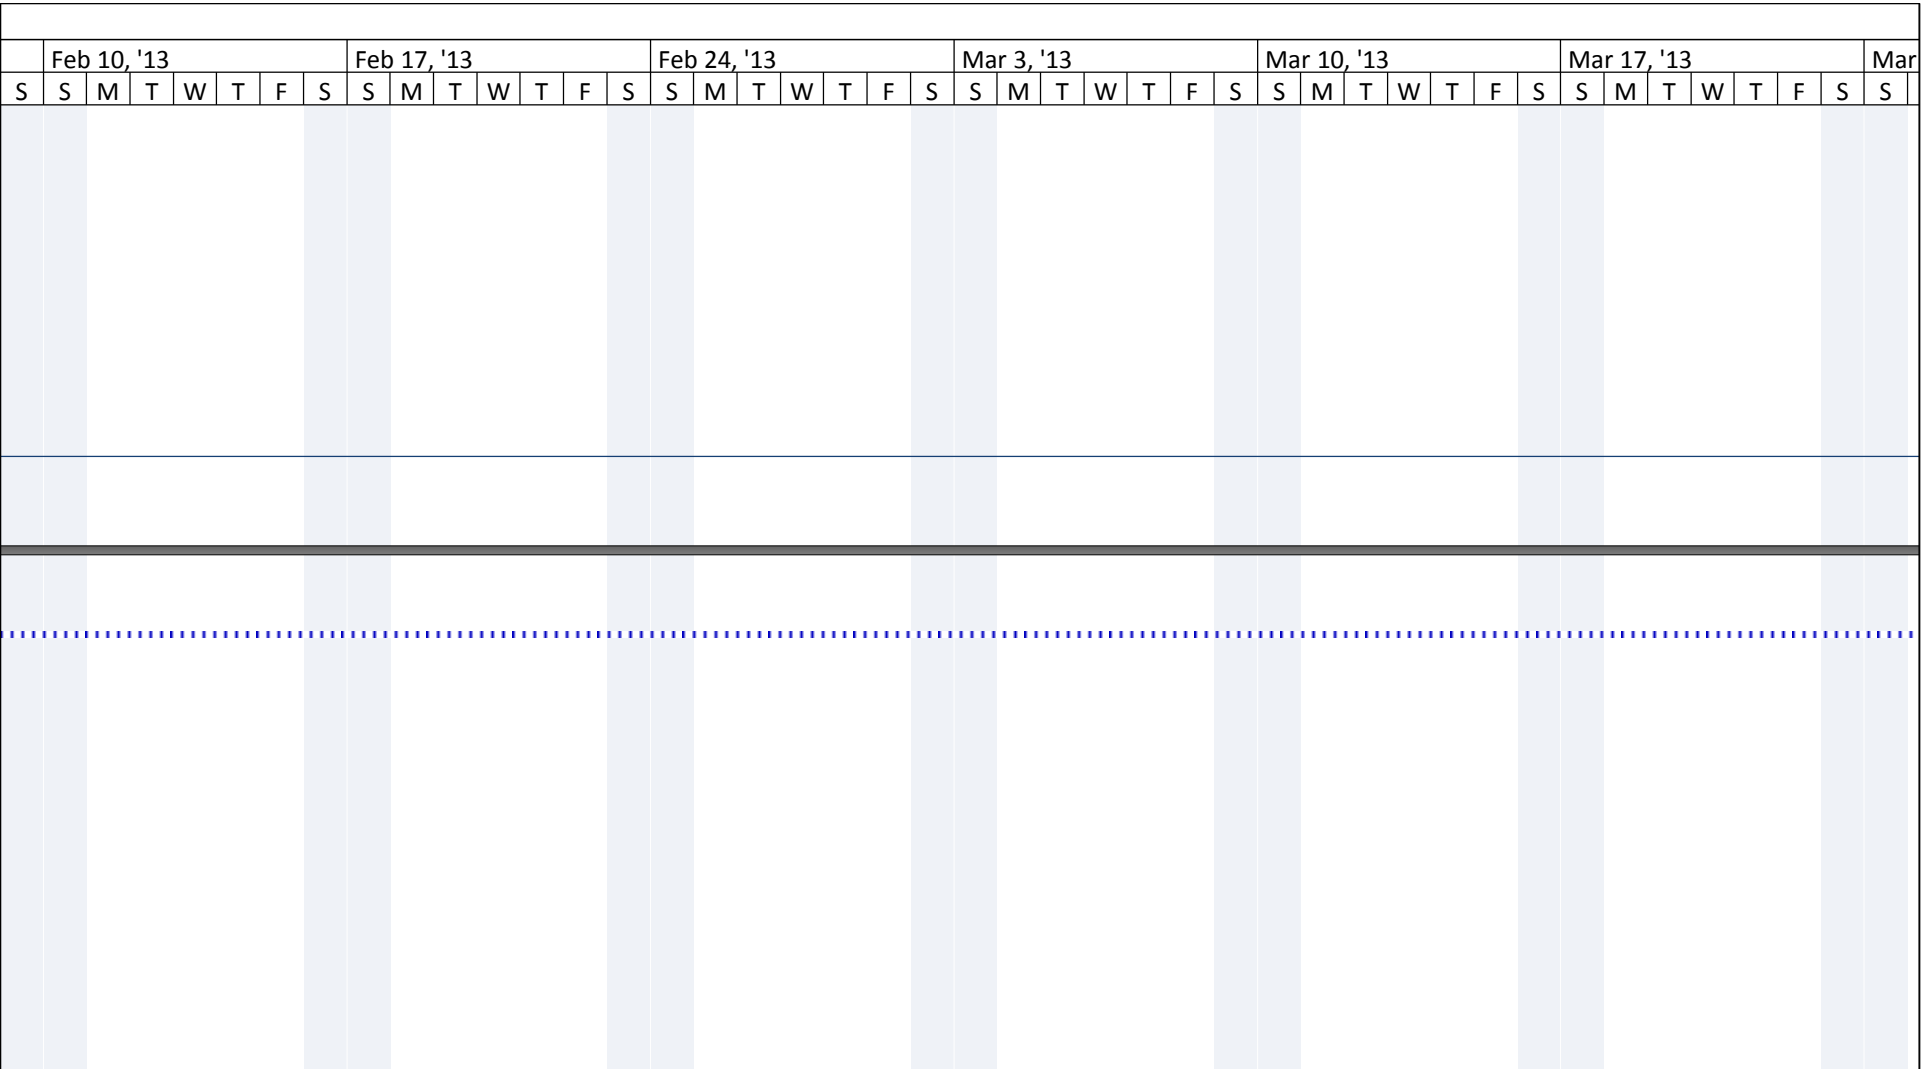

Project: Malware Protection Over
Date: 5/9/13

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	


Feb 10, '13							Feb 17, '13							Feb 24, '13							Mar 3, '13							Mar 10, '13							Mar 17, '13							Mar 24, '13		
S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	S




Project: Malware Protection Ove
Date: 5/9/13

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	

Mar 24, '13					Mar 31, '13					Apr 7, '13					Apr 14, '13					Apr 21, '13					Apr 28, '13					May 5, '13						
M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T

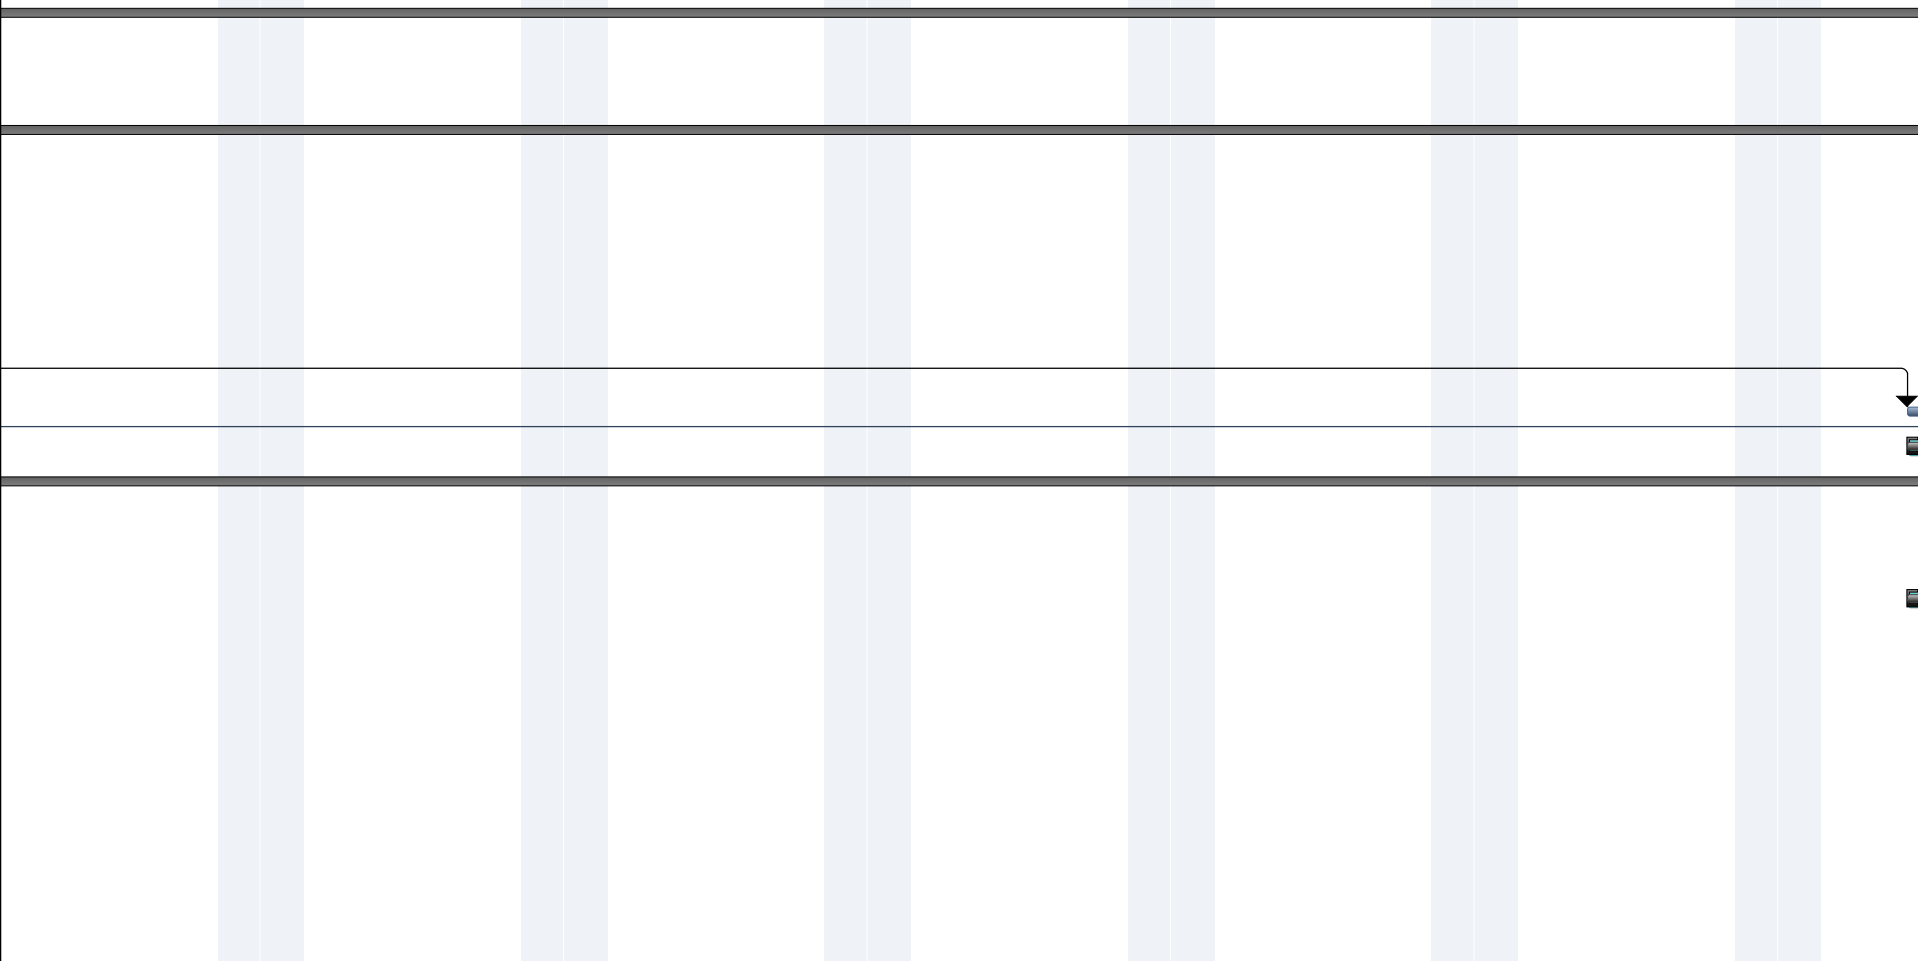

Project: Malware Protection Overdue Date: 5/9/13	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	

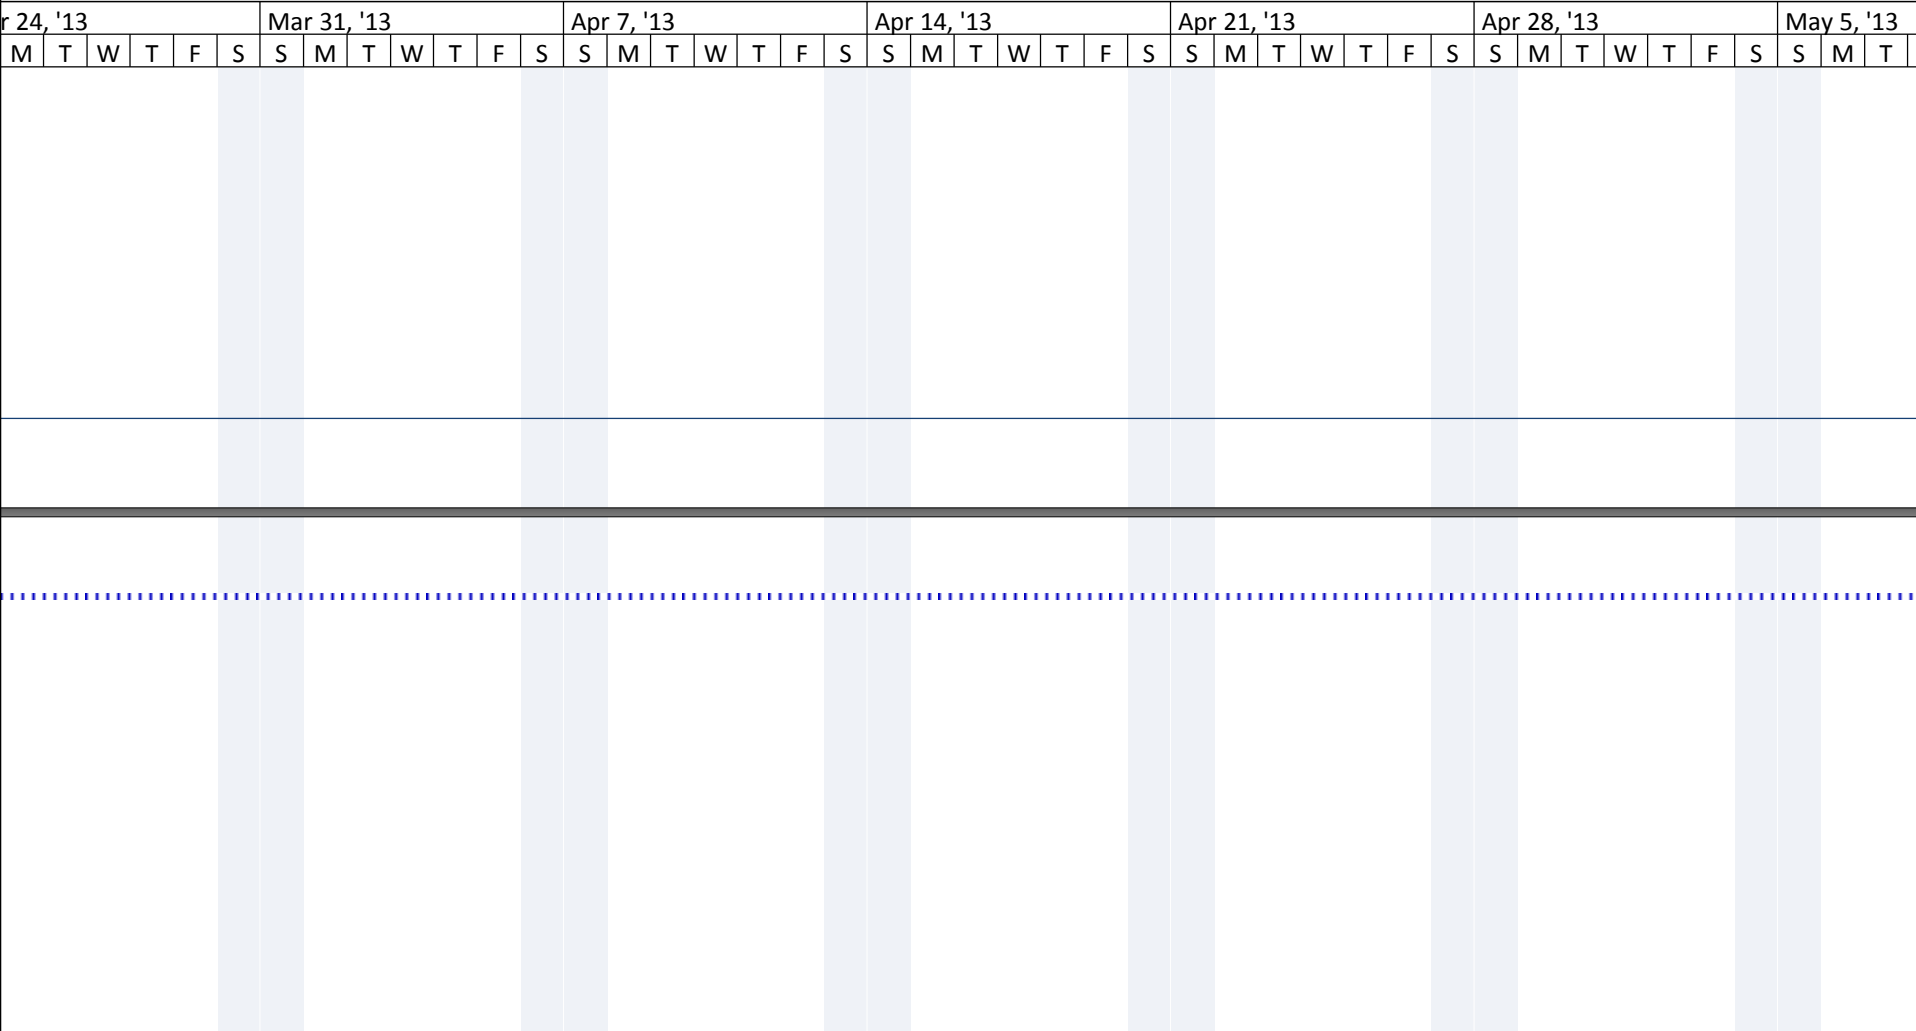

Project: Malware Protection Ove
 Date: 5/9/13


Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	

Mar 24, '13					Mar 31, '13					Apr 7, '13					Apr 14, '13					Apr 21, '13					Apr 28, '13					May 5, '13						
M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T




Project: Malware Protection Ove
Date: 5/9/13


Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	

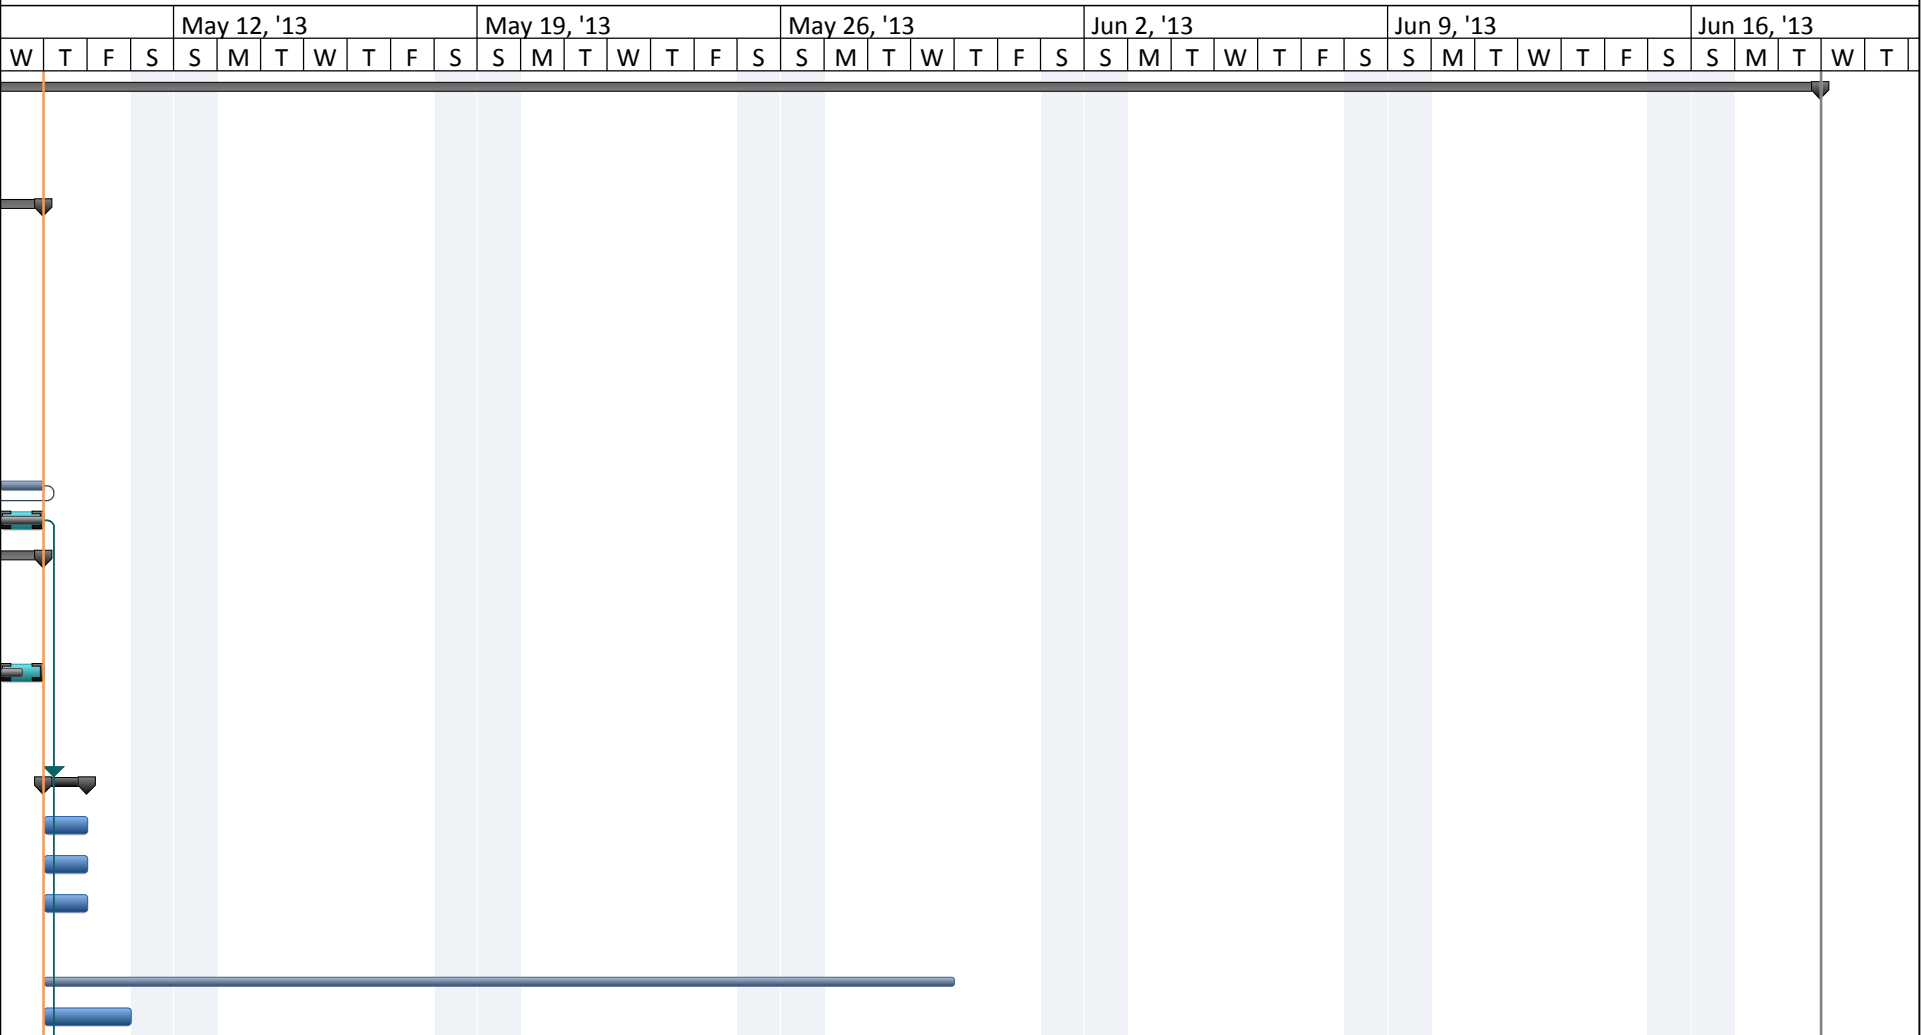

Project: Malware Protection Overdue Date: 5/9/13	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	

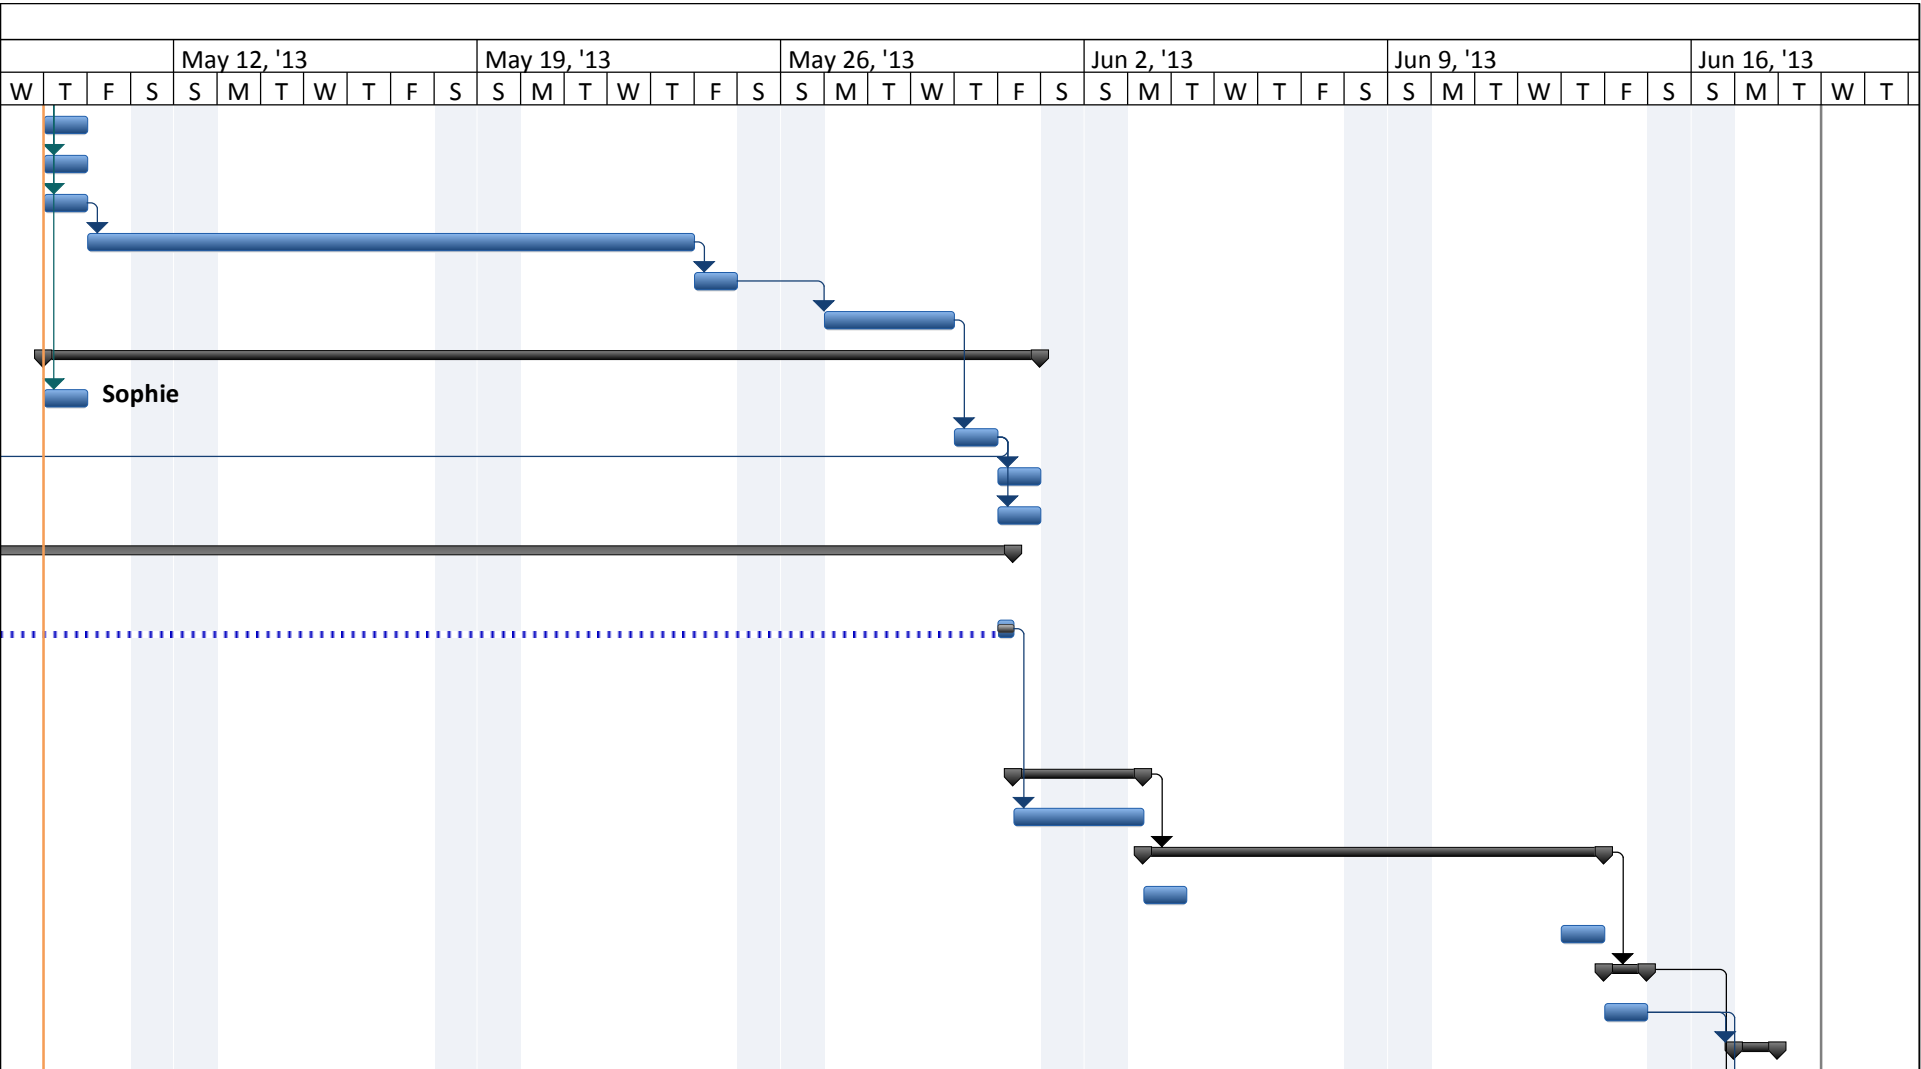

Project: Malware Protection Over Date: 5/9/13	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	

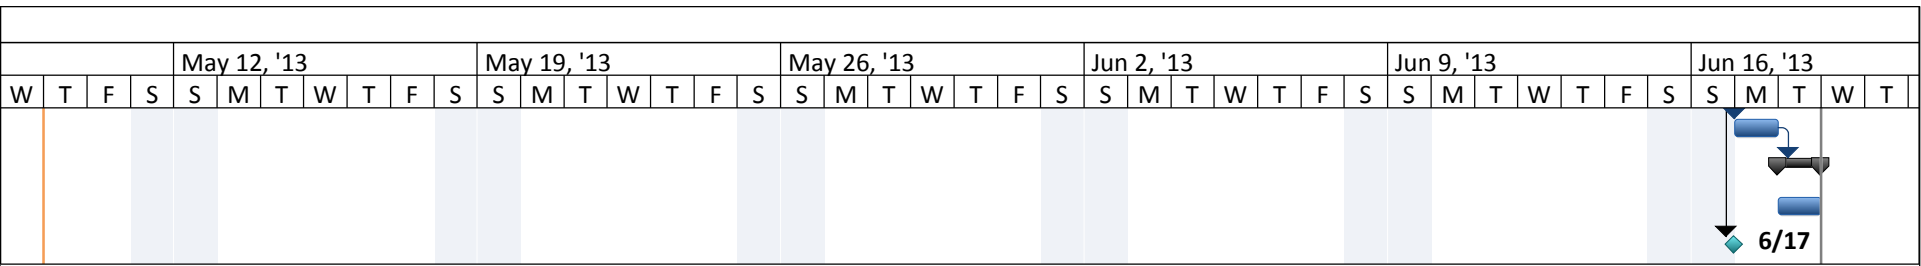

Project: Malware Protection Ove
Date: 5/9/13

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	
