

ID	% Complete	Task Name	Duration	Start	Finish	Predecessors	Resource Names	Nov 4, '12		
								S	S	M
1	14%	<b>Malware Protection Overhaul Project</b>	<b>23 days?</b>	<b>11/5/12</b>	<b>12/5/12</b>					
2	100%	<b>Planning</b>	<b>1 day</b>	<b>11/5/12</b>	<b>11/5/12</b>					
3	100%	Define scope	1 day	11/5/12	11/5/12		Sophie			
4	100%	Review scope with Mark	1 day	11/5/12	11/5/12		Sophie			
5	100%	Kickoff Meeting - include other teams	1 day	11/5/12	11/5/12		Sophie			
6	33%	<b>Communications</b>	<b>1 day?</b>	<b>11/14/12</b>	<b>11/14/12</b>					
7	100%	Initial IT Leader meeting presentation	1 day?	11/14/12	11/14/12		Andrew			
8	0%	Contact IT Leaders to solícite volunteers for pilot					Tim			
9	0%	Checklist for pilot					Andrew			
10	9%	<b>Windows Selection</b>	<b>1 day?</b>	<b>11/14/12</b>	<b>11/14/12</b>					
11	0%	<b>System Center 2012 (Forefront) Evaluation</b>	<b>1 day?</b>	<b>11/14/12</b>	<b>11/14/12</b>		<b>Andrew</b>			
12	0%	VM setup					Richard			
13	0%	Console setup					Richard			
14	0%	Console and client functionality evaluation								
15	0%	Document pros and cons								
16	0%	Go/No Go?								
17	60%	<b>ESET Evaluation (v5.0 - Jan 2013)</b>	<b>1 day?</b>	<b>11/14/12</b>	<b>11/14/12</b>		<b>Andrew</b>			
18	100%	VM setup	1 day	11/14/12	11/14/12					
19	100%	Console setup	1 day	11/14/12	11/14/12					
20	100%	Console and client functionality evaluation	1 day	11/14/12	11/14/12					
21	0%	Document pros and cons								
22	0%	Go/No Go?								
23	0%	<b>Vendor Demo</b>	<b>1 day?</b>	<b>11/14/12</b>	<b>11/14/12</b>					
24	0%	Determine invitees								

Project: Malware Protection Overhaul Date: 12/11/12	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	

ID	% Complete	Task Name	Duration	Start	Finish	Predecessors	Resource Names	Nov 4, '12		
								S	S	M
25	0%	Determine requirements								
26	0%	Demo								
27	0%	Team feedback								
28	0%	Go/No Go?								
29	<b>0%</b>	<b>Analyze Recommendation and Solution</b>	<b>1 day?</b>	<b>11/14/12</b>	<b>11/14/12</b>					
30	0%	Peer school comparion breakdown					Andrew			
31	0%	Determine any contract/licensing issues								
32	0%	Determine total cost of ownership								
33	0%	Determine benefits and concerns								
34	0%	Determine support process/structure								
35	<b>0%</b>	<b>Sponsor approval</b>	<b>1 day?</b>	<b>11/14/12</b>	<b>11/14/12</b>					
37	<b>50%</b>	<b>McAfee License</b>	<b>1 day?</b>	<b>11/14/12</b>	<b>11/14/12</b>					
38	100%	Understand current McAfee license constraints	1 day	11/14/12	11/14/12					
39	0%	Adjust McAfee license based on new requirements								
40	<b>0%</b>	<b>Documentation and communication</b>	<b>1 day?</b>	<b>11/14/12</b>	<b>11/14/12</b>					
44	<b>0%</b>	<b>Pilot rollout (STAKEHOLDERS)</b>	<b>1 day?</b>	<b>11/14/12</b>	<b>11/14/12</b>					
50	<b>0%</b>	<b>Procurement</b>	<b>1 day?</b>	<b>11/14/12</b>	<b>11/14/12</b>					
55	<b>0%</b>	<b>EARLY ADOPTERS</b>	<b>1 day?</b>	<b>11/14/12</b>	<b>11/14/12</b>					
60	0%	Final Checkpoint: Present all feedback including beta rollout feedback to Sponsor								
61	<b>0%</b>	<b>General Communications</b>	<b>1 day?</b>	<b>11/14/12</b>	<b>11/14/12</b>					
63	<b>0%</b>	<b>Prep Helpdesk for full rollout support</b>	<b>1 day?</b>	<b>11/14/12</b>	<b>11/14/12</b>					
65	<b>0%</b>	<b>Full rollout (COMMUNITY)</b>	<b>1 day?</b>	<b>11/14/12</b>	<b>11/14/12</b>					

Project: Malware Protection Over Date: 12/11/12	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	

ID	% Complete	Task Name	Duration	Start	Finish	Predecessors	Resource Names	Nov 4, '12		
								S	S	M
67	12%	<b>MAC Selection</b>	16 days?	11/14/12	12/5/12					
68	50%	<b>Evaluation</b>	6 days?	11/28/12	12/5/12					
69	40%	<b>Sophos Evaluation</b>	6 days?	11/28/12	12/5/12		Andrew			
70	100%	VM setup	1 day	11/28/12	11/28/12					
71	100%	Console setup	1 day	12/5/12	12/5/12					
72	0%	<b>Console and client functionality evaluation</b>								
73	0%	Document Pros and cons								
74	0%	Go/No Go?								
75	60%	<b>ESET Evaluation (v5.0 - Jan 2013)</b>	1 day?	12/5/12	12/5/12		Andrew			
76	100%	VM setup	1 day	12/5/12	12/5/12					
77	100%	Console setup	1 day	12/5/12	12/5/12					
78	100%	Console and client functionality evaluation	1 day	12/5/12	12/5/12					
79	0%	<b>Document pros and cons</b>								
80	0%	Go/No Go?								
81	0%	<b>Vendor Demo</b>	1 day?	11/14/12	11/14/12					
88	0%	<b>Analyze Recommendation and Solution</b>	1 day?	11/14/12	11/14/12					
93	0%	<b>Sponsor approval</b>	1 day?	11/14/12	11/14/12					
95	0%	<b>Documentation and communication</b>	1 day?	11/14/12	11/14/12					
99	0%	<b>Pilot rollout (STAKEHOLDERS)</b>	1 day?	11/14/12	11/14/12					
105	0%	<b>Procurement</b>	1 day?	11/14/12	11/14/12					
110	0%	<b>EARLY ADOPTERS</b>	1 day?	11/14/12	11/14/12					
115	0%	Final Checkpoint: Present all feedback including beta rollout feedback to Sponsor								
116	0%	<b>General Communications</b>	1 day?	11/14/12	11/14/12					
118	0%	<b>Prep Helpdesk for full rollout support</b>	1 day?	11/14/12	11/14/12					


Project: Malware Protection Over Date: 12/11/12

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	

ID	% Complete	Task Name	Duration	Start	Finish	Predecessors	Resource Names			
								Nov 4, '12		
								S	S	M
120	0%	<b>Full rollout (COMMUNITY)</b>	<b>1 day?</b>	<b>11/14/12</b>	<b>11/14/12</b>					
122	0%	<b>Project Wrapup</b>	<b>1 day?</b>	<b>11/14/12</b>	<b>11/14/12</b>					
123	0%	closeout project								


Project: Malware Protection Over  
Date: 12/11/12

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	

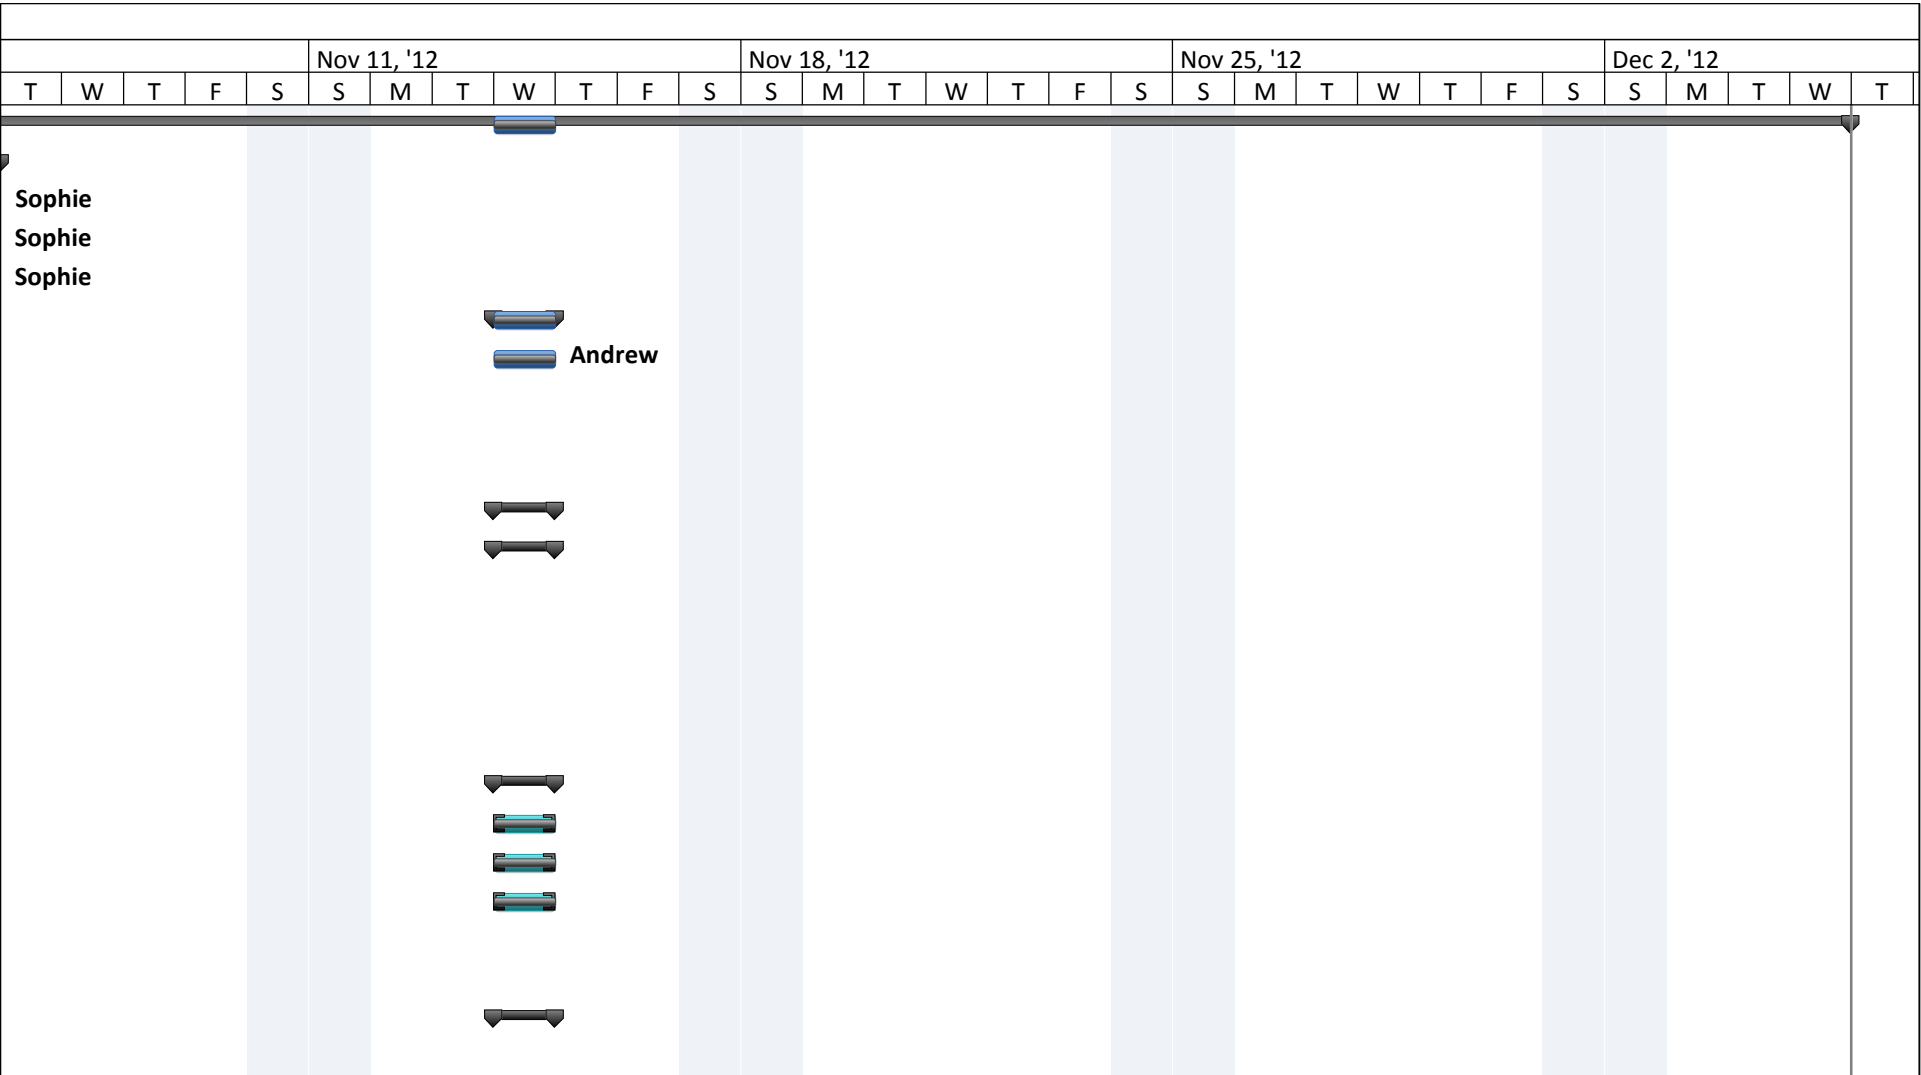


Project: Malware Protection Ove  
Date: 12/11/12

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	

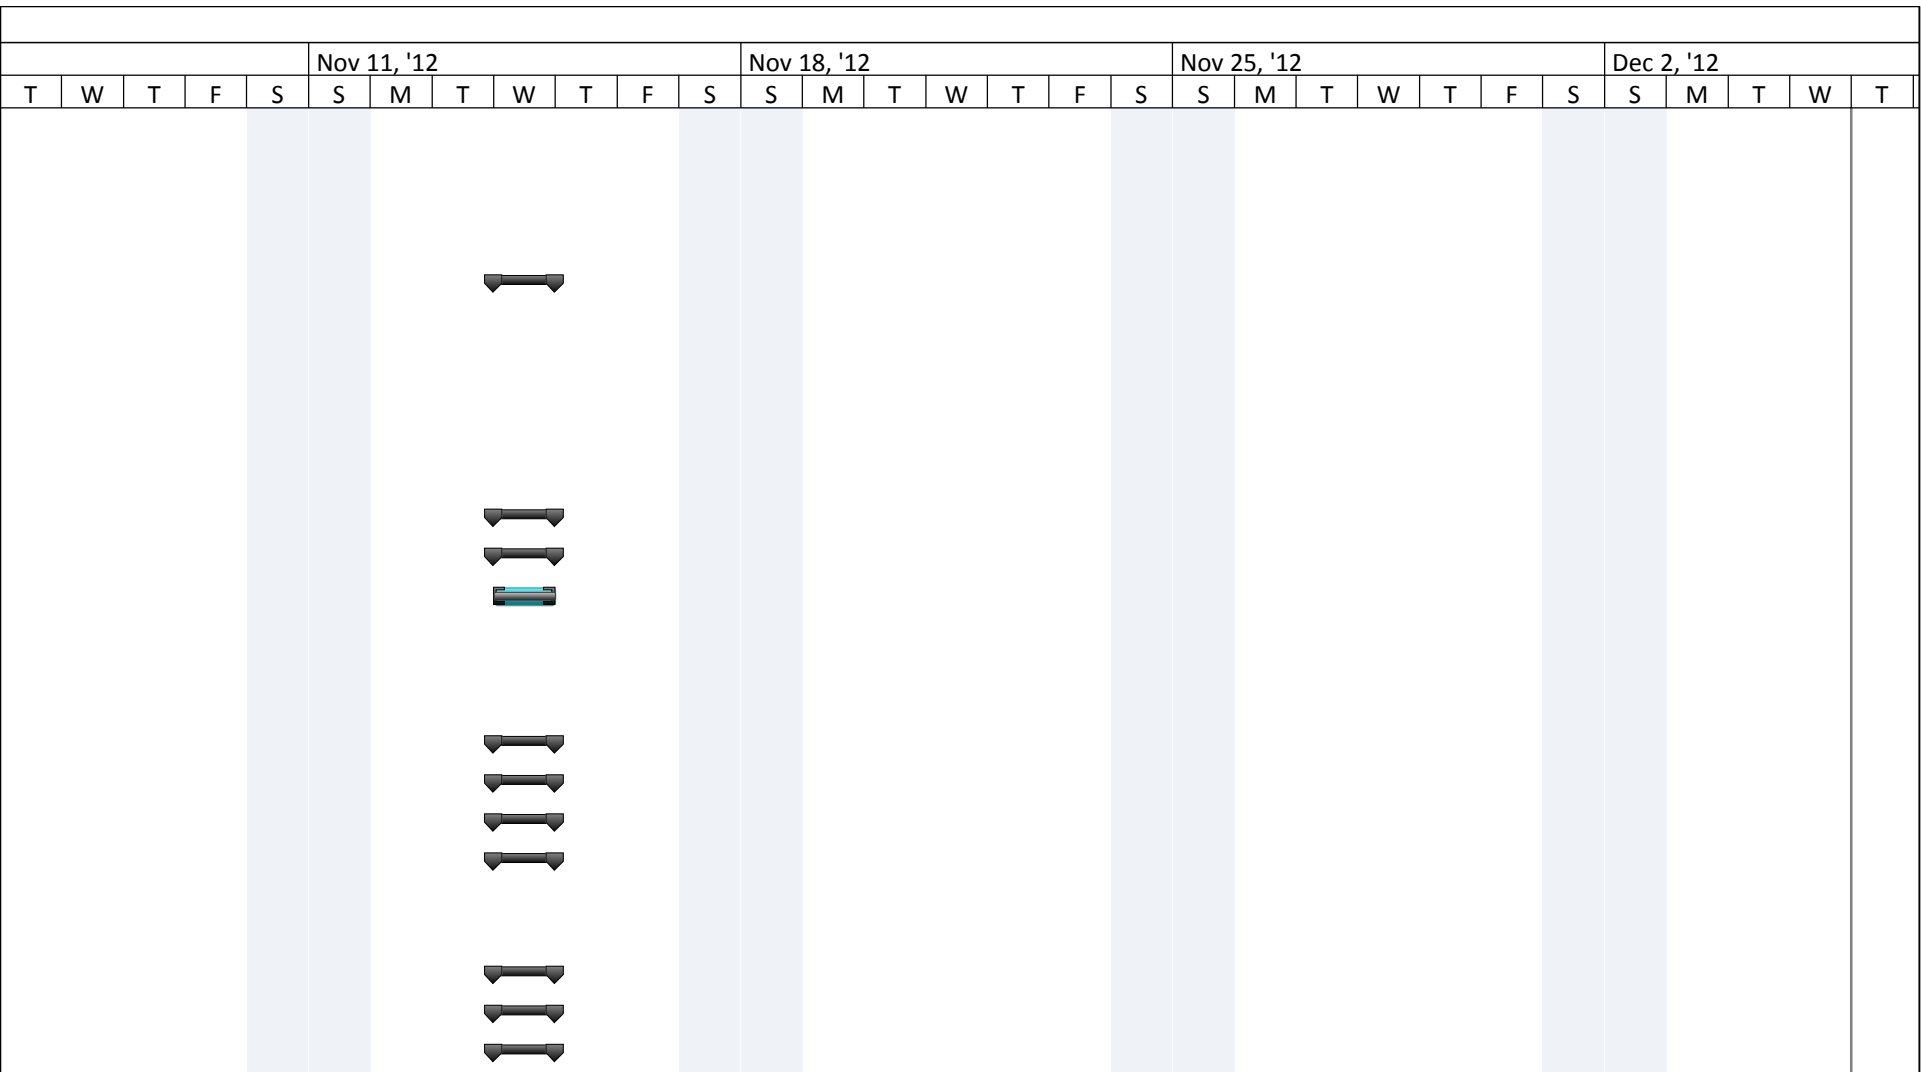

Project: Malware Protection Over Date: 12/11/12	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	

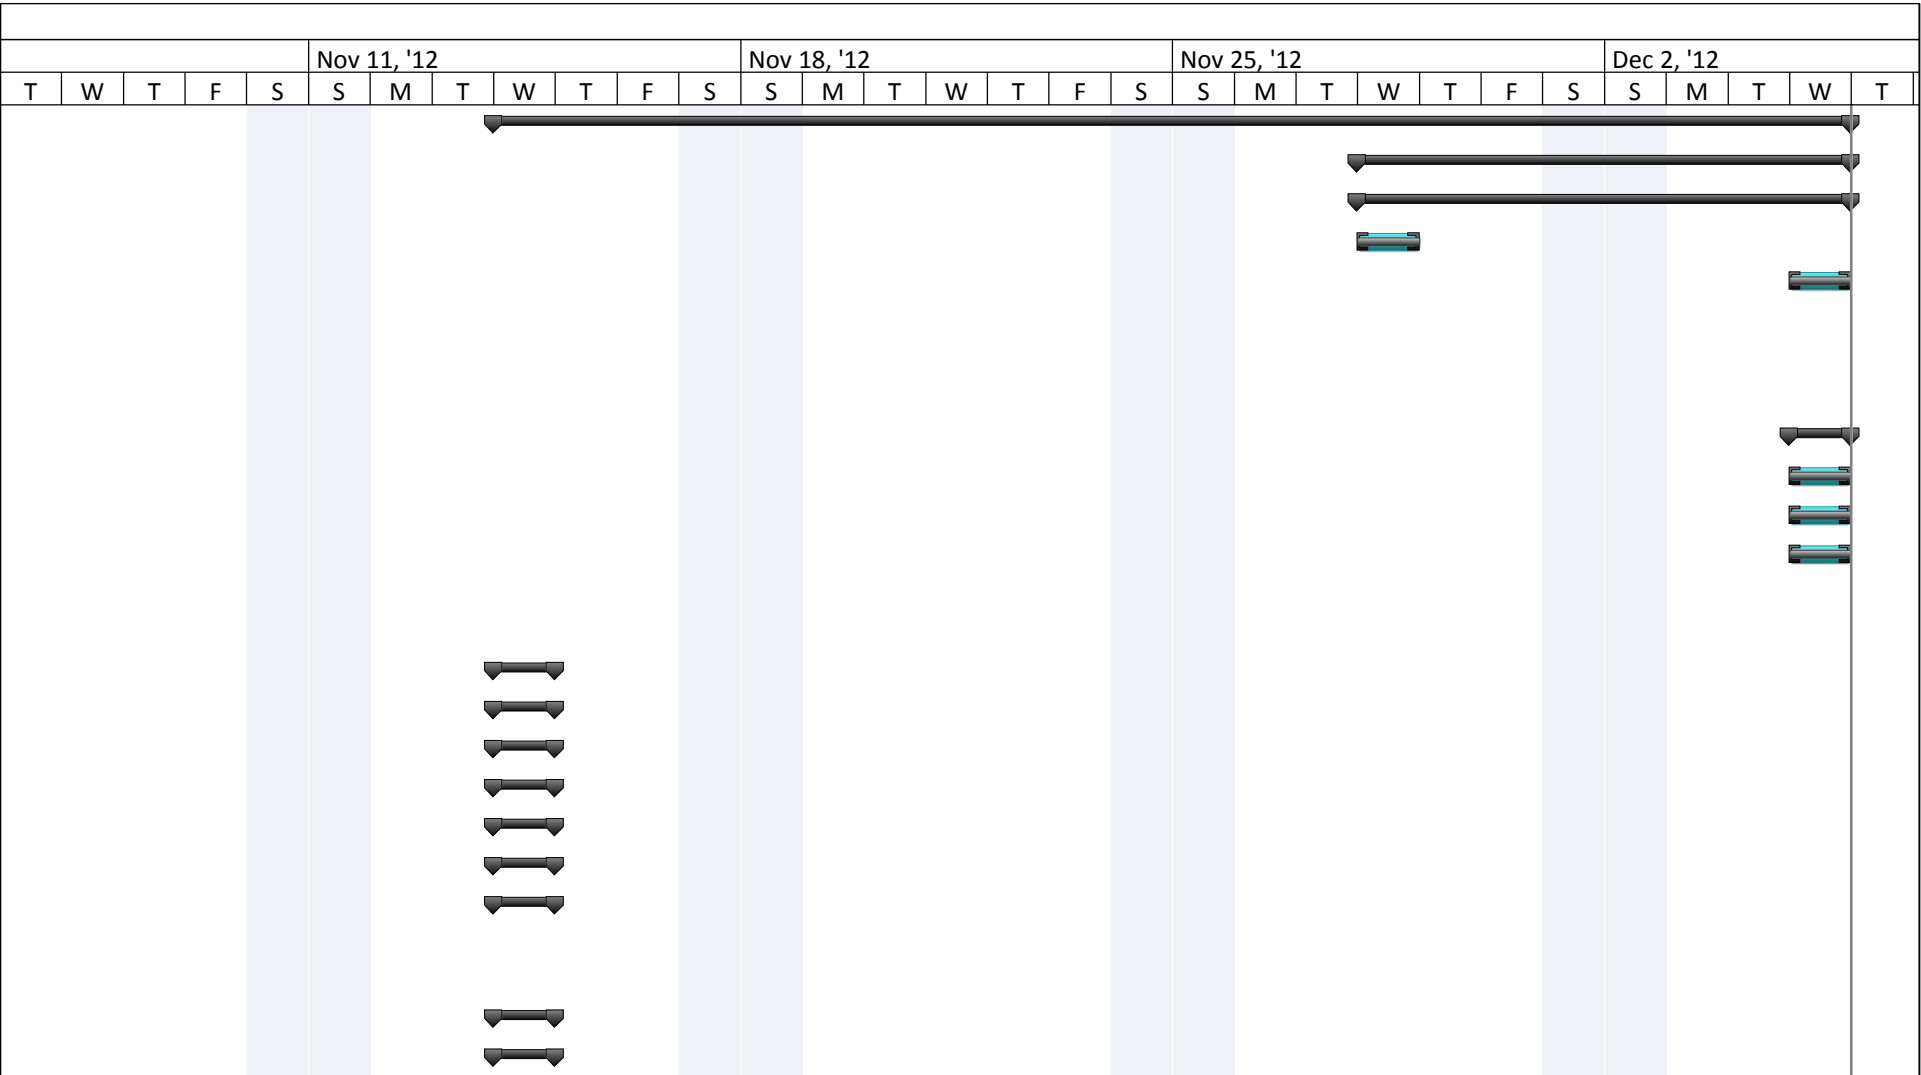

Project: Malware Protection Ove  
Date: 12/11/12

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	

					Nov 11, '12					Nov 18, '12					Nov 25, '12					Dec 2, '12											
T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	



Project: Malware Protection Ove  
Date: 12/11/12

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	
